

Job Name: 24-4208 - KYTC Christian Co. Call 100 (ID 241018)
Job Location: Hopkinsville, KY
Contractor: Scotty's Contracting & Stone, LLC

Plant: Beaver Dam

Tech: J. Horsley

7/30/2026 8:57:29 AM

PC: C. Goff



Structure ID: 259 (432+75 LT)

P2 BX024060-08LD08-1559

BX FLAT LID 8inW, w/15"x59" HOLE (KYTC DBI-13S)

- P4) 15" x 59" - P.I.P. - BY OTHERS - 8"
P3) 15" x 59" - FIELD ADJUSTMENT - 3"
P2) 24" x 60" - BX FLAT LID 8inW, w/15"x59" HOLE (KYTC DBI-13S) F/F - 8"
P1) 24" x 60" - BOX BASE 8inW, 8inF F/n - 36"
1) CASTING - HOE KY-230-S F/G (SAG)
1) 24" x 60" - Conseal CS-102 1.00"
1) Hole - 20
2) Hole - 6


0 lb
0 lb
1461 lb
6625 lb
474 lb
0 lb
0 lb
0 lb
Structure Total: 8560 lb

Structure Notes:
KYTC STATE PROJECT
1. KYTC DBI TYPE 13S / ASTM C-913 SPEC'S.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY ICAST (2x JBS 3413 F&G's)
4. STUB #5 BARS 4" OUT TOP OF TOP SLAB (SPA AT 12" C/C) AROUND 15"x59" HOLE.

REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. (DBL MAT).
- WALLS (As .31) #5 BARS AT 12" C.C.E.W..
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

NOTES:

1. MANUFACTURED TO KYTC DBI TYPE 13S/ASTM C-931 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: DOUBLE MAT #5 BAR @ 6" C.C. E.W. (GRADE 60).
4. STUB #5 BARS 4" OUT TOP SLAB AROUND OPENING @ 12" C/C.

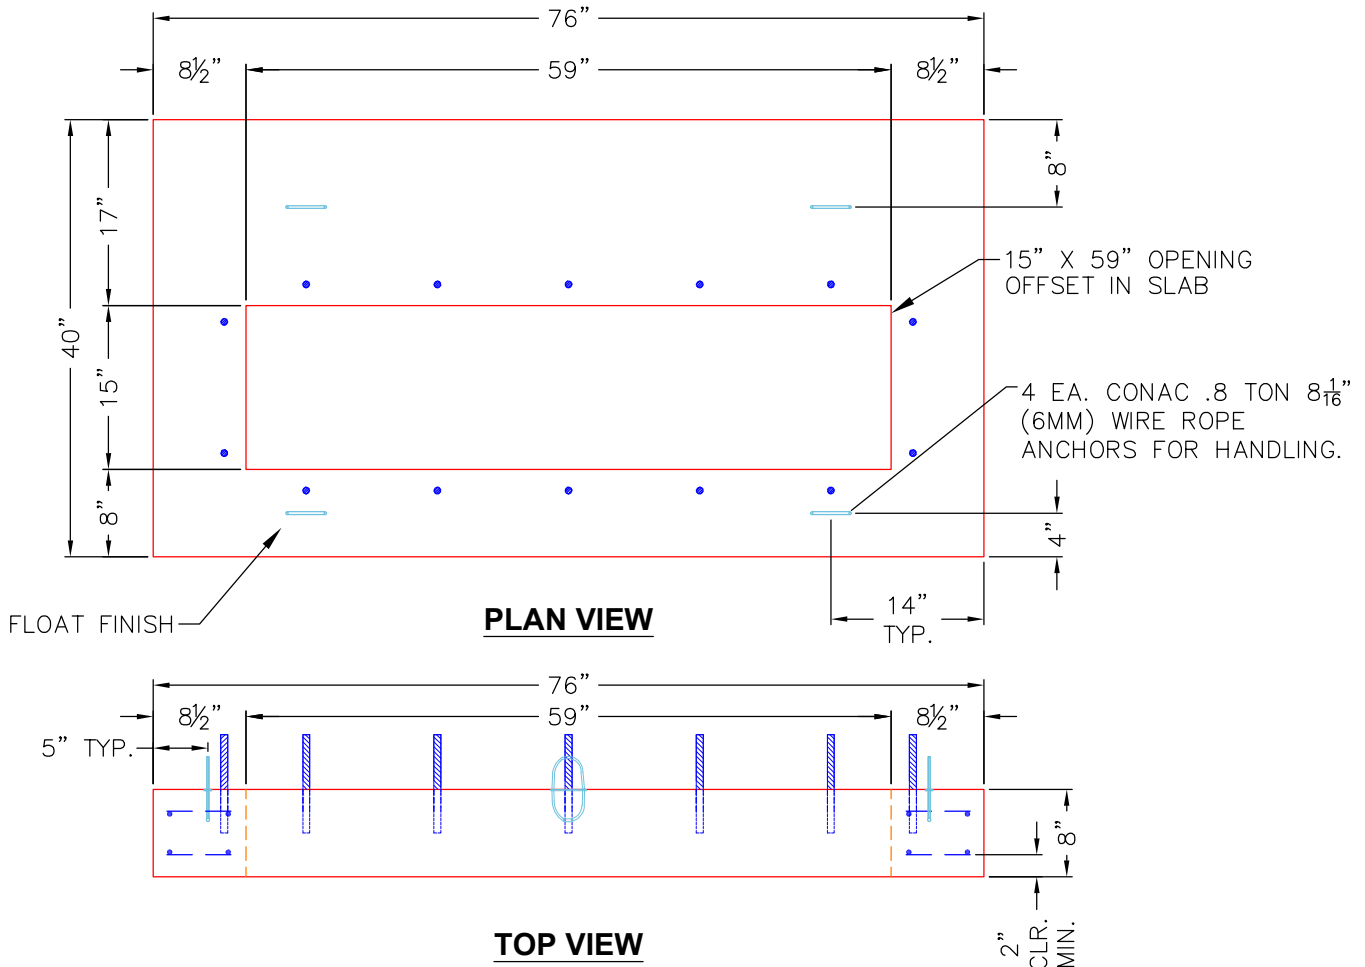

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 1461 lb
Volume (Net): 0.37cu.yd
