



Job Name: 24-4208 - KYTC Christian Co. Call 100 (ID 241018) Job Location: Hopkinsville, KY Contractor: Scotty's Contracting & Stone, LLC					Plant: Beaver Dam 6/26/2026 7:36:01 AM		Tech: J. Horsley PC: C. Goff				
Structure ID: 222											
P1 BX2436-08BVF			BOX BASE 8inW, 8inF, Variable Ht F/n								
P4) 24" x 120" - CB INLET KY A 10' TOP RIGHT F/G - 10" P3) 24" x 120" - CB INLET KY A 10' BOTTOM RIGHT T/G - 18" P2) 24" x 36" - FIELD ADJUSTMENT - 3" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 26" 1) CASTING - HOE KY-206 F/C (KY TY1) 1) This Structure Includes a Cast-in Item - KY-206 Frame (Supplied by iCast) 2) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 22 1) Hole - 6						3398 lb 5270 lb 0 lb 3669 lb 206 lb 0 lb 0 lb 0 lb 0 lb		Structure Notes: ** KYTC STATE PROJECT ** STATION: 420+26 LT 1. PER KYTC CBI TYPE A / ASTM C-913 SPECS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. HOE KY-206 FRAME & COVER "STORM" SUPPLIED BY ICAST - FRAME TO BE CAST INTO TOP PHASE TOP FLANGE SIDE UP			
Rim: 552.84' Rim to Invert: 4.83' Slack: 0.96" Sump: 0" Step Position:						Structure Total: 12543 lb					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	548.01'	225°	20.5"	15" RCP B WALL	19.5"	Hole 22	22"	31.113"	-2.25"	10.209"	
Invert 2	549.09'	0°	20"	4" HDPE (perf pipe)	4.8"	Hole 6	6"	6"	12.5"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

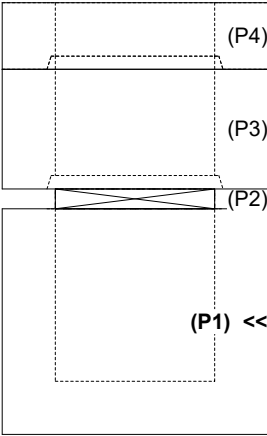

UPSIDE-DOWN VIEW (int. dimensions)

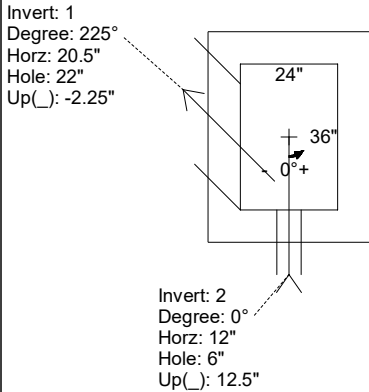

INSIDE WALL DIMENSIONS

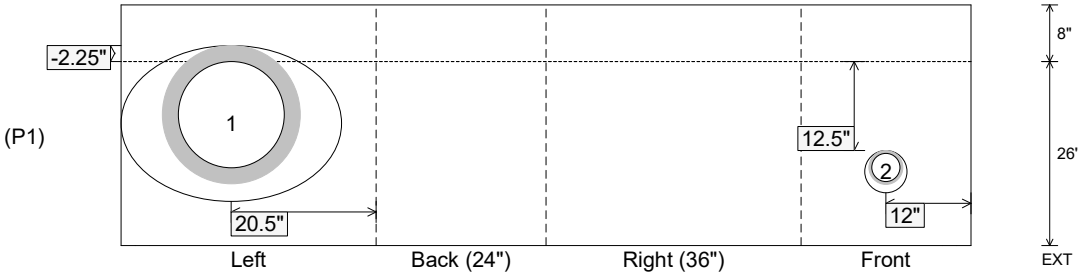

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 26" Height (Ext): 34"	Weight (Net): 3669 lb Volume (Net): 0.94cu.yd
----------------------------------	-------------------------------	--	--	--
