

Job Name: 23-1914 - KYTC Daviess County ID 231032
 Job Location: Owensboro, KY 42701
 Contractor: Mick-Murf Construction Inc.

Plant: 100
 1/8/2026 10:59:03 AM

Tech: J. Horsley
 PC: C. Goff



Structure ID: 089 (KY B 10ft)

P2 BX036048-08TS024024


CB FT REDUCER 24"X24" HOLE T/F

- P6) 8" x 120" - CB INLET KY B 10' TOP F/G - 9"
- P5) 24" x 120" - CB INLET KY B 10' BOTTOM RIGHT T/G - 17"
- P4) 24" x 24" - FIELD ADJUSTMENT - 3"
- P3) 24" x 24" - BOX RISER 8inW F/G - 24"
- P2) 36" x 48" - CB FT REDUCER 24"X24" HOLE T/F - 8"
- P1) 36" x 48" - BOX BASE 8inW, 8inF F/n - 60"
- 1) 36" x 48" - Conseal CS-102 1.00"
- 2) 24" x 24" - Conseal CS-102 1.00"
- 2) Hole - 40
- 1) Hole - 28
- 1) Hole - 6

- 1660 lb
- 2650 lb
- 0 lb
- 2043 lb
- 1847 lb
- 8189 lb
- 0 lb
- 0 lb
- 0 lb
- 0 lb
- 0 lb
-
- Structure Total: 16390 lb

Structure Notes:
 ** KYTC STATE PROJECT **
 1. PER KYTC CBI TYPE B / ASTM C913 SPEC'S.
 2. CONCRETE = 4,000 PI AT 28 DAYS.
 3. NO STEPS & NO INVERT CHANNEL.
 5. CBI KY B F/G - BY OTHERS.

REINFORCING PER ASTM A615 (GRADE 60).
 - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W.
 - TRANS SLAB (As .62) #5 BARS AT 6" C.C.E.W. (DBL MAT.)
 - WALLS/FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

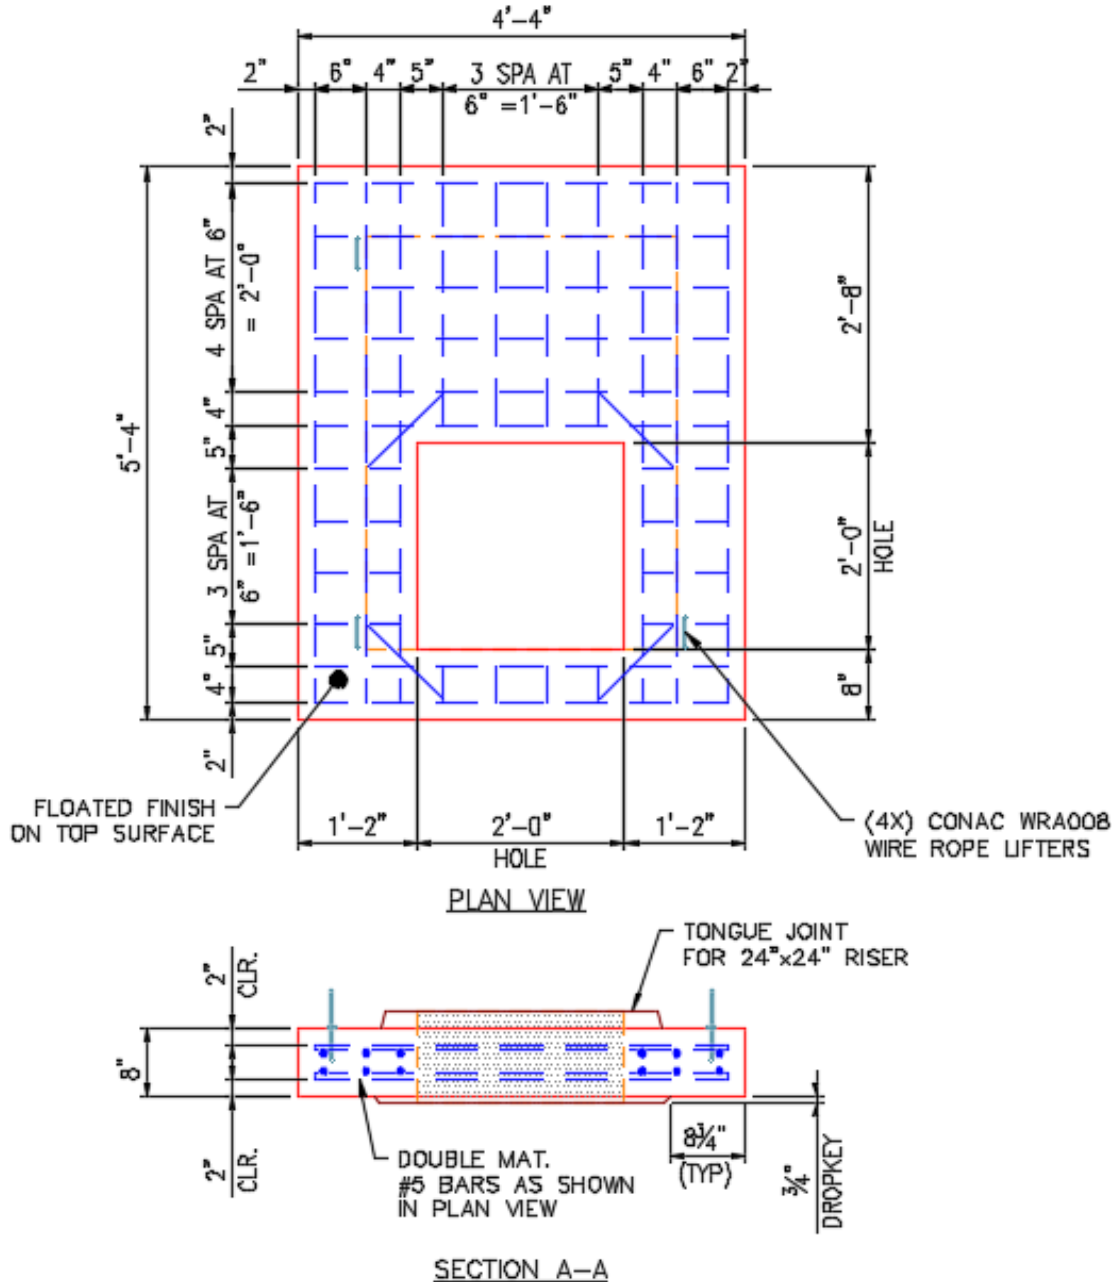

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Flat	Wall Thickness: 8"	Height (Ext): 8"	Weight (Net): 1847 lb Volume (Net): 0.47cu.yd
----------------------------------	----------------------------------	--------------------	------------------	--
