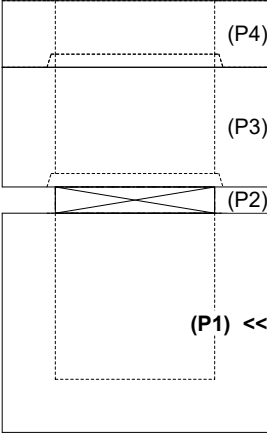
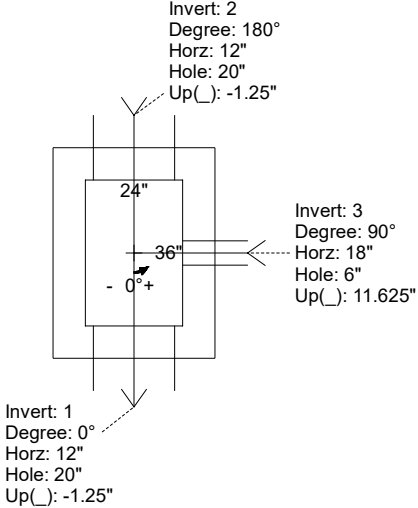
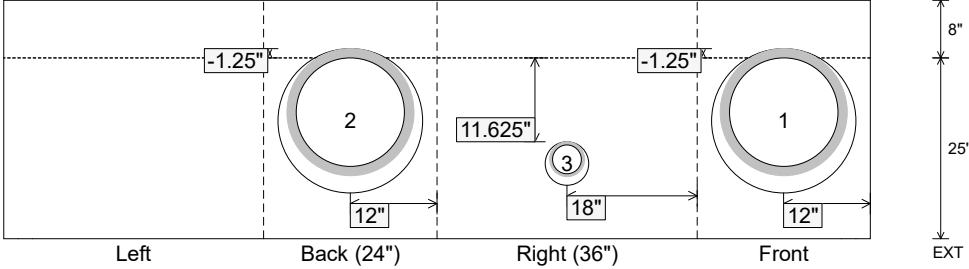


Job Name: 24-4208 - KYTC Christian Co. Call 100 (ID 241018) Job Location: Hopkinsville, KY Contractor: Scotty's Contracting & Stone, LLC					Plant: Beaver Dam 6/26/2026 7:35:33 AM		Tech: J. Horsley PC: C. Goff				
Structure ID: 102											
P1		BX2436-08BVF		BOX BASE 8inW, 8inF, Variable Ht F/n							
P4) 24" x 120" - CB INLET KY A 10' TOP RIGHT F/G - 10" P3) 24" x 120" - CB INLET KY A 10' BOTTOM RIGHT T/G - 18" P2) 24" x 36" - FIELD ADJUSTMENT - 4" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 25" 1) CASTING - HOE KY-206 F/C (KY TY1) 1) This Structure Includes a Cast-in Item - KY-206 Frame (Supplied by iCast) 2) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 20 1) Hole - 6						3398 lb 5270 lb 0 lb 3506 lb 206 lb 0 lb 0 lb 0 lb 0 lb		Structure Notes: ** KYTC STATE PROJECT ** STATION: 405+80 RT 1. PER KYTC CBI TYPE A / ASTM C-913 SPECS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. HOE KY-206 FRAME & COVER "STORM" SUPPLIED BY ICAST - FRAME TO BE CAST INTO TOP PHASE TOP FLANGE SIDE UP			
Rim: 561.87' Rim to Invert: 4.75' Slack: 0" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	557.12'	0°	20"	15" HDPE	17.6"	Hole 20	20"	20"	-1.25"	0"	
Invert 2	557.12'	180°	20"	15" HDPE	17.6"	Hole 20	20"	20"	-1.25"	0"	
Invert 3	558.12'	90°	26"	4" HDPE (perf pipe)	4.8"	Hole 6	6"	6"	11.625"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimensions)   INSIDE WALL DIMENSIONS 											
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 25" Height (Ext): 33"		Weight (Net): 3506 lb Volume (Net): 0.9cu.yd		
