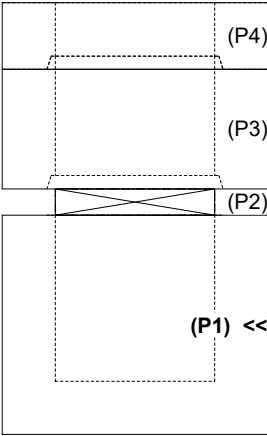
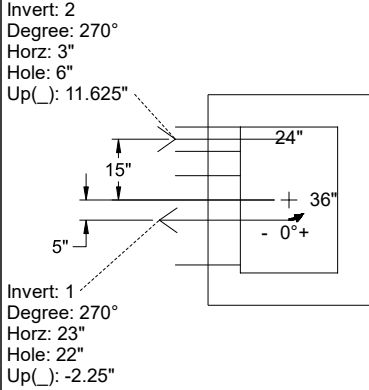
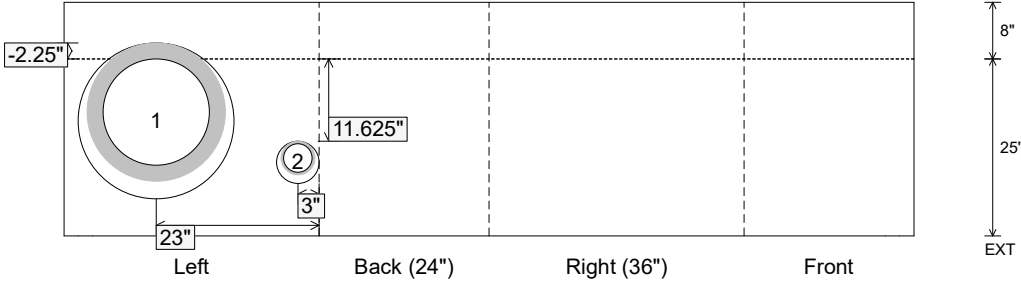


Job Name: 24-4208 - KYTC Christian Co. Call 100 (ID 241018) Job Location: Hopkinsville, KY Contractor: Scotty's Contracting & Stone, LLC					Plant: Beaver Dam 6/26/2026 7:35:29 AM		Tech: J. Horsley PC: C. Goff					
Structure ID: 106												
P1		BX2436-08BVF		BOX BASE 8inW, 8inF, Variable Ht F/n								
P4) 24" x 120" - CB INLET KY A 10' TOP LEFT F/G - 10" P3) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT T/G - 18" P2) 24" x 36" - FIELD ADJUSTMENT - 4" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 25" 1) CASTING - HOE KY-206 F/C (KY TY1) 1) This Structure Includes a Cast-in Item - KY-206 Frame (Supplied by iCast) 2) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 22 1) Hole - 6					3400 lb 5270 lb 0 lb 3725 lb 206 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 12601 lb		Structure Notes: ** KYTC STATE PROJECT ** STATION: 402+45 LT 1. PER KYTC CBI TYPE A / ASTM C-913 SPECS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. HOE KY-206 FRAME & COVER "STORM" SUPPLIED BY ICAST - FRAME TO BE CAST INTO TOP PHASE TOP FLANGE SIDE UP					
Rim: 545.66'					Rim to Invert: 4.75'		Slack: 0"		Sump: 0"		Step Position:	
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1	540.91'	270°	31"	15" RCP B WALL	19.5"	Hole 22	22"	22"	-2.25"	5"		
Invert 2	541.91'	270°	11"	4" HDPE (perf pipe)	4.8"	Hole 6	6"	6"	11.625"	-15"		
Invert 3												
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												
					RIGHT-SIDE UP VIEW (int. dimensions)					UPSIDE-DOWN VIEW (int. dimenions)		
												
					INSIDE WALL DIMENSIONS							
Coating (Int): Coating (Ext):					Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 25" Height (Ext): 33"		Weight (Net): 3725 lb Volume (Net): 0.95cu.yd	
