



Job Name: 24-4208 - KYTC Christian Co. Call 100 (ID 241018) Job Location: Hopkinsville, KY Contractor: Scotty's Contracting & Stone, LLC					Plant: Beaver Dam 6/26/2026 7:35:51 AM		Tech: J. Horsley PC: C. Goff				
Structure ID: 212											
P1		BX2436-08BVF		BOX BASE 8inW, 8inF, Variable Ht F/n							
P4) 24" x 120" - CB INLET KY A 10' TOP RIGHT F/G - 10" P3) 24" x 120" - CB INLET KY A 10' BOTTOM RIGHT T/G - 18" P2) 24" x 36" - FIELD ADJUSTMENT - 4" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 25" 1) CASTING - HOE KY-206 F/C (KY TY1) 1) This Structure Includes a Cast-in Item - KY-206 Frame (Supplied by iCast) 2) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 22 1) Hole - 6					3398 lb 5270 lb 0 lb 3678 lb 206 lb 0 lb 0 lb 0 lb 0 lb		Structure Notes: ** KYTC STATE PROJECT ** STATION: 416+00 LT 1. PER KYTC CBI TYPE A / ASTM C-913 SPECS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. HOE KY-206 FRAME & COVER "STORM" SUPPLIED BY ICAST - FRAME TO BE CAST INTO TOP PHASE TOP FLANGE SIDE UP				
Rim: 558.18' Rim to Invert: 4.75' Slack: 0" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	553.43'	270°	21"	15" RCP B WALL	19.5"	Hole 22	22"	22"	-2.25"	-5"	
Invert 2	554.43'	270°	41"	4" HDPE (perf pipe)	4.8"	Hole 6	6"	6"	11.625"	15"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

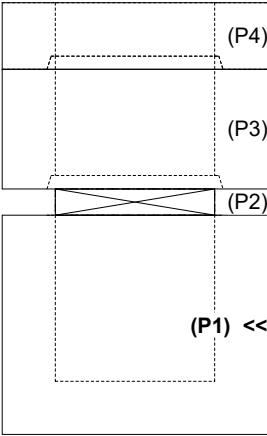

UPSIDE-DOWN VIEW (int. dimensions)

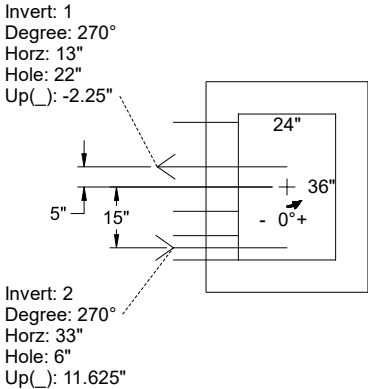

INSIDE WALL DIMENSIONS

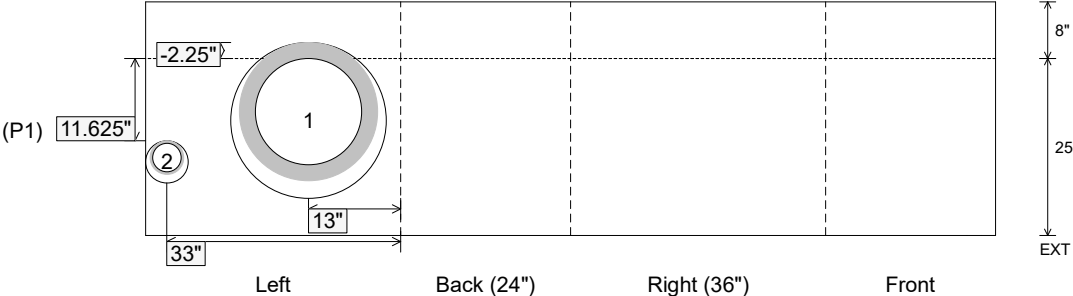

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 25" Height (Ext): 33"	Weight (Net): 3678 lb Volume (Net): 0.94cu.yd
----------------------------------	-------------------------------	--	--	--
