



Job Name: 24-4208 - KYTC Christian Co. Call 100 (ID 241018) Job Location: Hopkinsville, KY Contractor: Scotty's Contracting & Stone, LLC					Plant: Beaver Dam 7/30/2026 8:55:11 AM		Tech: J. Horsley PC: C. Goff				
Structure ID: 228 (423+15 LT)											
P1		BX2436-08BVF		BOX BASE 8inW, 8inF, Variable Ht F/n							
P4) 24" x 120" - CB INLET KY A 10' TOP RIGHT F/G - 10" P3) 24" x 120" - CB INLET KY A 10' BOTTOM RIGHT T/G - 18" P2) 24" x 36" - FIELD ADJUSTMENT - 4" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 25" 1) CASTING - HOE KY-206 F/C (KY TY1) 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 22 1) Hole - 6					3398 lb 5270 lb 0 lb 3673 lb 206 lb 0 lb 0 lb 0 lb ----- Structure Total: 12547 lb		Structure Notes: . ** KYTC STATE PROJECT ** 1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. HOE KY-206 F/C CAST INTO TOP SLAB. REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 551.38'		Rim to Invert: 4.75'		Slack: 0"		Sump: 0"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	546.63'	270°	26"	15" RCP B WALL	19.5"	Hole 22	22"	22"	-2.25"	0"	
Invert 2	547.92'	0°	20"	4" HDPE (perf pipe)	4.8"	Hole 6	6"	6"	15.08"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

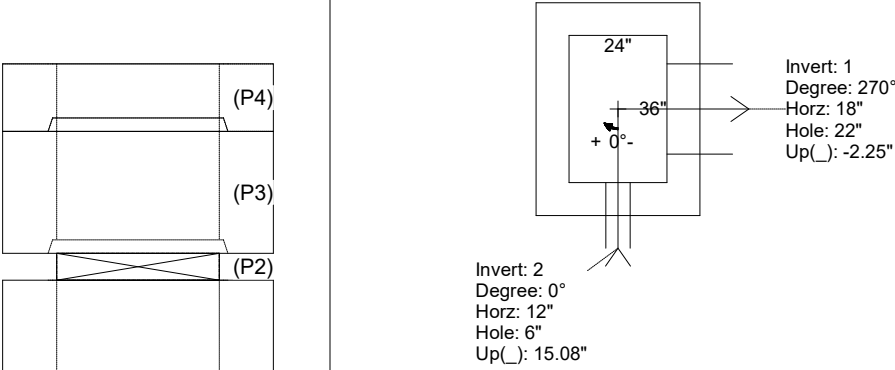

UPSIDE-DOWN VIEW (int. dimensions)

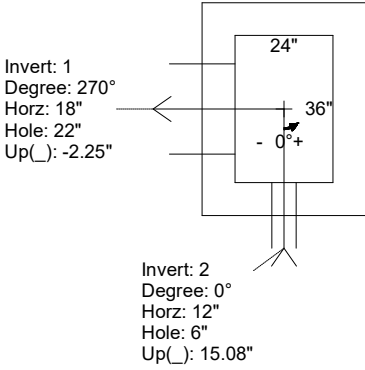

INSIDE WALL DIMENSIONS

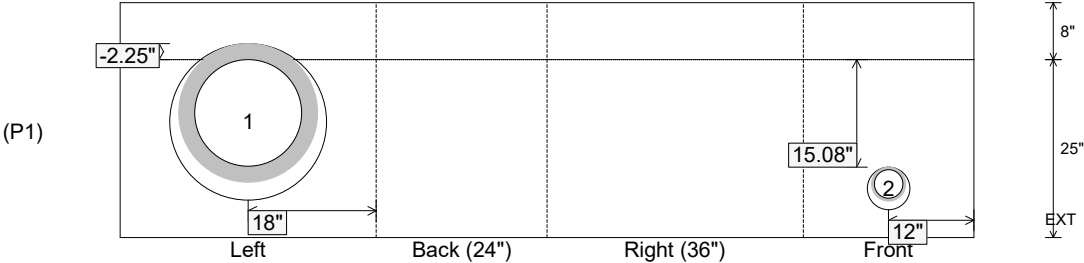

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 25" Height (Ext): 33"	Weight (Net): 3673 lb Volume (Net): 0.94cu.yd
----------------------------------	-------------------------------	--	--	--
