



Job Name: 24-4208 - KYTC Christian Co. Call 100 (ID 241018) Job Location: Hopkinsville, KY Contractor: Scotty's Contracting & Stone, LLC					Plant: Beaver Dam 7/30/2026 8:55:20 AM		Tech: J. Horsley PC: C. Goff				
Structure ID: 236 (426+15 LT)											
P1		BX24300808VF		BOX BASE 8inW, 8inF, Variable Ht F/n							
P3) 15" x 27" - P.I.P. - BY OTHERS - 8" P2) 24" x 30" - CB FLAT TOP 8"W w/15"x27" HOLE F/F - 8" P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht F/n - 26" 1) CASTING - HOE KY-230-G F/G (GRADE) 1) 24" x 30" - Conseal CS-102 1.00" 1) Hole - 20 2) Hole - 4					0 lb 963 lb 3443 lb 237 lb 0 lb 0 lb 0 lb ----- Structure Total: 4644 lb		Structure Notes: ** KYTC STATE PROJECT ** 1. KYTC DBI TYPE 13G / ASTM C-913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE KY-230-G F/G). 4. STUB #5 BARS UP 6" AROUND 15"x27" HOLE IN TOP SLAB (SPA. AT 12" C/C). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. (DBL MAT). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 543.57'		Rim to Invert: 3.81'		Slack: 3.72"		Sump: 0"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	539.76'	195°	20.986"	15" HDPE	17.6"	Hole 20	20"	20.706"	-1.3"	-5"	
Invert 2	541.26'	90°	23"	4" WEEP HOLE	4"	Hole 4	4"	4"	18"	0"	
Invert 3	541.26'	270°	23"	4" WEEP HOLE	4"	Hole 4	4"	4"	18"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

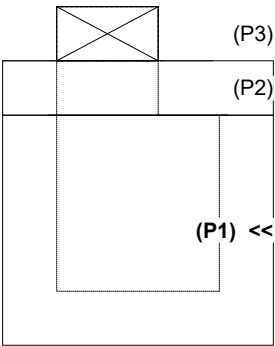

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

INSIDE WALL DIMENSIONS

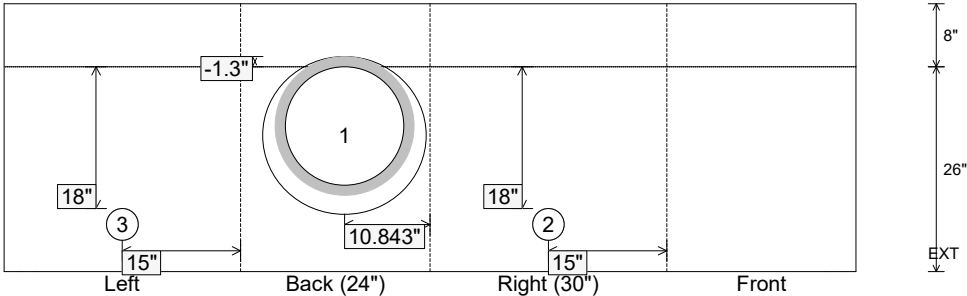

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 26" Height (Ext): 34"	Weight (Net): 3443 lb Volume (Net): 0.88cu.yd
----------------------------------	-------------------------------	--	--	--
