

Job Name: 24-4208 - KYTC Christian Co. Call 100 (ID 241018)
Job Location: Hopkinsville, KY
Contractor: Scotty's Contracting & Stone, LLC

Plant: Beaver Dam

Tech: J. Horsley

7/30/2026 8:57:20 AM

PC: C. Goff



Structure ID: 236 (426+15 LT)

P2 BX024030-08LD08-15X27

CB FLAT TOP 8"W w/15"x27" HOLE F/F

P3) 15" x 27" - P.I.P. - BY OTHERS - 8"
P2) 24" x 30" - CB FLAT TOP 8"W w/15"x27" HOLE F/F - 8"
P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht F/n - 26"
1) CASTING - HOE KY-230-G F/G (GRADE)
1) 24" x 30" - Conseal CS-102 1.00"
1) Hole - 20
2) Hole - 4


Structure Total: 4644 lb

Structure Notes:

**** KYTC STATE PROJECT ****

1. KYTC DBI TYPE 13G / ASTM C-913 SPEC'S.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY ICAST (HOE KY-230-G F/G).
4. STUB #5 BARS UP 6" AROUND 15"x27" HOLE IN TOP SLAB (SPA. AT 12" C/C).


REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. (DBL MAT).
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

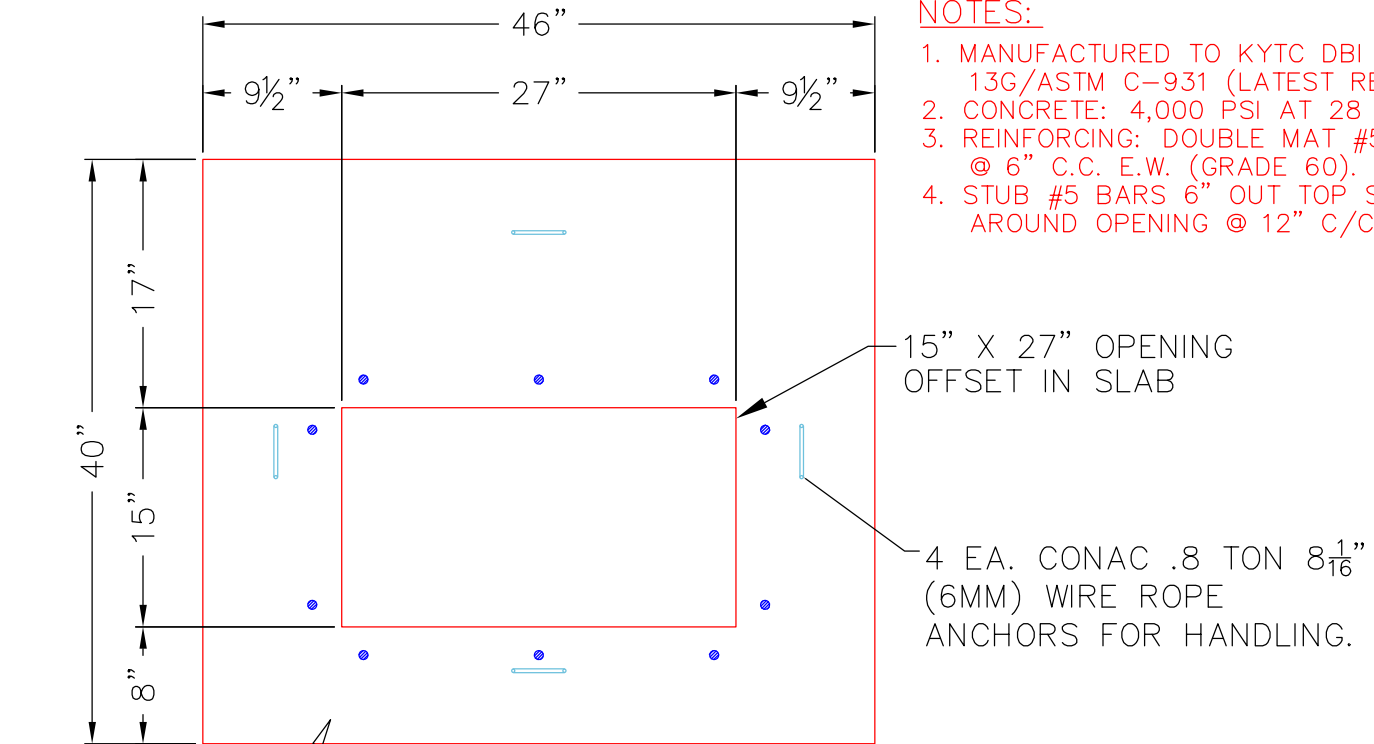

NOTES:

1. MANUFACTURED TO KYTC DBI TYPE 13G/ASTM C-931 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: DOUBLE MAT #5 BAR @ 6" C.C. E.W. (GRADE 60).
4. STUB #5 BARS 6" OUT TOP SLAB AROUND OPENING @ 12" C/C.

FLOAT FINISH **PLAN VIEW**

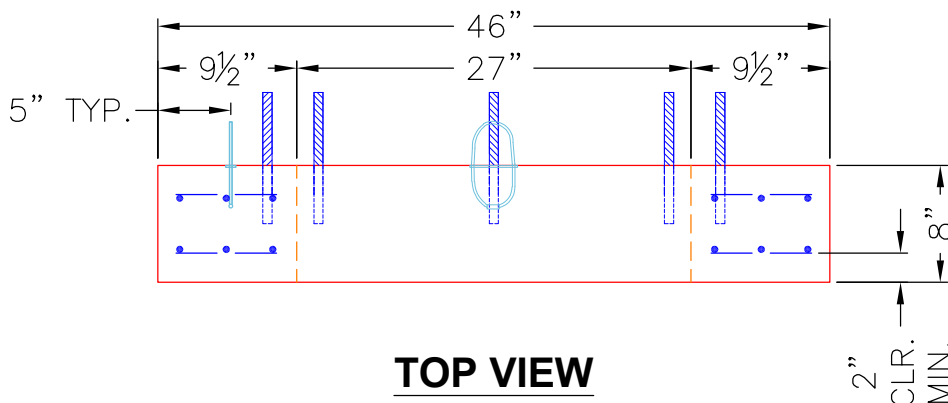

TOP VIEW

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 963 lb
Volume (Net): 0.25cu.yd
