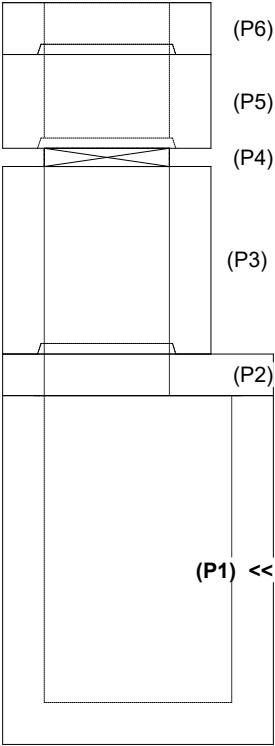

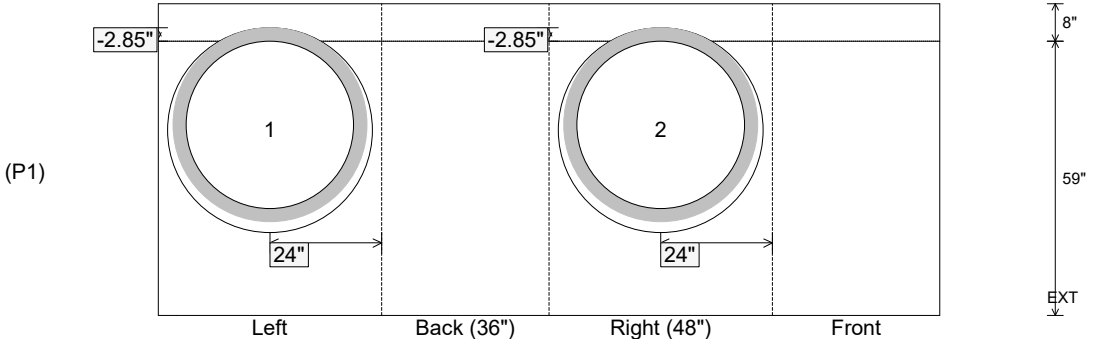


Job Name: 24-4208 - KYTC Christian Co. Call 100 (ID 241018) Job Location: Hopkinsville, KY Contractor: Scotty's Contracting & Stone, LLC					Plant: Beaver Dam 7/30/2026 8:55:52 AM		Tech: J. Horsley PC: C. Goff						
Structure ID: 276 (438+65 RT)													
P1		BX3648-08BAVF		BOX BASE 8inW, 8inF, Variable Ht F/n									
P6) 24" x 120" - CB INLET KY A 10' TOP LEFT F/G - 10" P5) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT T/G - 18" P4) 24" x 36" - FIELD ADJUSTMENT - 3.5" P3) 24" x 36" - BOX RISER 8inW F/G - 36" P2) 36" x 48" - CB FT REDUCER 24"X36" HOLE T/F - 8" P1) 36" x 48" - BOX BASE 8inW, 8inF, Variable Ht F/n - 59" 1) CASTING - HOE KY-206 F/C (KY TY1) 1) 36" x 48" - Conseal CS-102 1.00" 2) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 44 1) Hole - 6						3400 lb 5270 lb 0 lb 3654 lb 1654 lb 8114 lb 206 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 22298 lb		Structure Notes: . ** KYTC STATE PROJECT ** 1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. HOE KY-206 F/C CAST INTO TOP SLAB. REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - TRANS. SLAB (As .62) #5 BARS AT 6" C.C.E.W (DBL MAT) - WALLS (As .31) #5 BARS AT 6" C.C.E.W. - FLOOR (As .31) #5 BARS AT 6" C.C.E.W.					
Rim: 542.75'		Rim to Invert: 11.23'		Slack: 0.26"		Sump: 0"		Step Position:					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset			
Invert 1	531.52'	270°	32"	36" HDPE	41.7"	Hole 44	44"	44"	-2.85"	0"			
Invert 2	531.52'	90°	32"	36" HDPE	41.7"	Hole 44	44"	44"	-2.85"	0"			
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimensions)  INSIDE WALL DIMENSIONS 													
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 59" Height (Ext): 67"		Weight (Net): 8114 lb Volume (Net): 2.07cu.yd				
