



Job Name: 24-4208 - KYTC Christian Co. Call 100 (ID 241018) Job Location: Hopkinsville, KY Contractor: Scotty's Contracting & Stone, LLC				Plant: Beaver Dam 7/30/2026 8:55:53 AM		Tech: J. Horsley PC: C. Goff				
Structure ID: 277 (439+85 RT)										
P1 BX24300808VF				BOX BASE 8inW, 8inF, Variable Ht F/n						
P2) 24" x 30" - CASTING HEIGHT - 3.75" P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht F/n - 35" 1) CASTING - HOE KY-460-11 F/G (DBI 11) 1) 24" x 30" - Conseal CS-102 1.00" 1) Hole - 20						0 lb 4314 lb 421 lb 0 lb 0 lb ----- 0 lb Structure Total: 4735 lb		Structure Notes: . **KYTC STATE PROJECT** 1. KYTC DBI TYPE 11 / ASTM C-913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE KY-460-11 F/G). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W.. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.		
Rim: 537.75' Rim to Invert: 3.25' Slack: 0.25' Sump: 0' Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	534.5'	90°	23"	15" HDPE	17.6"	Hole 20	20"	20"	-1.3"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

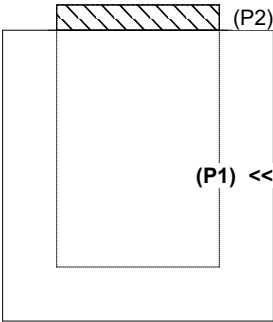

(P1) <<


(P2)

RIGHT-SIDE UP VIEW (int. dimensions)

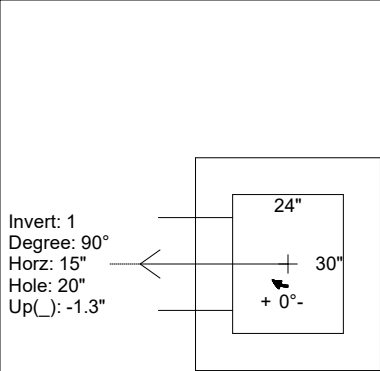


Invert: 1
Degree: 90°
Horz: 15"
Hole: 20"
Up(_): -1.3"

UPSIDE-DOWN VIEW (int. dimenions)



Invert: 1
Degree: 90°
Horz: 15"
Hole: 20"
Up(_): -1.3"

INSIDE WALL DIMENSIONS

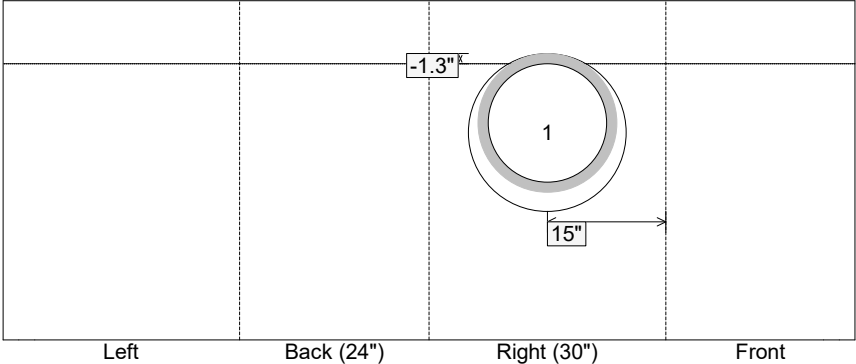

(P1)

Left Back (24") Right (30") Front

EXT

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 35" Height (Ext): 43"	Weight (Net): 4314 lb Volume (Net): 1.1cu.yd
----------------------------------	-------------------------------	--	--	---
