



THIS DRAWING IS INTENDED TO BE PRINTED IN COLOR.

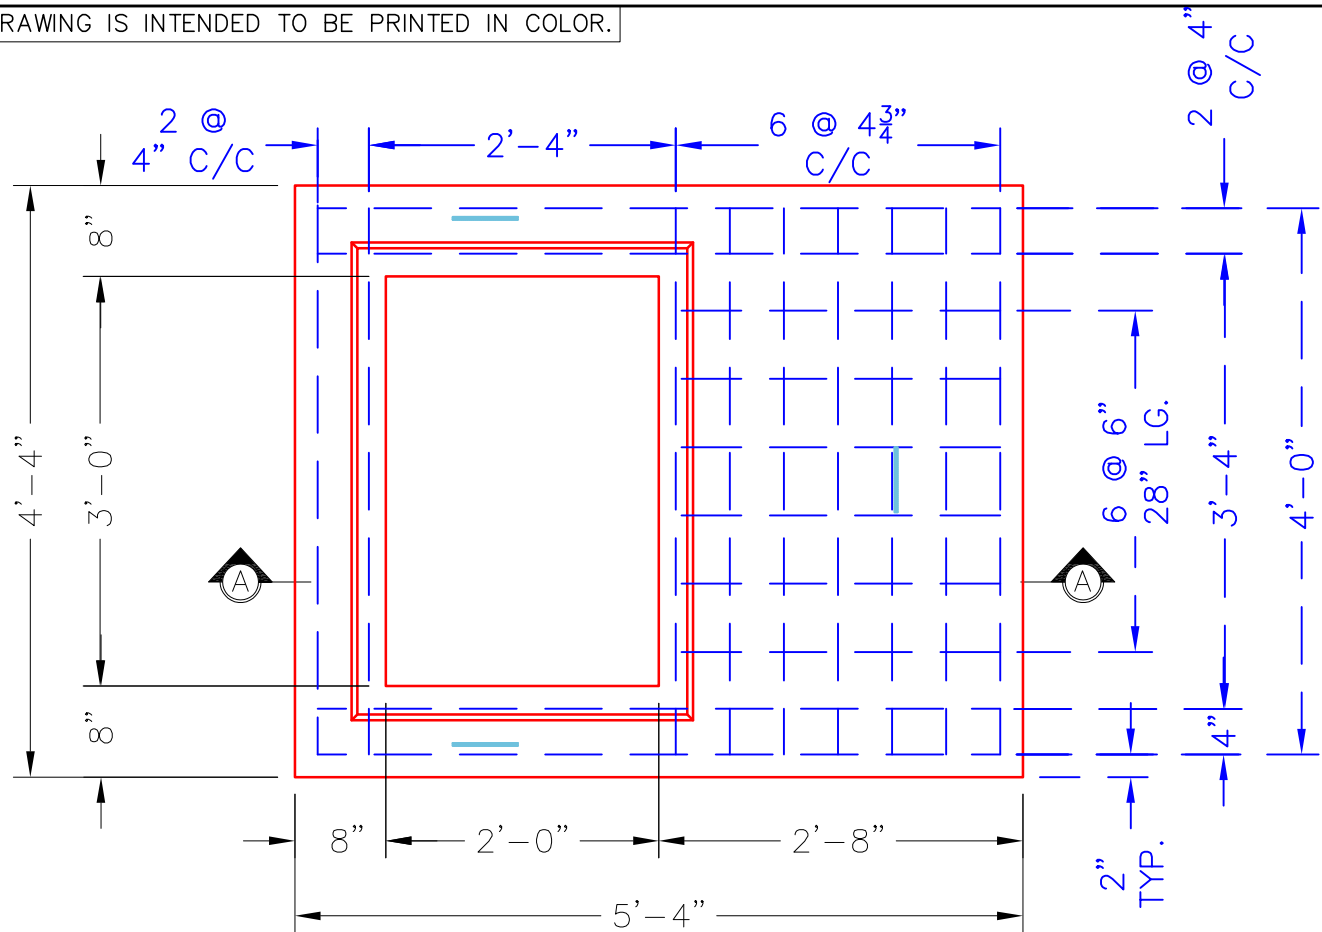

PLAN VIEW

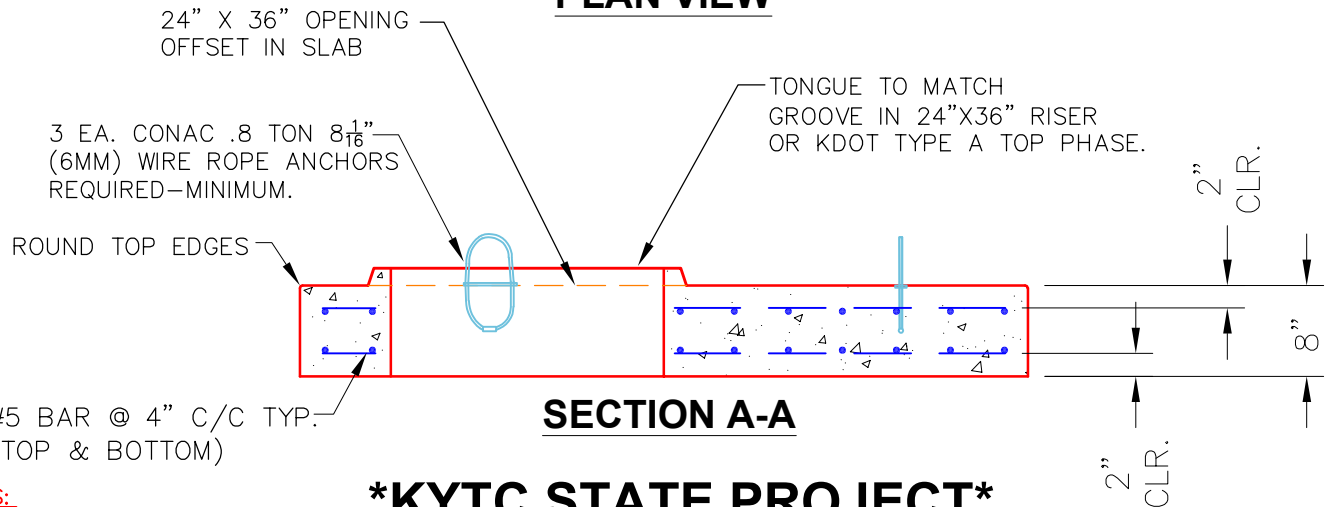

SECTION A-A

NOTES:

- CONCRETE: 4500 PSI @ 28 DAYS.
- MANUFACTURED TO KYTC & ASTM C-913 SPECIFICATIONS.
- REINFORCING: #5 BAR AS SHOWN-GRADE 60.
(TOP & BOTTOM LAYER)
- 3 EA. CONAC WIRE LOOP LIFTS REQUIRED (MIN.)

KYTC STATE PROJECT

#5 BAR CUT LIST
8 EA. @ 60" LG.
18 EA. @ 48" LG.
12 EA. @ 28" LG.

PRODUCTION WORK ORDER		PRODUCT I.D.: BX036048-08TS024036	DESCRIPTION: CURB INLET TRANSITION SLAB 48" X 36" X 8"	
	QUALITY CONTROL CHECKLIST		PRODUCT VIEW: RIGHT SIDE UP	CUSTOMER: SCOTTY'S CONTRACTING & STONE LLC
	☐ ALL DIMENSIONS CORRECT.		PLANT: BEAVER DAM, KY.	PROJECT: KYTC CHRISTIAN CO. CALL 100 (ID 241018)
	☐ LIFTERS INSTALLED.		WEIGHT: 1,654 LBS.	STRUCTURE: 281 (441+18 RT) (SEC. P2)
	☐ OPENING OFFSET.		TOP SECTION JOINT: TONGUE	QUOTE/SALES ORDER NO: 24-4208
	☐ REINFORCING CORRECT.		BOTTOM JOINT: FLAT	PC: C. GOFF
	☐ SHIP-LAP TONGUE INSTALLED.		QC CHECK INITIALS:	DRAWING: S. FELLETER
☐ EDGES CHAMFERED.			DATE: 07/30/26	SCALE: NTS
☐ ANY PATCHWORK ACCEPTABLE.				PG. 1 of 1
