



THIS DRAWING IS INTENDED TO BE PRINTED IN COLOR.

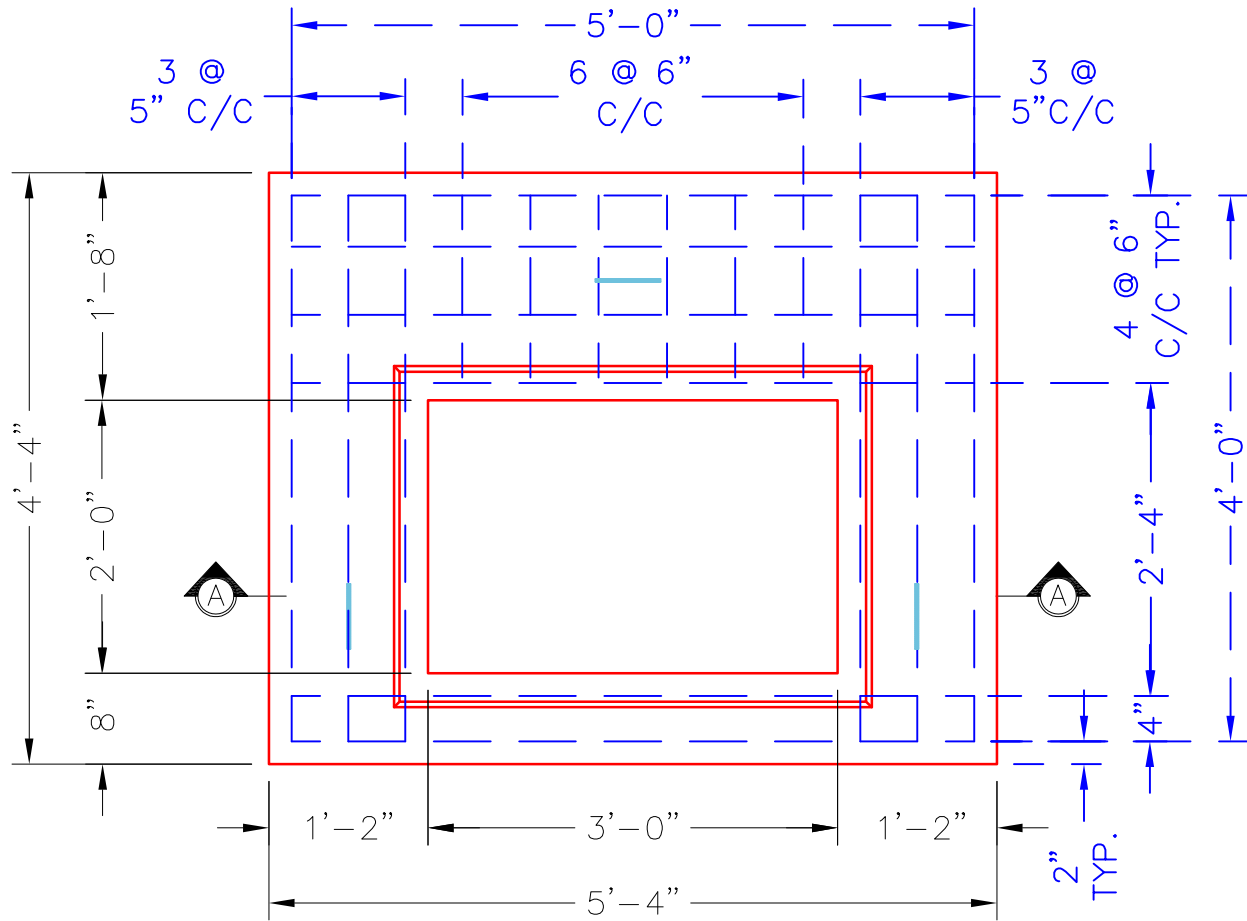

PLAN VIEW

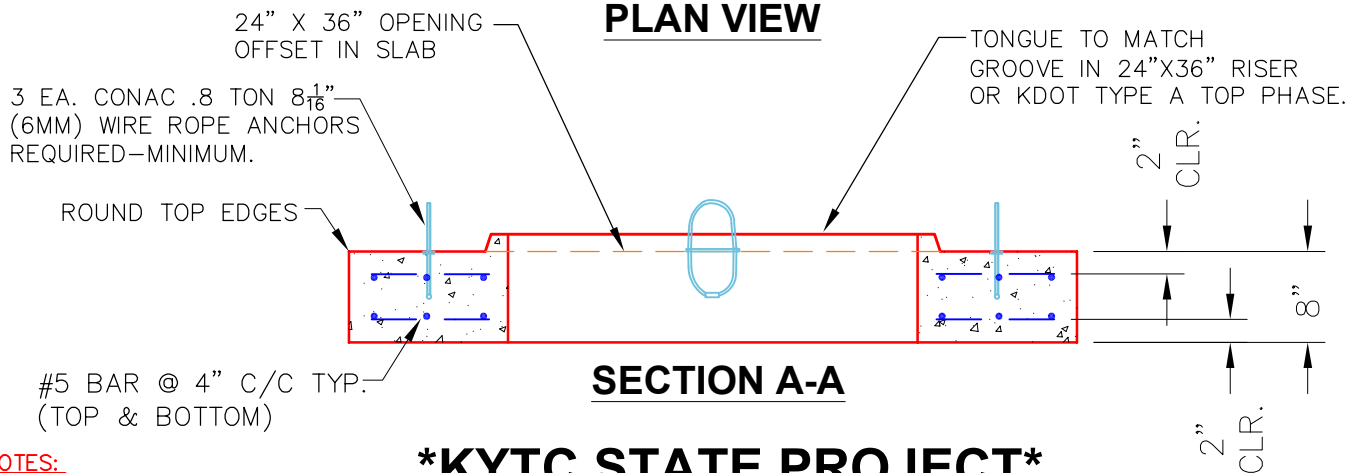

NOTES:

- CONCRETE: 4500 PSI @ 28 DAYS.
- MANUFACTURED TO KYTC & ASTM C-913 SPECIFICATIONS.
- REINFORCING: #5 BAR AS SHOWN-GRADE 60.
(TOP & BOTTOM LAYER)
- 3 EA. CONAC WIRE LOOP LIFTS REQUIRED (MIN.)

KYTC STATE PROJECT

#5 BAR CUT LIST

- 12 EA. @ 60" LG.
- 12 EA. @ 48" LG.
- 12 EA. @ 16" LG.

PRODUCTION WORK ORDER		PRODUCT I.D.: BX036048-08TS024036	DESCRIPTION: CURB INLET TRANSITION SLAB 36" X 48" X 8"		
	QUALITY CONTROL CHECKLIST	PRODUCT VIEW: RIGHT SIDE UP	CUSTOMER: SCOTTY'S CONTRACTING & STONE LLC		
	☐ ALL DIMENSIONS CORRECT. ☐ LIFTERS INSTALLED. ☐ OPENING OFFSET. ☐ REINFORCING CORRECT. ☐ SHIP-LAP TONGUE INSTALLED. ☐ EDGES CHAMFERED. ☐ ANY PATCHWORK ACCEPTABLE.	PLANT: BEAVER DAM, KY.	PROJECT: KYTC CHRISTIAN CO. CALL 100 (ID 241018)		
		WEIGHT: 1,654 LBS.	STRUCTURE: 302 (541+00 LT) (SEC. P2)		
		TOP SECTION JOINT: TONGUE	QUOTE/ORDER NO: 24-4208		
		BOTTOM JOINT: FLAT	PC: C. GOFF		DRAWING: S. FELLETER
		QC CHECK INITIALS:	DATE: 08/05/26	SCALE: NTS	PG. 1 of 1
