

Job Name: 24-4208 - KYTC Christian Co. Call 100 (ID 241018)
Job Location: Hopkinsville, KY
Contractor: Scotty's Contracting & Stone, LLC

Plant: Beaver Dam
8/3/2026 4:27:26 PM

Tech: J. Horsley
PC: C. Goff



Structure ID: MH 286 (422+65 RT)

P2 BX048048-08LD0824E

CB FLAT TOP 8"W w/24"Hole F/F

- P3) 24" - CASTING HEIGHT - 8"
P2) 48" x 48" - CB FLAT TOP 8"W w/24"Hole F/F - 8"
P1) 48" x 48" - BX BASE w/FLANGE 08W/12F/08EF F/n - 67"
1) CASTING - HOE KY-460-11 F/G (DBI 11)
1) 48" x 48" - Conseal CS-102 1.00"
2) Hole - 44
1) Hole - 20
6) MH Step ML-10-TDS-NCR - 10"


0 lb
2446 lb
14220 lb
421 lb
0 lb
0 lb
0 lb
0 lb
0 lb
Structure Total: 17087 lb

Structure Notes:
** KYTC STATE PROJECT**
1. PER KYTC MANHOLE TYPE C / ASTM C913 SPEC'S.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY ICAST (HOE KY-510 F/C)
4. SECONDARY POUR REQ'D FOR EXTENDED FLANGE (8"WD x 12" THICK).


REINFORCING PER ASTM A615 (GRADE 60).
- TRANS. SLAB #5's AT 6" C.C.E.W (DBL MAT).
- WALLS #5's AT 6" C.C.E.W.
- FLOOR #5's AT 12" C.C.E.W.

NOTES:

1. MANUFACTURED TO ASTM C-913 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: DBL MAT #5 BAR @ 6" C.C.E.W. (GRADE 60)

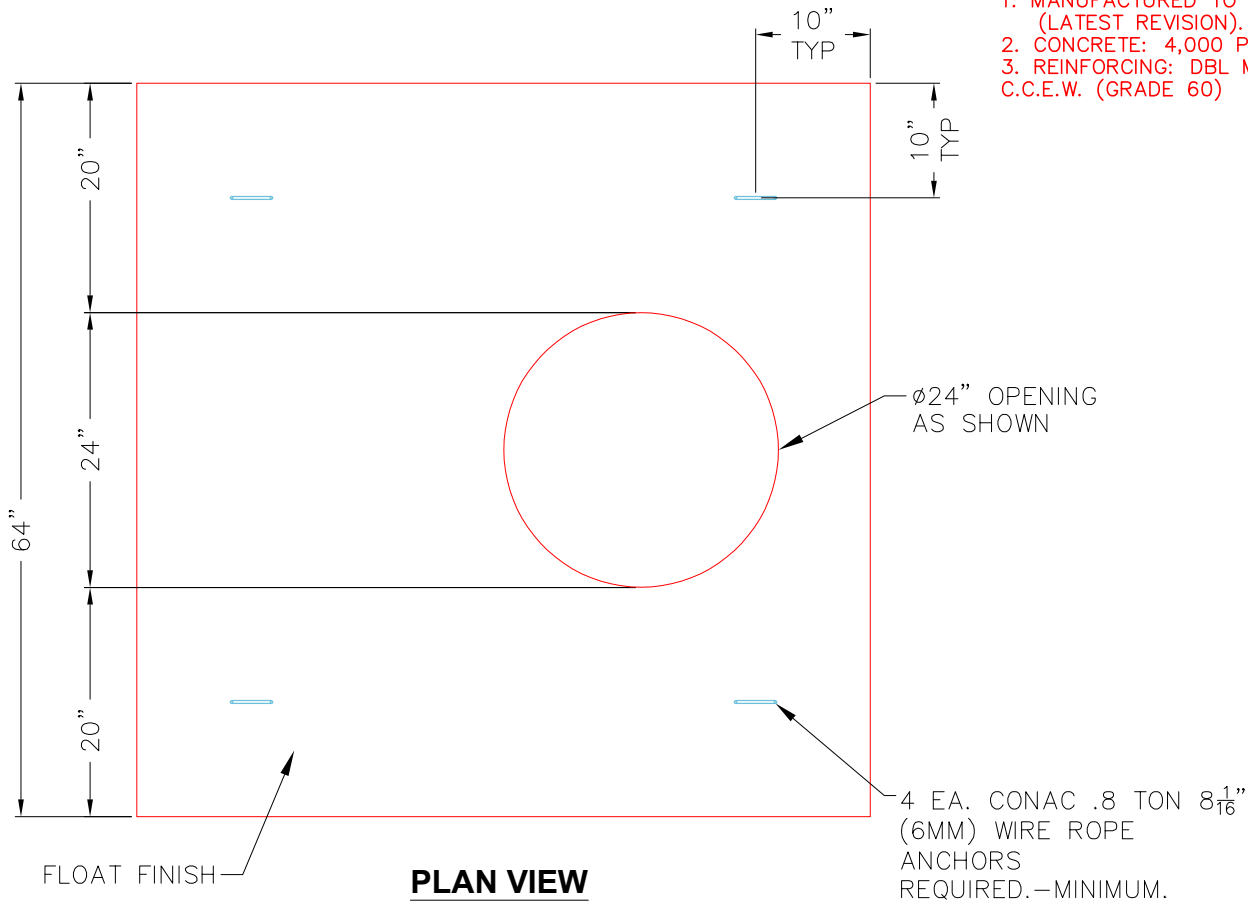

PLAN VIEW

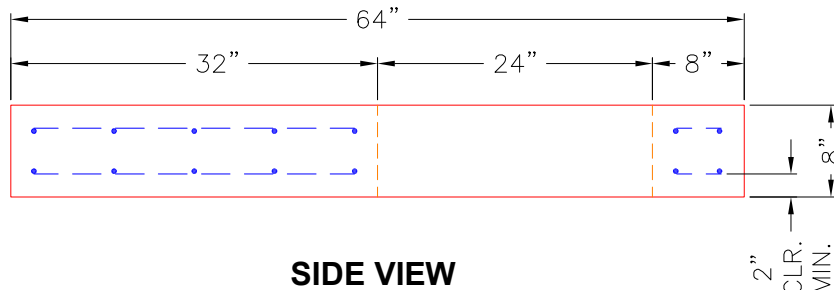

SIDE VIEW

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 2446 lb
Volume (Net): 0.62cu.yd
