

Job Name: 24-4208 - KYTC Christian Co. Call 100 (ID 241018)
Job Location: Hopkinsville, KY
Contractor: Scotty's Contracting & Stone, LLC

Plant: Beaver Dam

Tech: J. Horsley

8/3/2026 4:27:31 PM

PC: C. Goff



Structure ID: MH287 (445+05 RT)

P2 BX060060-08LD08

CB FLAT TOP 8"W w/24" HOLE F/F

- P3) 24" - CASTING HEIGHT - 8"
P2) 60" x 60" - CB FLAT TOP 8"W w/24" HOLE F/F - 8"
P1) 60" x 60" - BX BASE w/FLANGE 08W/12F/08EF F/n - 68"
1) CASTING - HOE KY-460-11 F/G (DBI 11)
1) 60" x 60" - Conseal CS-102 1.00"
2) Hole - 52
1) Hole - 20
2) I-Beam Notch n/n - 7"x9"x5"
6) MH Step ML-10-TDS-NCR - 10"


Structure Total: 21787 lb

Structure Notes:

- ** KYTC STATE PROJECT**
1. PER KYTC MANHOLE TYPE C / ASTM C913 SPEC'S.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY ICAST (HOE KY-510 F/C KY TY2).
4. SECONDARY POUR REQ'D FOR EXTENDED FLANGE (8"W x 12" THICK).
REINFORCING PER ASTM A615 (GRADE 60).
- TRANS. SLAB #5's AT 6" C.C.E.W (DBL MAT).
- WALLS #5's AT 6" C.C.E.W.
- FLOOR #5's AT 12" C.C.E.W..

NOTES:

1. MANUFACTURED TO ASTM C-913 (LATEST REVISION).
2. CONCRETE: 4,500 PSI AT 28 DAYS.
3. REINFORCING DBL BAR #5 BAR @ 6" C.C.E.W. (GRADE 60)

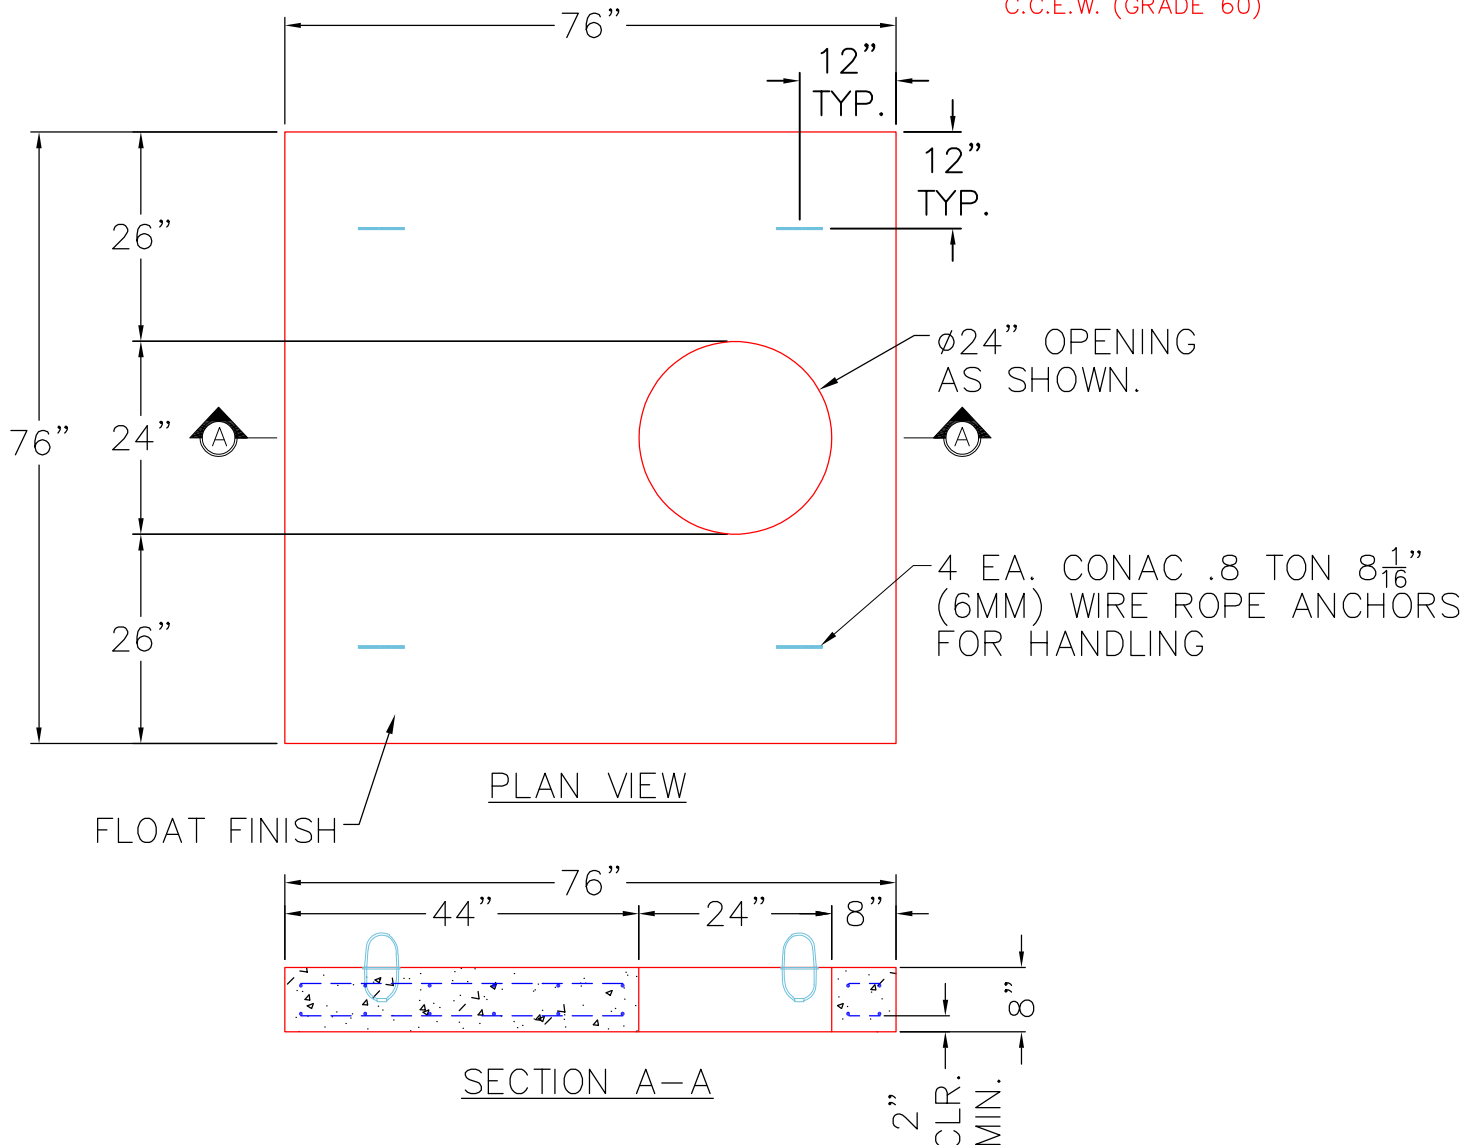

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 3574 lb
Volume (Net): 0.91cu.yd
