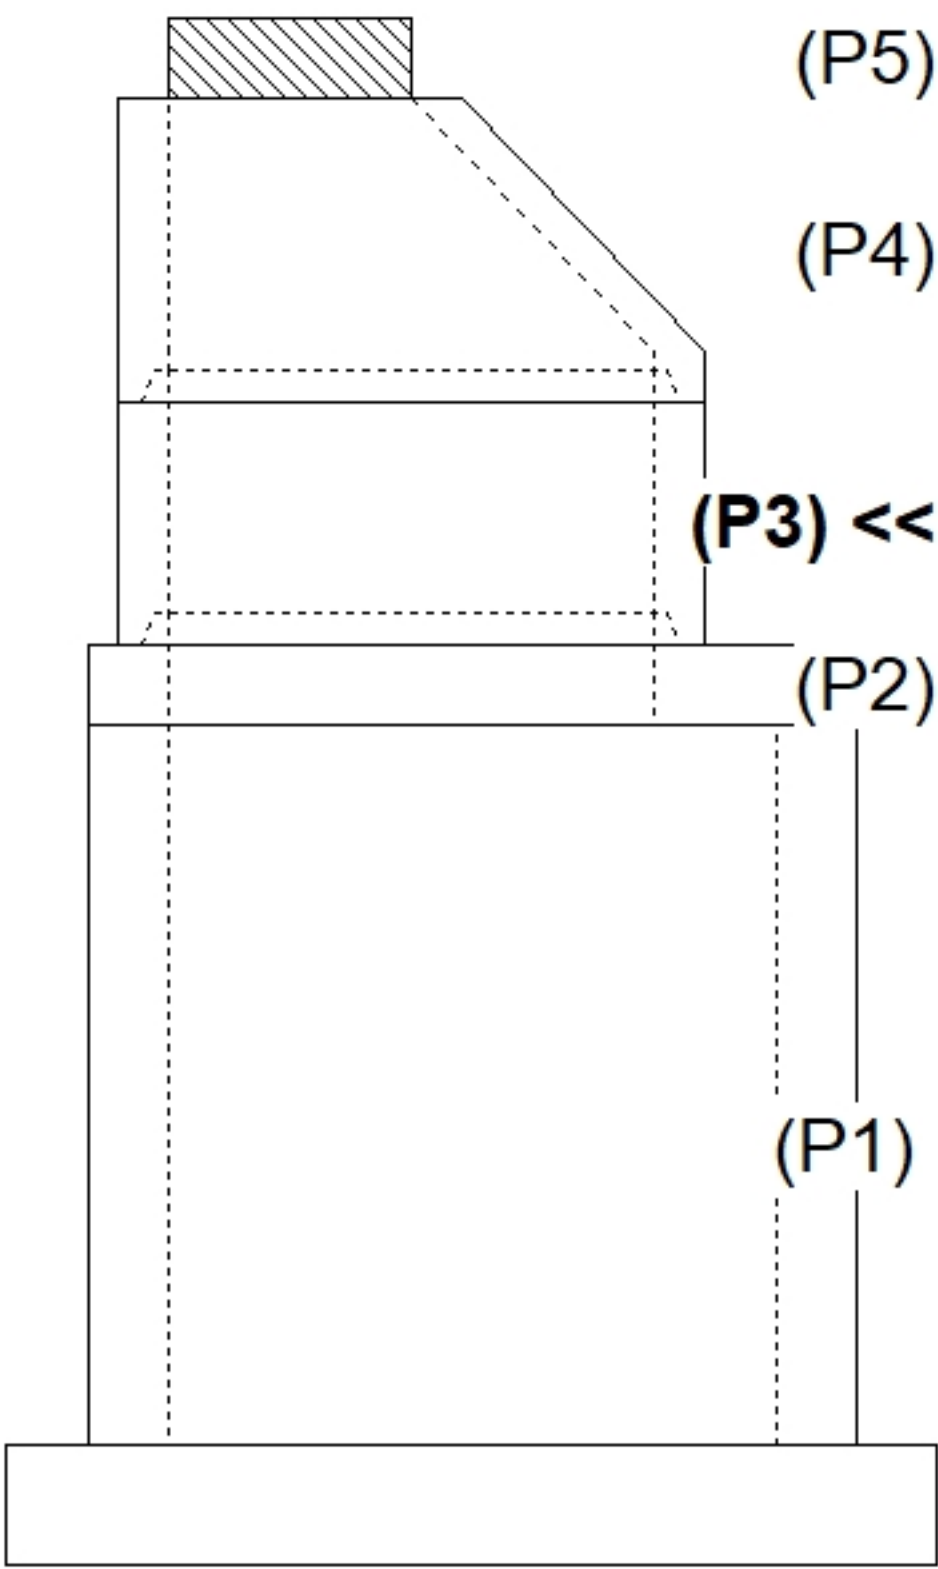
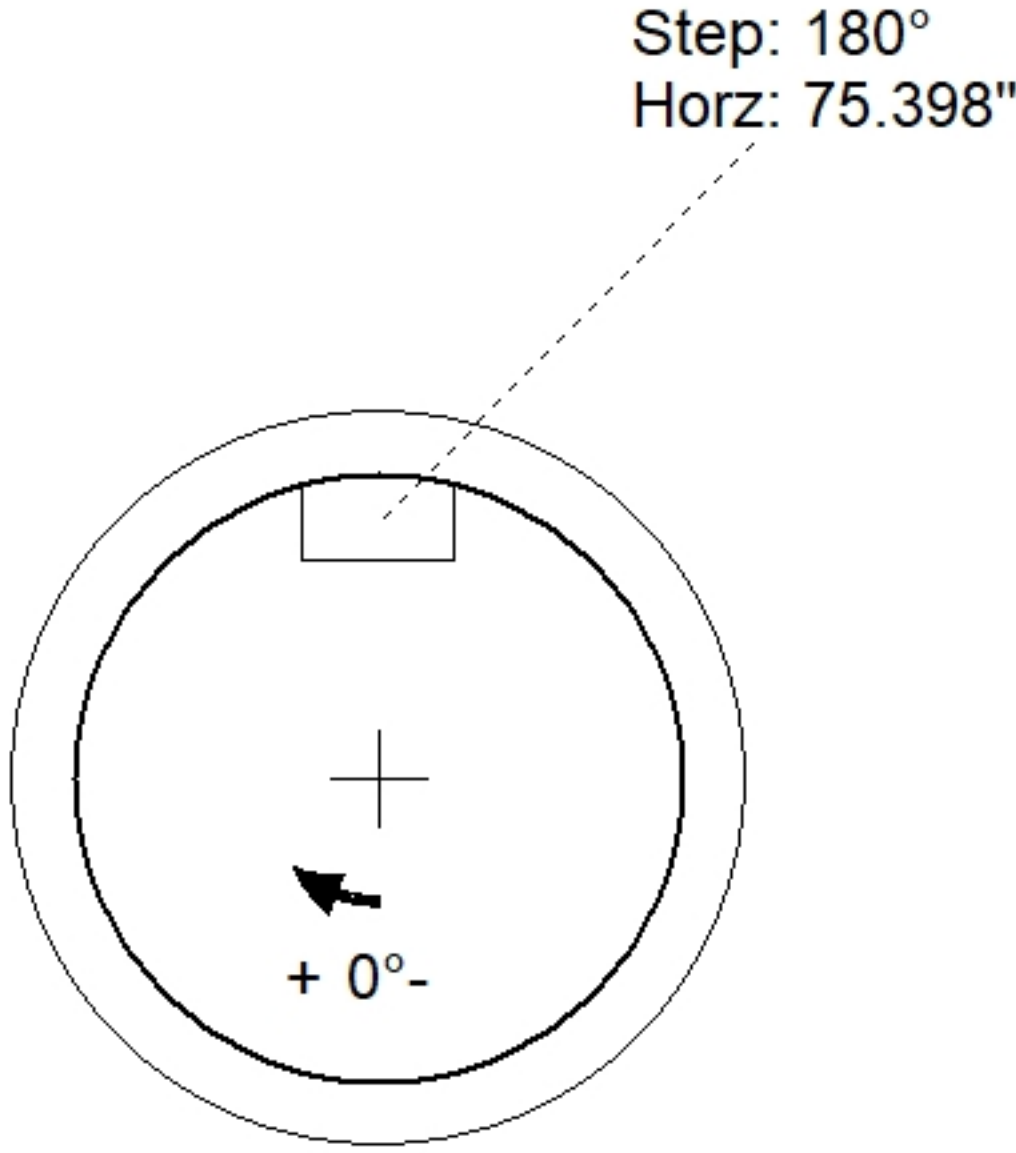
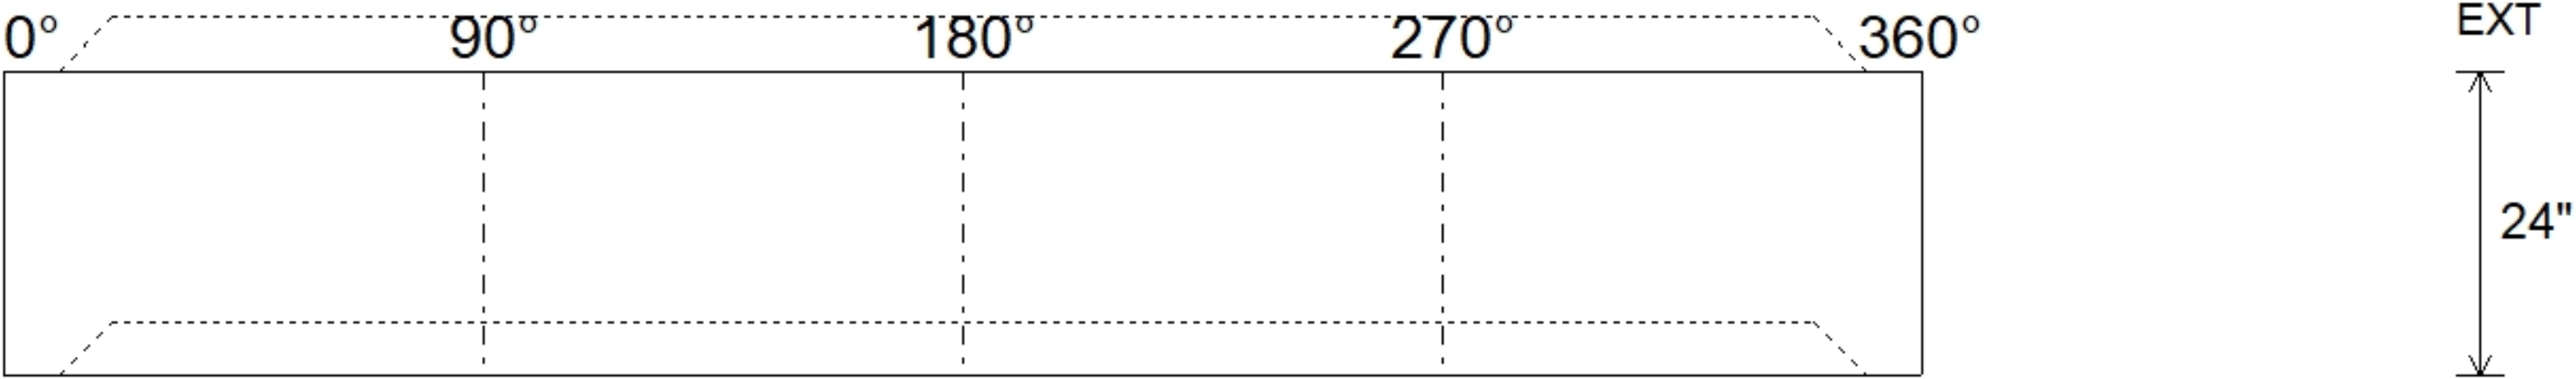


Job Name: 24-4208 - KYTC Christian Co. Call 100 (ID 241018) Job Location: Hopkinsville, KY Contractor: Scotty's Contracting & Stone, LLC				Plant: Beaver Dam 8/3/2026 4:28:41 PM		Tech: J. Horsley PC: C. Goff						
Structure ID: MH294 (450+40 RT)												
P3			MH048RS24			MH RISER T/G						
P5) 24" - CASTING HEIGHT - 8" P4) 48" - ECC CONE w/ 24" HOLE F/G - 30" P3) 48" - MH RISER T/G - 24" P2) 60" x 60" - CB FT REDUCER 48" HOLE T/F - 8" P1) 60" x 60" - BX BASE w/FLANGE 08W/12F/08EF F/n - 71" 1) CASTING - HOE KY-460-11 F/G (DBI 11) 1) 60" x 60" - Conseal CS-102 1.00" 2) 48" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 2) Hole - 56 2) I-Beam Notch n/n - 7"x9"x5" 9) MH Step ML-10-TDS-NCR - 10"						0 lb 2050 lb 1677 lb 2663 lb 17989 lb 421 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- 24800 lb		Structure Notes: . ** KYTC STATE PROJECT** 1. PER KYTC MANHOLE TYPE C / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE KY-510 F/C, KY TY2). 4. SECONDARY POUR REQ'D FOR EXTENDED FLANGE (8"WD x 12" THICK). . REINFORCING PER ASTM A615 (GRADE 60). - TRANS. SLAB #5's AT 6" C.C.E.W (DBL MAT). - WALLS #5's AT 6" C.C.E.W. - FLOOR #5's AT 12" C.C.E.W..				
Rim: 527.09' Rim to Invert: 11.82' Slack: 0.84" Sump: 0" Step Position: 180°												
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1												
Invert 2												
Invert 3												
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												
RIGHT-SIDE UP VIEW (int. dimensions)												
												
INSIDE WALL DIMENSIONS												
(P3)												
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 24" Height (Ext): 24"		Weight (Net): 1677 lb Volume (Net): 0.43cu.yd		
