

Job Name: 25-0202 Bedford GM ARV
 Job Location: Bedford, IN
 Contractor: Deig Bros Lumber & Construction Co, Inc.

Plant: Beaver Dam
 10/16/2025 7:57:59 PM

Tech: C.Russ
 PC: E.Bradley



Structure ID: ARV VAULT OPT 2

P3 BX7272_08LD08

CB FLAT TOP 8"W w/42" HOLE F/F

- P4) 42" - CASTING HEIGHT - 8"
- P3) 72" x 72" - CB FLAT TOP 8"W w/42" HOLE F/F - 8"
- P2) 72" x 72" - BOX RISER 8inW, Variable Ht F/F - 40"
- P1) 72" x 72" - P.I.P. BY OTHERS - BTM SLAB F/n - 0"
- 2) DOGHOUSE - 8"x12"
- 3) MH Step ML-10-TDS-NCR - 10"


0 lb
 4268 lb
 8433 lb
 0 lb
 0 lb
 0 lb

Structure Total: 12702 lb

Structure Notes:

1. PER ASTM C913 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO INVERT CHANNEL.
4. HOE EJ-1986 BY ICAST

REINFORCING PER ASTM A615 (GRADE 60).
 - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
 - WALLS (As 31) #5 BARS AT 12" C.C.E.W.

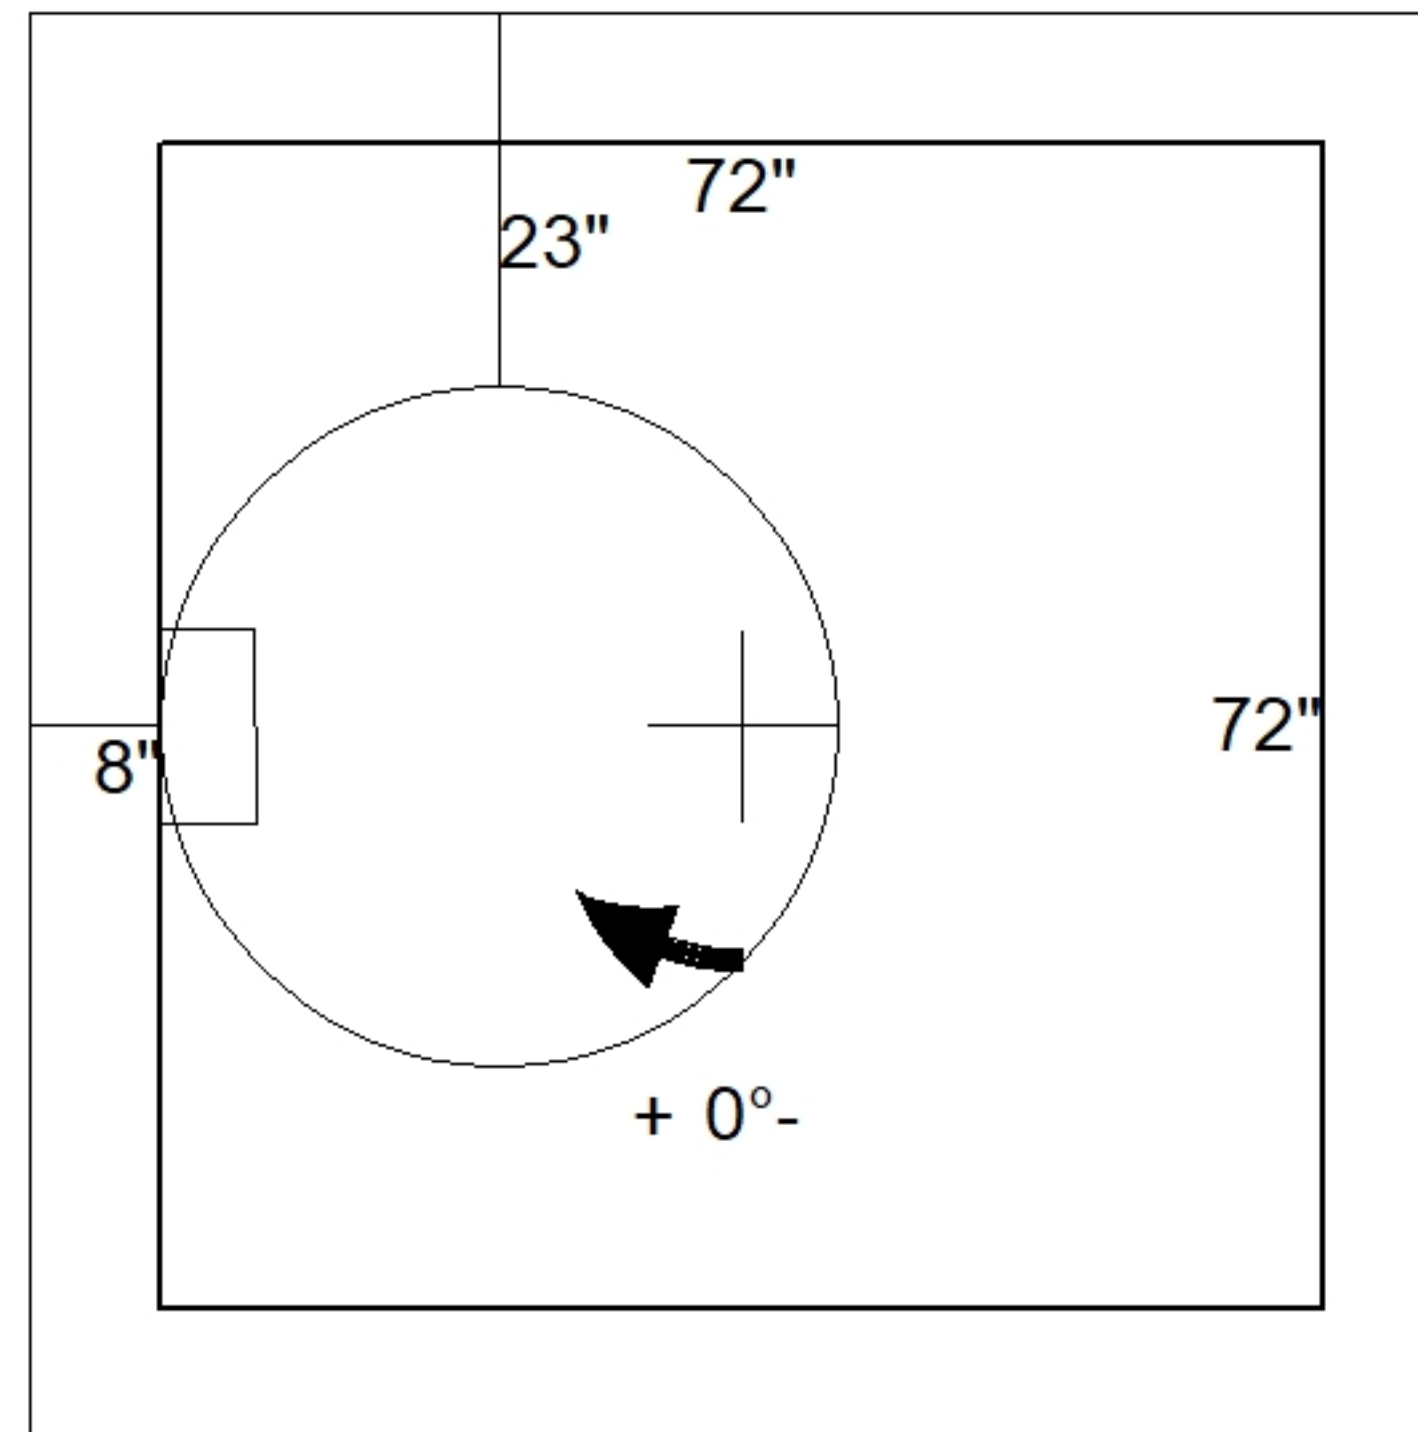

72" x 72" - CB FLAT TOP 8"W w/42" HOLE F/F - 8" - (P3)

Coating (Int):	Seam Up: Flat	Wall Thickness: 8"	Height (Ext): 8"	Weight (Net): 4268 lb
Coating (Ext):	Seam Dn: Flat			Volume (Net): 1.09cu.yd
