


KYTC STATE PROJECT

FLOATED FINISH ON TOP SURFACE

3 EA. CONAC .8 TON $8\frac{1}{16}$ " (6MM) WIRE ROPE ANCHORS REQUIRED—MINIMUM.

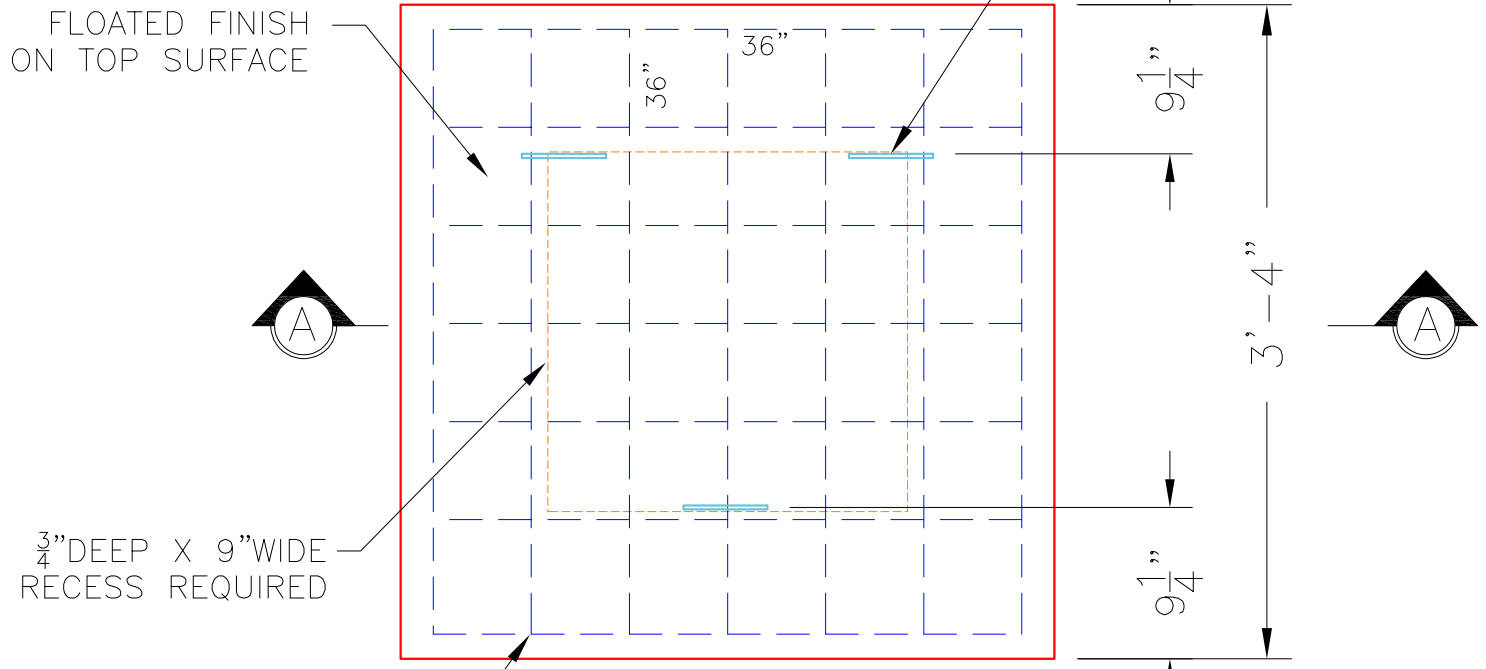


$\frac{3}{4}$ " DEEP X 9" WIDE RECESS REQUIRED

#4 BAR @ 6" C/C E.W. (TYP.)

PLAN VIEW

BULL NOSE TOP EDGE

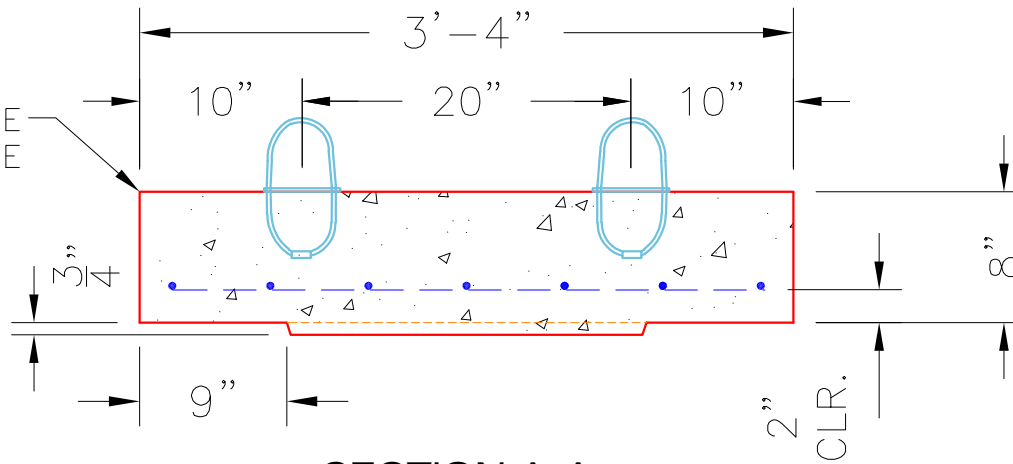


SECTION A-A

NOTES:

- CONCRETE: 4500 PSI @ 28 DAYS.
- MANUFACTURE TO KYTC SPECIFICATIONS.
- REINFORCING: #4 BAR @ 6" C/C E.W.—GRADE 60. (BOTTOM LAYER ONLY)
- 3 EA. CONAC WIRE LOOP LIFTERS REQUIRED.
- KYTC CERTIFICATIONS REQUIRED.

#4 BAR CUT LIST
14 EA. @ 36"

PRODUCTION WORK ORDER		PRODUCT I.D.: BX024024-08LD08S	DESCRIPTION: JUNCTION BOX TOP SLAB 24" X 24" X 8"	
	QUALITY CONTROL CHECKLIST	PRODUCT VIEW: RIGHT SIDE UP	CUSTOMER: CLEARY CONSTRUCTION, INC.	
	<input type="checkbox"/> ALL DIMENSIONS CORRECT.	PLANT: BEAVER DAM, KY.	PROJECT: KYTC JEFFERSON CO. 251007	
	<input type="checkbox"/> LIFTERS INSTALLED.	WEIGHT: 1,121 LBS.	STRUCTURE ID.: 117+51 LT JB-A (SEC. P2)	
	<input type="checkbox"/> NO OPENINGS.	TOP SECTION JOINT: NOT REQ'D.	SALES ORDER NO.: 25-1684P3	
	<input type="checkbox"/> REINFORCING CORRECT.	BOTTOM JOINT: $\frac{3}{4}$ " RECESS	P.C.: J. JARVIS	DRAWING: N. RICHARDS
<input type="checkbox"/> $\frac{3}{4}$ " RECESS INSTALLED.	QC CHECK INITIALS:	DATE: 02/11/26	SCALE: NTS	PG. 1 of 1
<input type="checkbox"/> TOP EDGE ROUNDED.				
<input type="checkbox"/> ANY PATCHWORK ACCEPTABLE.				
