

Contractor: Louisville Paving and Construction


PC:	J. Jarvis
TECH:	J. Horsley - A
Plant: 100	



Floor (Bot): 545.933'
Overall Height: 4.667'
Slack: 0"

1. PER KYTC DBI TYPE 14 / ASTM C-913 SPECS
2. CONCRETE: 4,000 PSI AT 28 DAYS
3. REINFORCEMENT:
 - FLAT LID: #5 BAR @ 6" C.C. E.W. (GRADE 60)
 - PIPE CHAMBER: #5 BAR @ 12" C.C. E.W. (GRADE 60)
4. NO STORM INVERT
5. NO STEPS
6. HOE KY-210 FRAME & GRATE SUPPLIED BY OTHERS - FRAME TO BE CAST INTO FLAT LID


Structure Total: 5257 lb

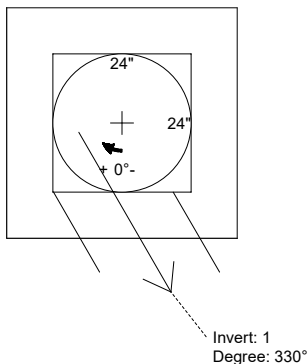

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	550.6'							
Reducer								
Invert 1	546.6'	330°	12" HDPE	14.5"	18"	Hole 18	-3"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								


24" x 24" - CB FLAT TOP 8"W (HOE KY-210) F/F - 8" - (P2)

24" x 24" - BOX BASE 8inW, 8inF, Variable Ht F/n - 40" - (P1)

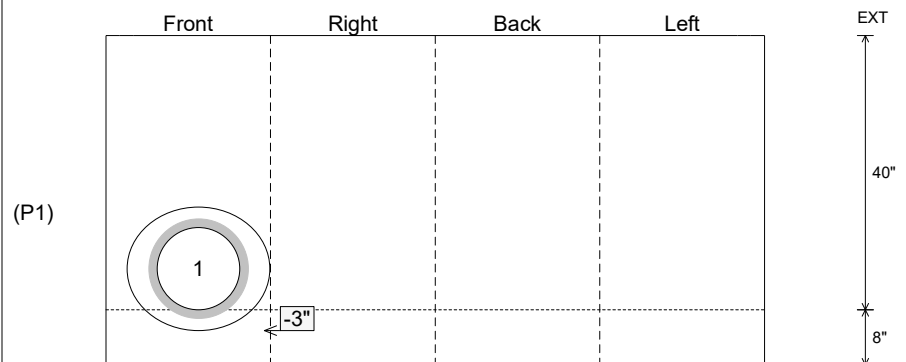
SUBMITTAL
APPROVED BY:

GENERAL NOTES:

1. MANUFACTURE TO ASTM C-913 (LATEST REVISION)
2. CONCRETE: 5,000 PSI AT 28 DAYS
3. REINFORCING: #5 BAR @ 6" C.C. E.W. (GRADE 60)
4. WEIGHT: 943 LBS
5. HOE KY-210 FRAME & GRATE SUPPLIED BY OTHERS - FRAME TO BE CAST INTO FLAT LID

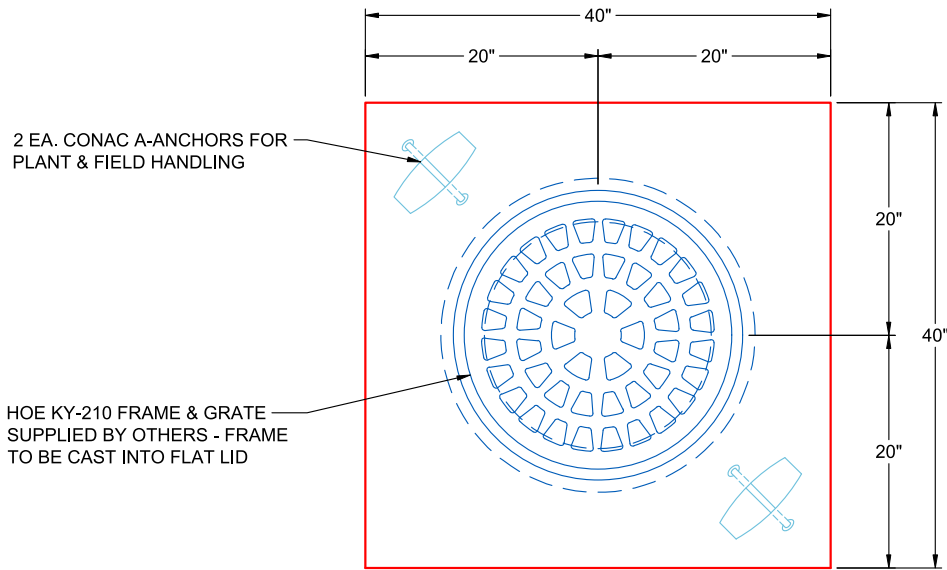

PLAN VIEW



FRONT VIEW

REVISIONS

REV. 0 DATE: NO REVISIONS TO DATE



SUBMITTAL DRAWING: 40" X 40" X 8" FLAT LID SPECIAL		
CUSTOMER: LOUISVILLE PAVING & CONSTRUCTION		
PROJECT: KYTC JEFFERSON CO CALL 106 (251315)		
STRUCTURE: 79		
SALES ORDER NO: 25-2952		
CHECKED BY: B. SMITH	DRAWN BY: K. CARDWELL	
DATE: 05/12/26	SCALE: NTS	PG. 1 OF 1
