

Job Name: 25-2977 KYTC Hopkins CO Call 105 (255382)  
 Job Location:  
 Contractor: Scotty's Contracting & Stone, LLC

Plant: Beaver Dam  
 1/12/2026 1:58:51 PM

Tech: J. Copping  
 PC: Celina Goff



**Structure ID: 1978R**

**P2 BX3636-08R42**

**BOX RISER 8inW**

- P3) 36" x 36" - P.I.P. - BY OTHERS - 8"
- P2) 36" x 36" - BOX RISER 8inW - 42"
- P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 59"
- 2) 36" x 36" - Conseal CS-102 1.00"
- 1) Hole - 26



0 lb  
 4962 lb  
 8430 lb  
 0 lb  
 0 lb  
 -----  
 Structure Total: 13392 lb

**Structure Notes:**  
 \*\*KYTC STATE PROJECT\*\*  
 1. JR HOE KY-316 PROVIDED BY ICAST.  
 2. KYTC DBI TYPE 1 / ASTM C913 SPECIFICATIONS.  
 3. CONCRETE = 4,000 PSI AT 28 DAYS.  
 4. NO STEPS.  
 5. REINFORCING PER ASTM A615 (GRADE 60).  
 - WALLS (As .31) #5 BARS AT 12" C.C.E.W.  
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.  
 6. STUB #5 BARS 20" OUT TOP OF WALLS (SPA@12"C/C)


Rim: 381.91' Rim to Invert: 9.1' Slack: 0.2" Sump: 0" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (L)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

**RIGHT-SIDE UP VIEW (int. dimensions)**

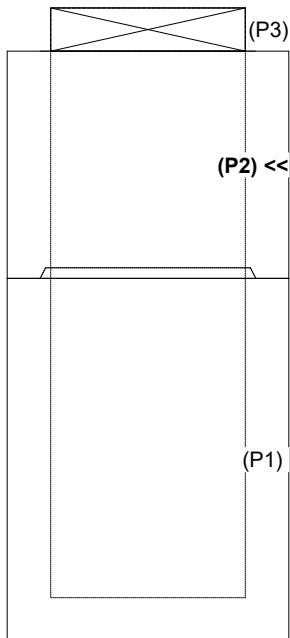

**INSIDE WALL DIMENSIONS**

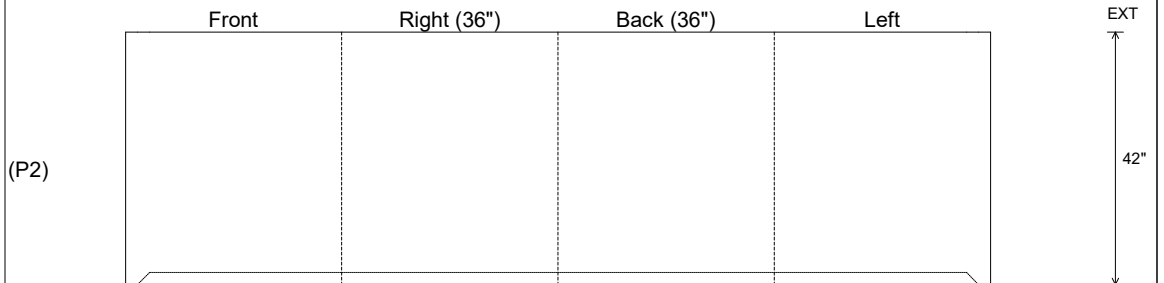

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 8" Floor Height: 0"	Height (Int): 42" Height (Ext): 42"	Weight (Net): 4962 lb Volume (Net): 1.27cu.yd
----------------------------------	----------------------------------	--	--	--
