

Job Name: 25-3000 - Wilkinson Lane PS Job Location: White House, TN Contractor: Cumberland Valley Constructors, Inc.	Plant: 100 1/12/2026 7:32:24 AM	Tech: J. Horsley - F PC: A. Chambers	
--	------------------------------------	---	--

**Structure ID: 57 x 27 Meter Box**

**P2 BX2757-06RVF**

**BOX RISER 6inW, Variable Ht F/F**



P4) 20" x 44" - HATCH (CAST FLUSH) - 3"	100 lb
P3) 27" x 57" - CB FLAT TOP 6"W w/20"x44" HATCH F/F - 6"	912 lb
P2) 27" x 57" - BOX RISER 6inW, Variable Ht F/F - 30"	2900 lb
P1) 27" x 57" - P.I.P. BY OTHERS - BTM SLAB F/n - 0"	0 lb
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212	0 lb
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)	0 lb
1) This Structure Includes a Cast-In Item - S1R 20" x 44" Hatch	0 lb
1) HATCH (Alum.) - HALLIDAY S1R 20"x44"	57 lb
1) 27" x 57" - Conseal CS-202 1.00"	0 lb
1) 27" x 57" - Conseal CS-202 1.00" (Double)	0 lb
1) No Hole	0 lb
<b>Structure Total:</b>	<b>3969 lb</b>

**Structure Notes:**  
 1. PER ASTM C-913 SPECIFICATIONS  
 2. CONCRETE: 4,000 PSI AT 28 DAYS  
 3. REINFORCEMENT: #4 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP)  
 4. HATCH BY ICAST (HALLIDAY S1R 20" X 44") - TO BE CAST INTO FLAT LID  
 5. NO STEPS  
 6. NO OPENINGS


Rim: 3'	Rim to Invert: 3'	Slack: 0"	Sump: 0"	Step Position:
---------	-------------------	-----------	----------	----------------

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ( )	Offset
Invert 1				No Hole						
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

**RIGHT-SIDE UP VIEW (int. dimensions)**

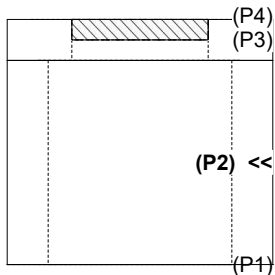

**INSIDE WALL DIMENSIONS**



Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Flat	Wall Thickness: 6" Floor Height: 0"	Height (Int): 30" Height (Ext): 30"	Weight (Net): 2900 lb Volume (Net): 0.74cu.yd
----------------------------------	--------------------------------	--	--	--
