

Job Name: 25-3193 - KYTC Kenton Co Call 328 (251320)
Job Location: Independence, KY
Contractor: Eaton Asphalt

Plant: 100

Tech: Jared - A

7/1/2026 12:33:20 PM

PC: J. Jarvis



Structure ID: 461

P3 GR3

GRADE RING

- P4) 24" - CASTING HEIGHT - 8"
P3) 24" - GRADE RING - 3"
P2) 48" - ECC CONE w/ 24" HOLE - 24"
P1) 48" - MH BASE - 54"
1) CASTING - HOE KY-510 F/C (KY TY.2)
1) 48" - Conseal CS-102 1.00"
2) Hole - 24
1) Hole - 20
6) MH Step ML-10-TDS-NCR - 10"

Structure Total:

0 lb
202 lb
1550 lb
4573 lb
510 lb
0 lb
0 lb
0 lb
0 lb

6835 lb


Structure Notes:

****KYTC STATE PROJECT****


1. HOE KY-510 F/C (KY TY2) PROVIDED BY ICAST.
2. PER KYTC MH A / ASTM C478 SPEC'S.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60.)
 - CONE (As .62)
 - RISER/WALLS (As .12)
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

NOTES:


1. GRADE RINGS MEET OR EXCEED THE FOLLOWING SPECIFICATIONS:
 - CONCRETE: 4,000 PSI @ 28 DAYS.
 - REINFORCING: (1) #3 HOOP CENTERED (GRADE 60)

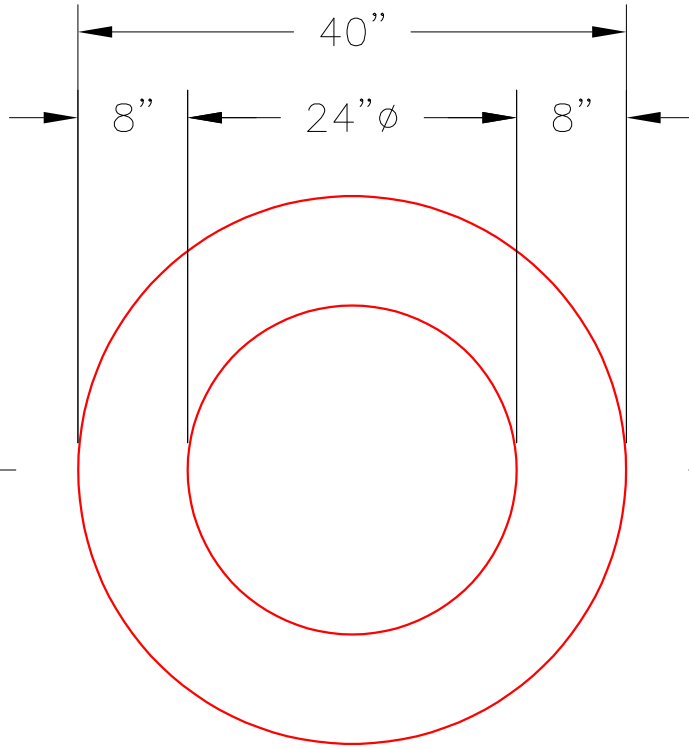

PLAN VIEW

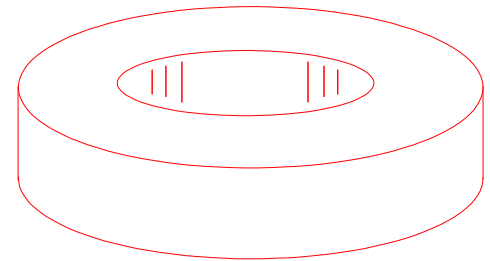

ISOMETRIC VIEW



SECTION A-A

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 3"

Weight (Net): 202 lb
Volume (Net): 0.05cu.yd
