

Job Name: 25-3193 - KYTC Kenton Co Call 328 (251320)
Job Location: Independence, KY
Contractor: Eaton Asphalt

Plant: 100

Tech: Jared - A

7/1/2026 12:33:14 PM

PC: J. Jarvis



Structure ID: 468

P2 BX024030-08LD08-15X27

CB FLAT TOP 8"W w/15"x27" HOLE


P3) 15" x 27" - P.I.P. - BY OTHERS - 8"
P2) 24" x 30" - CB FLAT TOP 8"W w/15"x27" HOLE - 8"
P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht - 40"
1) CASTING - HOE KY-230-G F/G (GRADE)
1) 24" x 30" - Conseal CS-102 1.00"
1) 15" x 27" - Conseal CS-102 1.00"
1) Hole - 24
2) Hole - 4

0 lb
963 lb
4607 lb
237 lb
0 lb
0 lb
0 lb
0 lb
Structure Total: 5807 lb

Structure Notes:

KYTC STATE PROJECT


1. HOE KY-230-G F/G (GRADE) PROVIDED BY ICAST.
2. KYTC DBI TYPE 13G / ASTM C-913 SPEC'S.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60).
 - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
 - WALLS (As .31) #5 BARS AT 12" C.C.E.W..
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.
5. STUB #5 BARS 12" OUT OF THE TOP OF THE SLAB
(SPACED AT 12" CC) AROUND THE 15" X 27" HOLE

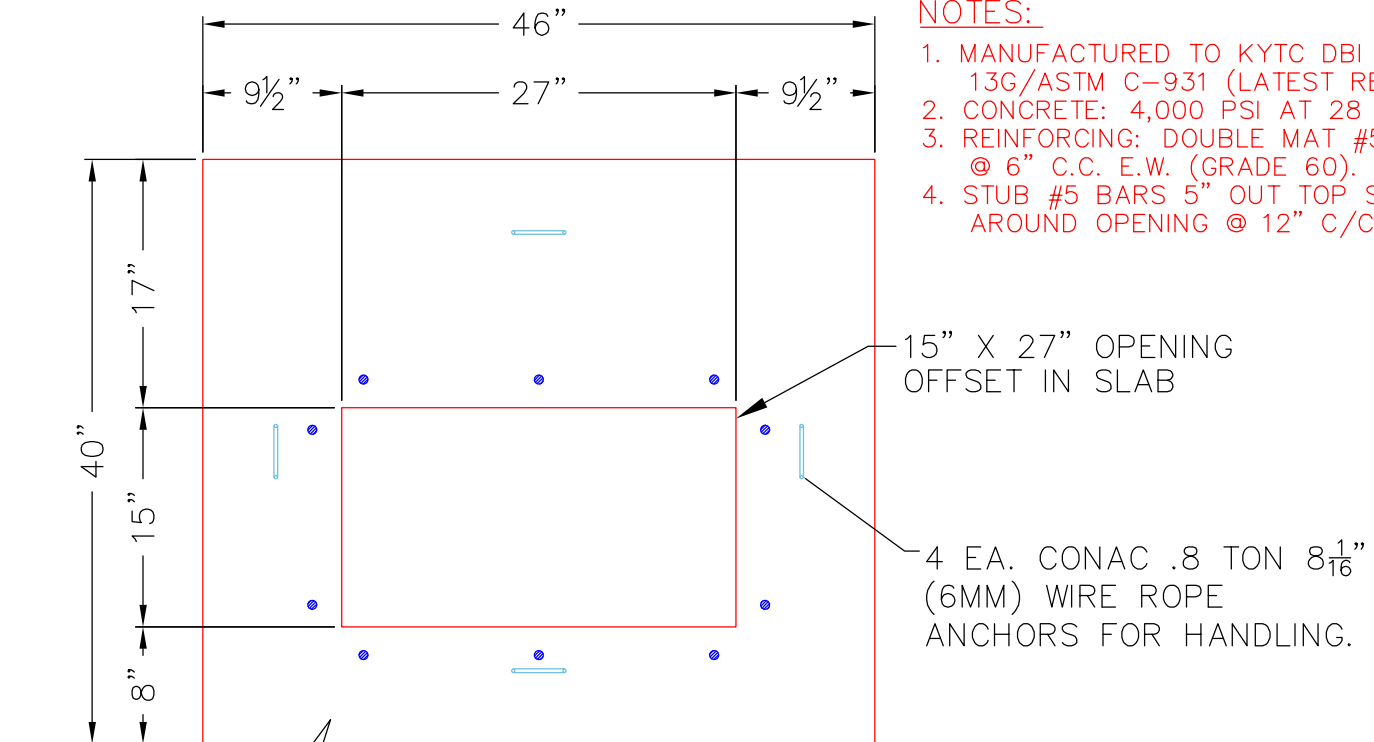

NOTES:

1. MANUFACTURED TO KYTC DBI TYPE 13G/ASTM C-931 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: DOUBLE MAT #5 BAR @ 6" C.C. E.W. (GRADE 60).
4. STUB #5 BARS 5" OUT TOP SLAB AROUND OPENING @ 12" C/C.

FLOAT FINISH **PLAN VIEW**

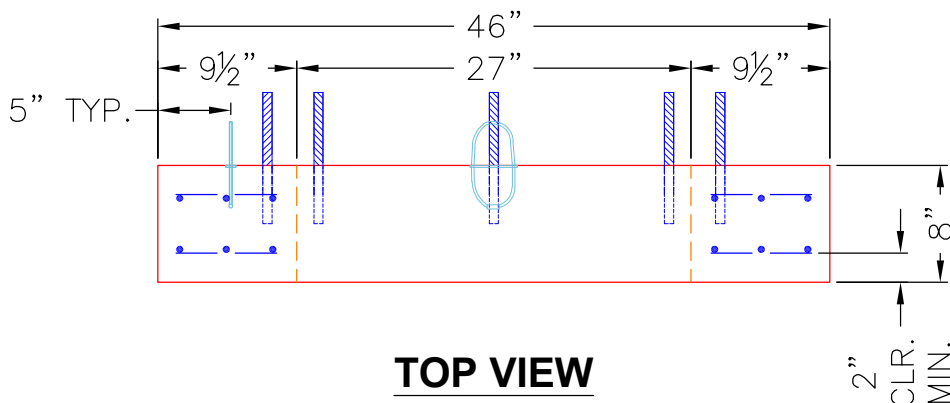

TOP VIEW

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 963 lb
Volume (Net): 0.25cu.yd
