

Job Name: 25-3193 - KYTC Kenton Co Call 328 (251320)
Job Location: Independence, KY
Contractor: Eaton Asphalt

Plant: 100

7/1/2026 12:33:12 PM

Tech: Jared - A

PC: J. Jarvis



Structure ID: 474

P2 BX036036-08TS024036

CB TRANSITION SLAB 24"X36" HOLE

P4) 24" x 120" - CB INLET KY A 10' TOP LEFT - 10"
P3) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT - 18"
P2) 36" x 36" - CB TRANSITION SLAB 24"X36" HOLE - 8"
P1) 36" x 36" - BOX BASE 8inW, 8inF - 54"
1) CASTING - HOE KY-206 F/C (KY TY1)
1) 36" x 36" - Conseal CS-102 1.00"
1) 24" x 36" - Conseal CS-102 1.00"
2) Hole - 32
1) Hole - 24
2) Hole - 8


3400 lb
5270 lb
1235 lb
6701 lb
206 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 16812 lb


Structure Notes:

**** KYTC STATE PROJECT ****

1. HOE KY 206 F/C (KY TY1) PROVIDED BY ICAST.
2. CONCRETE = 4,000 PI AT 28 DAYS.
3. REINFORCING PER ASTM A615 (GRADE 60).
 - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W.
 - WALLS (As .31) #5 BARS AT 12" C.C.E.W.
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

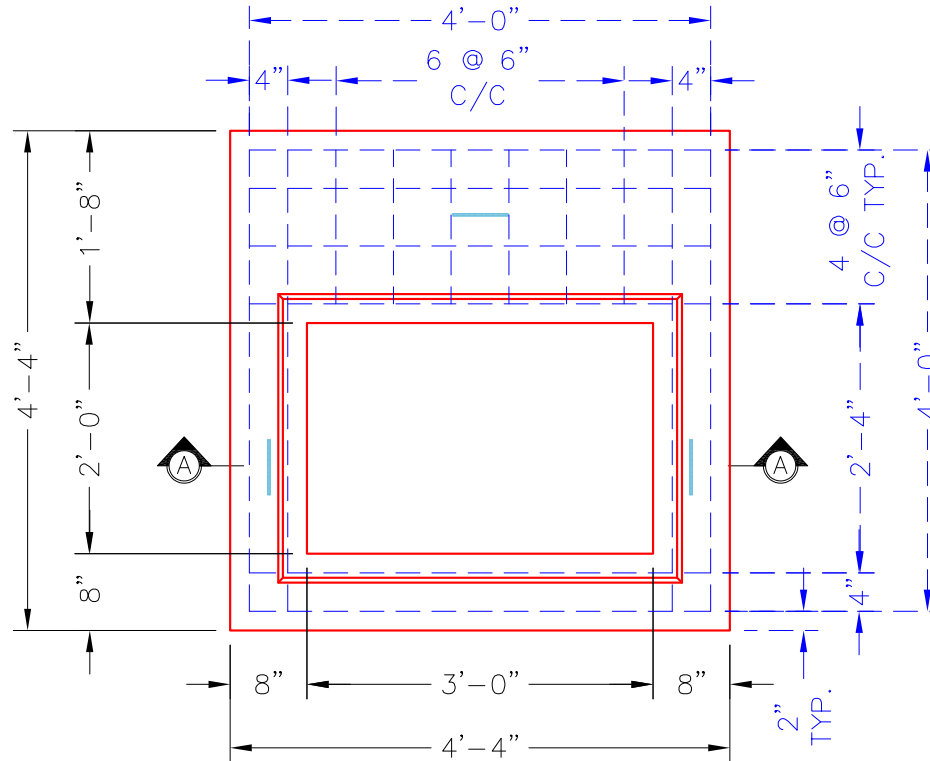

PLAN VIEW

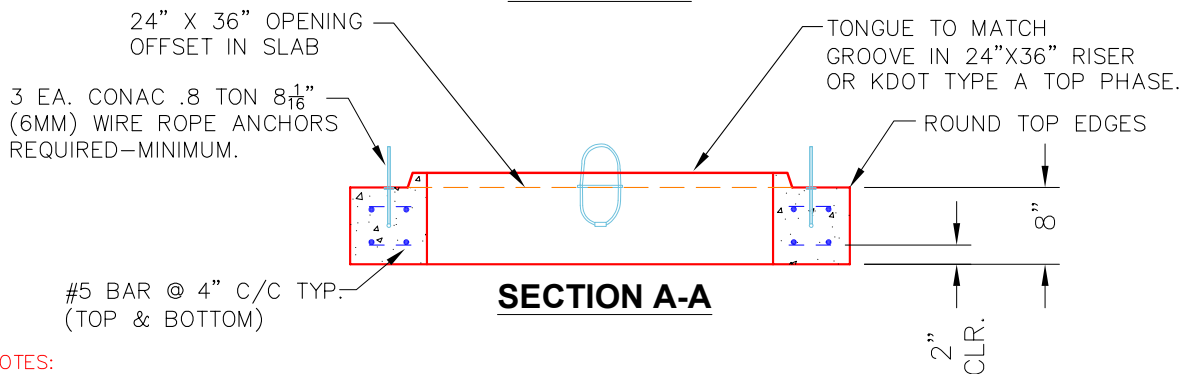

NOTES:

- CONCRETE: 4500 PSI @ 28 DAYS.
- REINFORCING: #5 BAR @ 4" & 6" C/C-GRADE 60.
(TOP & BOTTOM LAYERS).
- 3 EA. CONAC WIRE LOOP LIFTERS REQUIRED.

#5 BAR CUT LIST
20 EA. @ 48" LG.
12 EA. @ 16" LG.

Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 1235 lb
Volume (Net): 0.32cu.yd
