

Contractor: Eaton Asphalt

Plant: 100




Slack: 0"

1. PER KYTC DBI TY 1 / ASTM C-913 SPECS
2. CONCRETE: 4,000 PSI AT 28 DAYS
3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60)
4. NO STORM INVERT
5. NO STEPS
6. KY-316 FRAME & GRATES SUPPLIED BY ICAST - FRAME TO BE POURED IN PLACE BY OTHERS
7. STUB #5 BAR @ 12" C.C. (GRADE 60) 20" OUT TOP OF WALLS FOR FIELD POUR TIE-IN

P2) 36" x 36" - P.I.P. - BY OTHERS - 8"
P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 28"
1) CASTING - HOE KY-316 SET (DBI 1)
1) 36" x 36" - Conseal CS-102 1.00"
1) Hole - 24



0 lb
4820 lb
317 lb
0 lb
0 lb

Structure Total: 5137 lb



Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	892'							
Reducer								
Invert 1	889'	0°	18" ADS N-12	22"	24"	Hole 24	-3"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Cast (Int. Dim.) - Interior Dimensions

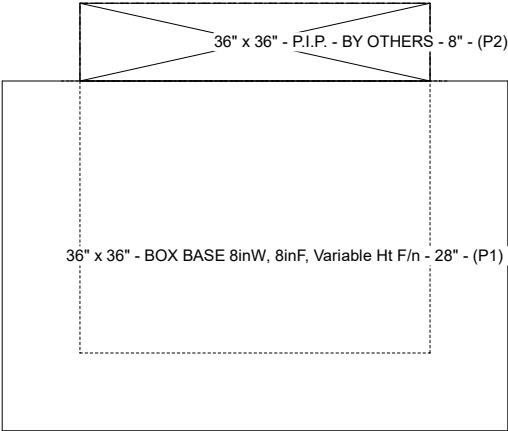

Submittal Drawing
6/5/2026 9:49:55 AM

SUBMITTAL
APPROVED BY:
