

Job Name: 25-3193 - KYTC Kenton Co Call 328 (251320)
Job Location: Independence, KY
Contractor: Eaton Asphalt

Plant: 100
6/10/2026 11:59:11 AM

Tech: Jared - A
PC: J. Jarvis




Structure ID: ICAST LI6 (9)


P1 HWSF18

18" - SLOPED & FLARED HEADWALL F/F


DIMENSIONS									
PIPE Ø	A	B	C	D	E	F	G	H	I
18"	3'-10"	3'-9"	2'-3"	1'-6"	4'-6"	4"	2'-6"	2'-2"	5'-2"
									WEIGHT
									3,640 LBS.

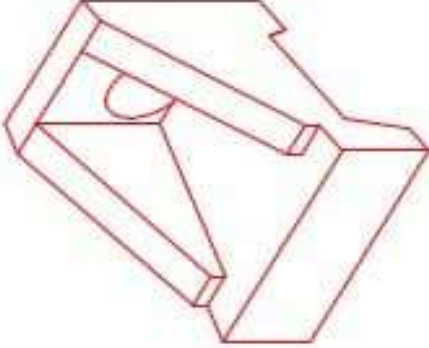

ISOMETRIC VIEW
18" HEADWALL

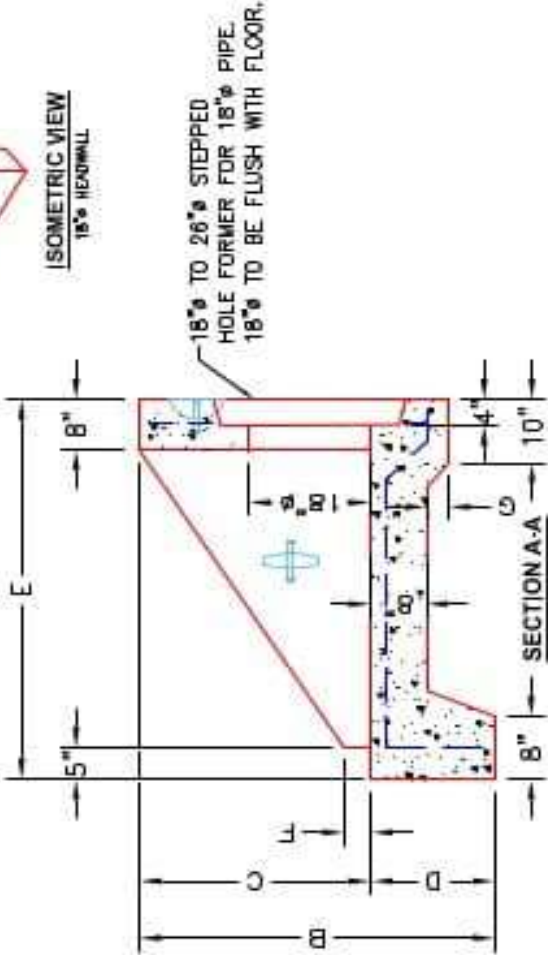


FRONT ELEVATION

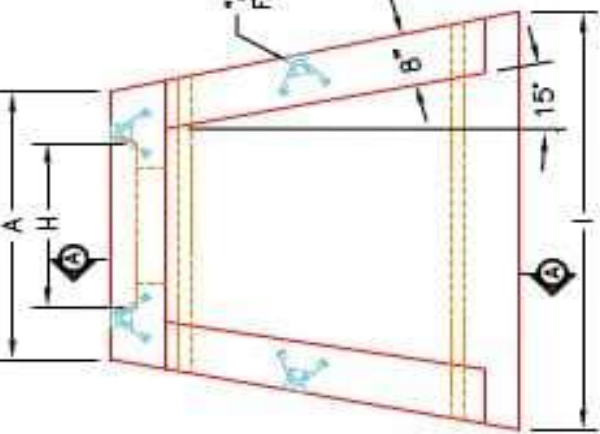

PLAN VIEW

"A"-ANCHOR LIFTING SYSTEM
FOR PLANT & FIELD HANDLING.

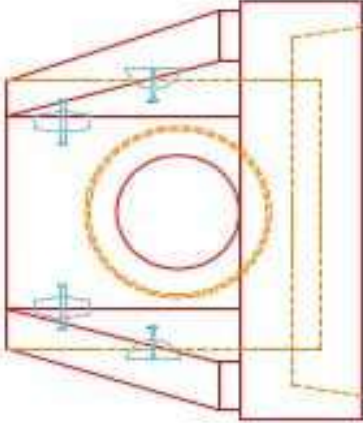

ISOMETRIC VIEW
18" HEADWALL

NOTES:

1. CONCRETE: 4500 PSI @ 28 DAYS
2. REINFORCING: #4 BAR @ 12" C/C E-W; GRADE 60, (WITH 2" CONCRETE COVER MINIMUM)
3. REINFORCING BARS TO BE TACK WELDED OR TIED.
4. DRAWING TO BE USED IN CONJUNCTION WITH KYTC STD. DRAWING RDH-000-03 AND THE STANDARD SPECIFICATIONS FOR ROAD AND BRIDGE CONSTRUCTION.
5. CHAMFER ON ALL EXPOSED EDGES.

PRODUCTION WORK ORDER

QUALITY CONTROL CHECKLIST	
☐	ALL DIMENSIONS CORRECT.
☐	LIFTERS INSTALLED.
☐	STEPPED IF CORRECT SIZE.
☐	REINFORCING CORRECT.
☐	DISPATCHER BLOCK INSTALLED.
☐	EDGES CHAMFERED.
☐	ALL PATCHWORK ACCEPTABLE.



DESCRIPTION: KYTC 18" SLOPED & FLARED HEADWALL
CUSTOMER: STOCK
PROJECT: STOCK INVENTORY
STRUCTURE ID.: N/A
QUOTE/SALES ORDER NO: N/A
CHECK: JH. ROSS, PE
DATE: REV. 4/22/24
SCALE: NTS
PG. 1 of 1

THIS DRAWING IS THE PROPERTY OF INFRASTRUCTURE PRECAST, INC. ANY USE OR DUPLICATION OF THIS DRAWING WITHOUT PRIOR AUTHORIZATION IS STRICTLY PROHIBITED.
