

Job Name: 25-3193 - KYTC Kenton Co Call 328 (251320)
Job Location: Independence, KY
Contractor: Eaton Asphalt

Plant: 100
6/10/2026 11:59:14 AM

Tech: Jared - A
PC: J. Jarvis




Structure ID: ICAST LI7 (6)


P1 HWSF24

24" - SLOPED & FLARED HEADWALL F/F


DIMENSIONS									
PIPE Ø	A	B	C	D	E	F	G	H	I
24"	3'-8"	4'-4"	2'-10"	1'-8"	5'-0"	4"	3"	2'-10"	6'-0"
									WEIGHT
									4,956 LBS.

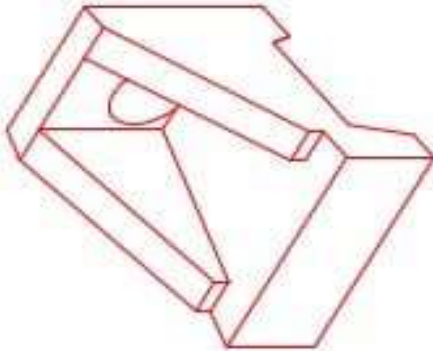


ISOMETRIC VIEW
24" HEADWALL

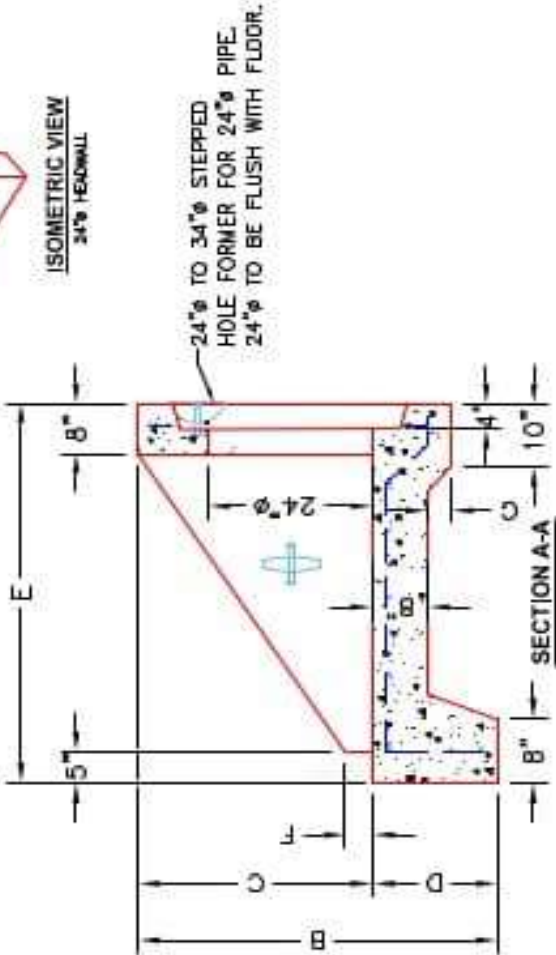

SECTION A-A

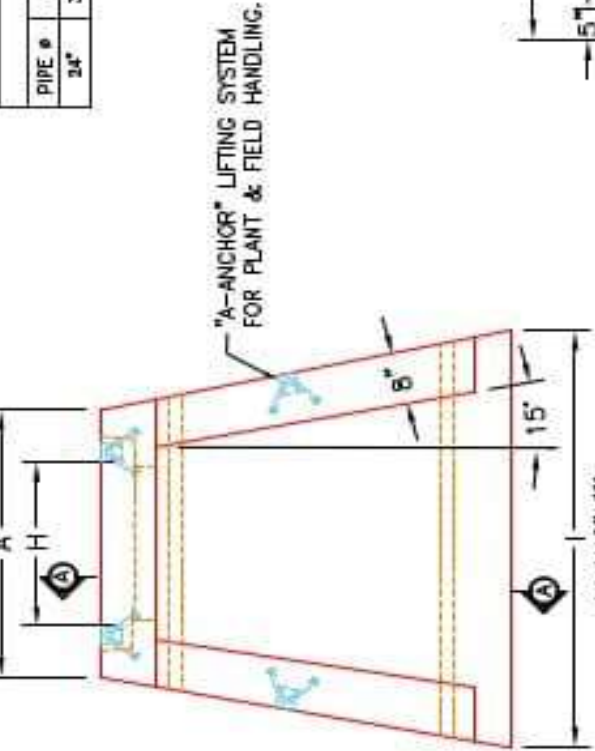

PLAN VIEW

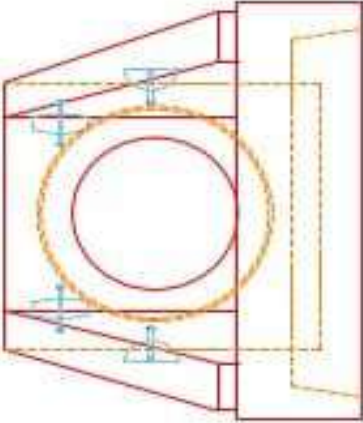

FRONT ELEVATION

- NOTES:
1. CONCRETE 4000 PSI @ 28 DAYS.
 2. REINFORCING #4 BAR @ 12" O.C. E.W. - GRADE 60, (WITH 3" CONCRETE COVER MINIMUM)
 3. REINFORCING BARS TO BE TACK WELDED OR TIED.
 4. DRAWING TO BE USED IN CONJUNCTION WITH KYTC STD. DRAWING RCH-020-03 AND THE STANDARD SPECIFICATIONS FOR ROAD AND BRIDGE CONSTRUCTION.
 5. CHAMFER ON ALL EXPOSED EDGES.

PRODUCTION WORK ORDER

QUALITY CONTROL CHECKLIST	
☐	ALL DIMENSIONS CORRECT.
☐	LETTERS INSTALLED.
☐	STEPPED HF CORRECT SIZE.
☐	REINFORCING CORRECT.
☐	DISSIPATOR BLOCK INSTALLED.
☐	EDGES CHAMFERED.
☐	ALL PATCHWORK ACCEPTABLE.



DESCRIPTION: KYTC 24" SLOPED & FLARED HEADWALL
CUSTOMER: STOCK
PROJECT: STOCK INVENTORY
STRUCTURE ID.: N/A
QUOTE/SALES ORDER NO: N/A
CHECK: J.H. ROSS, PE
DRAWING: N. RICHARDS
DATE: REV. 4/22/24
SCALE: NTS
PG. 1 of 1

THIS DRAWING IS THE PROPERTY OF INFRASTRUCTURE PRECAST, INC. ANY USE OR DUPLICATION OF THIS DRAWING WITHOUT PRIOR AUTHORIZATION IS STRICTLY PROHIBITED.
