
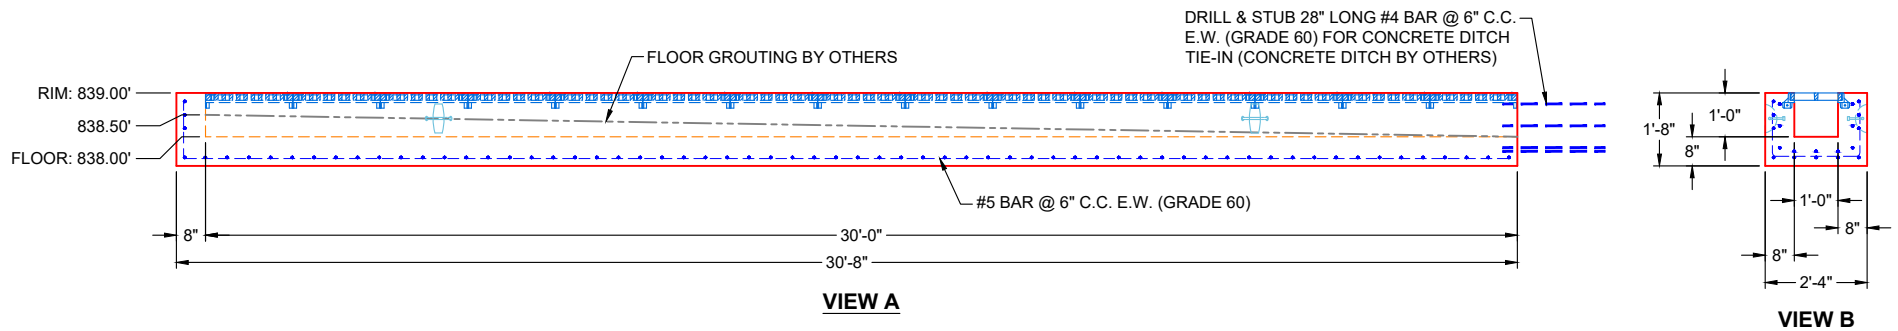


GENERAL NOTES:

1. PER KYTC DBI TY 12 / ASTM C-913 SPECIFICATIONS
2. CONCRETE: 4,500 PSI AT 28 DAYS
3. REINFORCEMENT: #5 BAR @ 6" C.C. E.W. (GRADE 60)
4. TOTAL WEIGHT:
30'-0" X 1'-0" X 1'-0" BASE: 12,943 LBS
KY-65 CAST-IN FRAMES: 450 LBS
KY-65 GRATES: 1,500 LBS
5. CONTRACTOR TO VERIFY ALL DIMENSIONS BEFORE MANUFACTURE
6. HOE KY-65 (KYTC DBI TY 12) FRAMES & GRATES SUPPLIED BY ICAST - FRAMES TO BE CAST INTO TOP OF WALLS
7. DRILL & STUB 28" LONG #4 BAR @ 6" C.C. E.W. (GRADE 60) FOR CONCRETE DITCH TIE-IN (CONCRETE DITCH BY OTHERS) - MIN. 4" PENETRATION INTO BASE

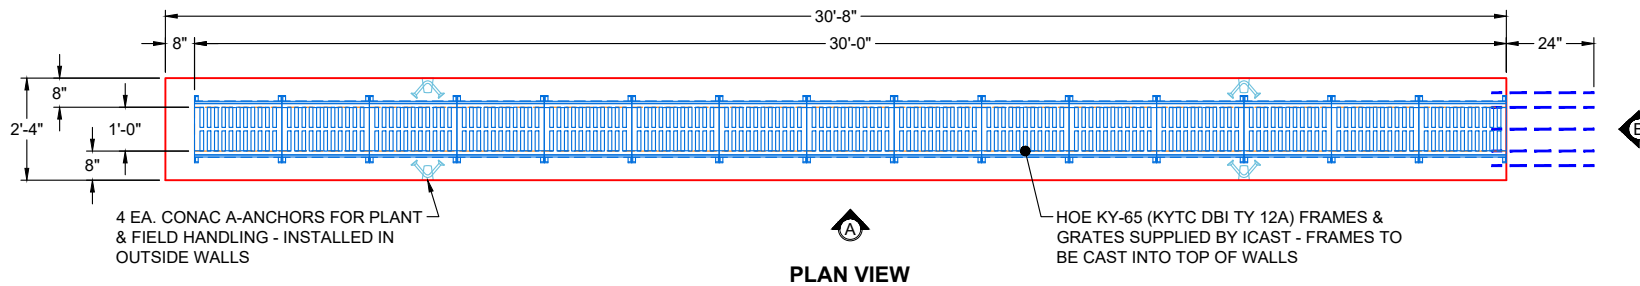

REVISION INFORMATION

REV.  DATE: NO REVISIONS TO DATE



SUBMITTAL DRAWING: 30'-0" X 1'-0" X 1'-0" TRENCH DRAIN

CUSTOMER: EDMONSON PLUMBING & HEATING SUPPLY

PROJECT: BUCK HILLS SUBDIVISION

STRUCTURE: ICAST LI10

QUOTE/SALES ORDER NO: 25-3241

CHECKED BY: B. SMITH

DRAWN BY: K. CARDWELL

DATE: 05/19/26

SCALE: NTS

PG. 1 OF 1
