

Contractor: Kauffeld Brothers Construction

Plant: 100




Slack: 0.61"

1. HOE 360 FLAT SET PROVIDED BY ICAST.
2. PER ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60).
 - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
 - RISER/WALLS (As .12)
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


P3) 24" x 30" - CASTING HEIGHT - 6"
P2) 48" - MH FLAT TOP w/24"x30" Hole - 12"
P1) 48" - MH BASE Custom Ht - 55"
1) CASTING - HOE 360 L Vane Set (F/G/H)
1) 48" - Conseal CS-102 1.00"
1) 24" x 30" - Conseal CS-102 1.00"
3) Hole - 18

0 lb
1935 lb
4845 lb
362 lb
0 lb
0 lb
0 lb


Structure Total: 7143 lb

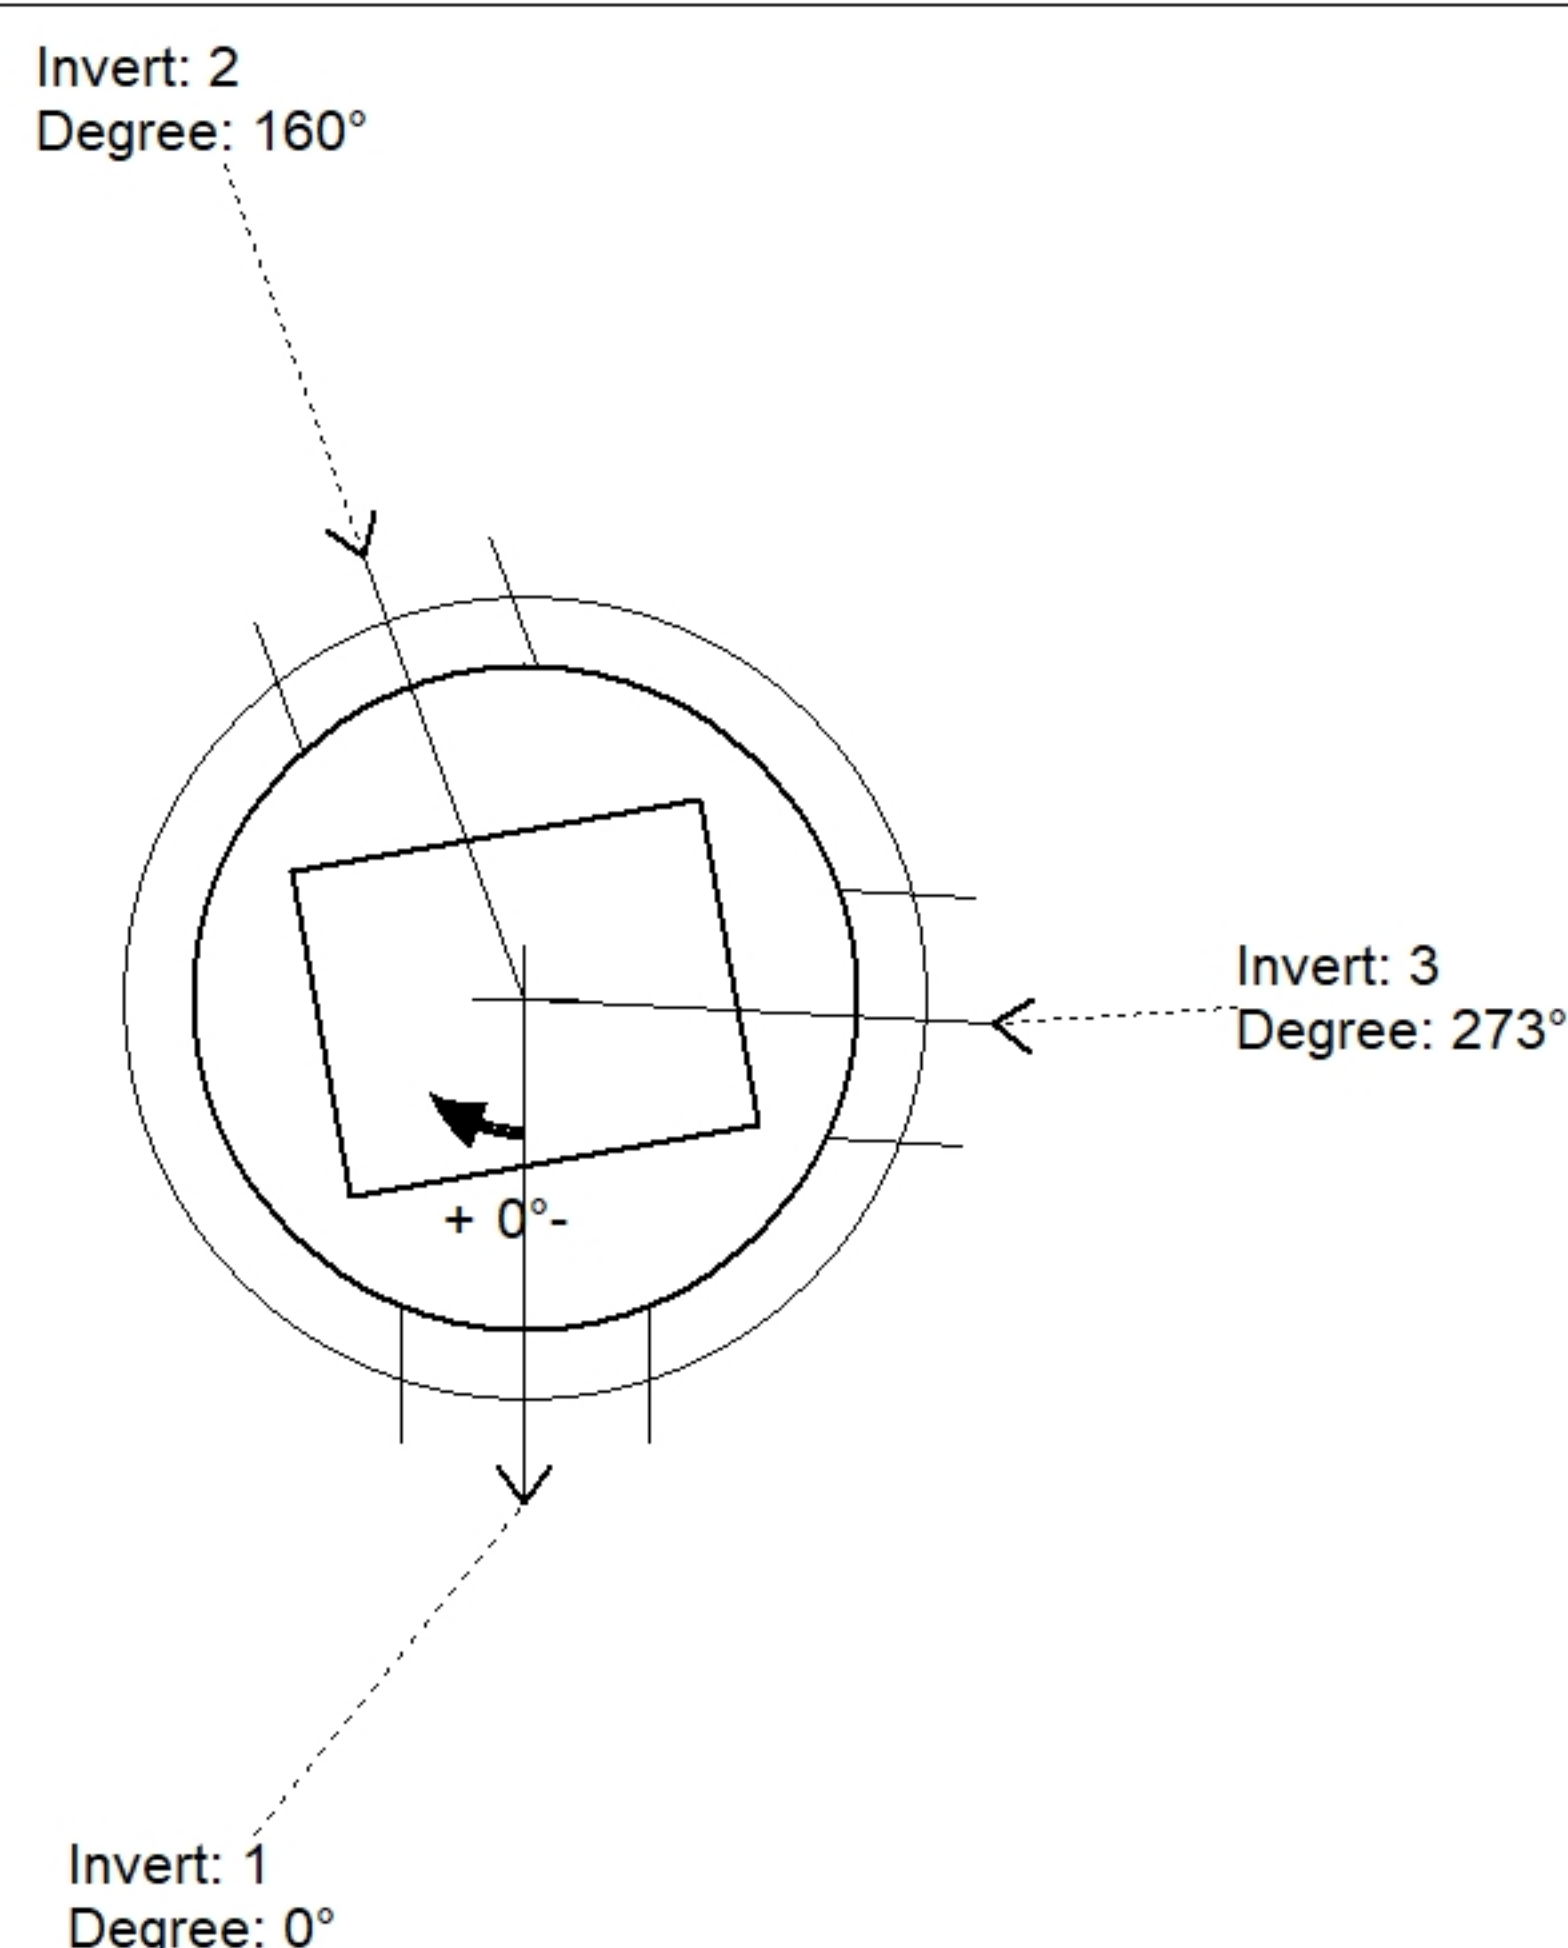

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	884.38'							
Reducer								
Invert 1	878.35'	0°	12" HDPE	14.5"	18"	Hole 18	0"	P1
Invert 2	878.46'	160°	12" HDPE	14.5"	18"	Hole 18	1.32"	P1
Invert 3	878.43'	273°	12" HDPE	14.5"	18"	Hole 18	0.96"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

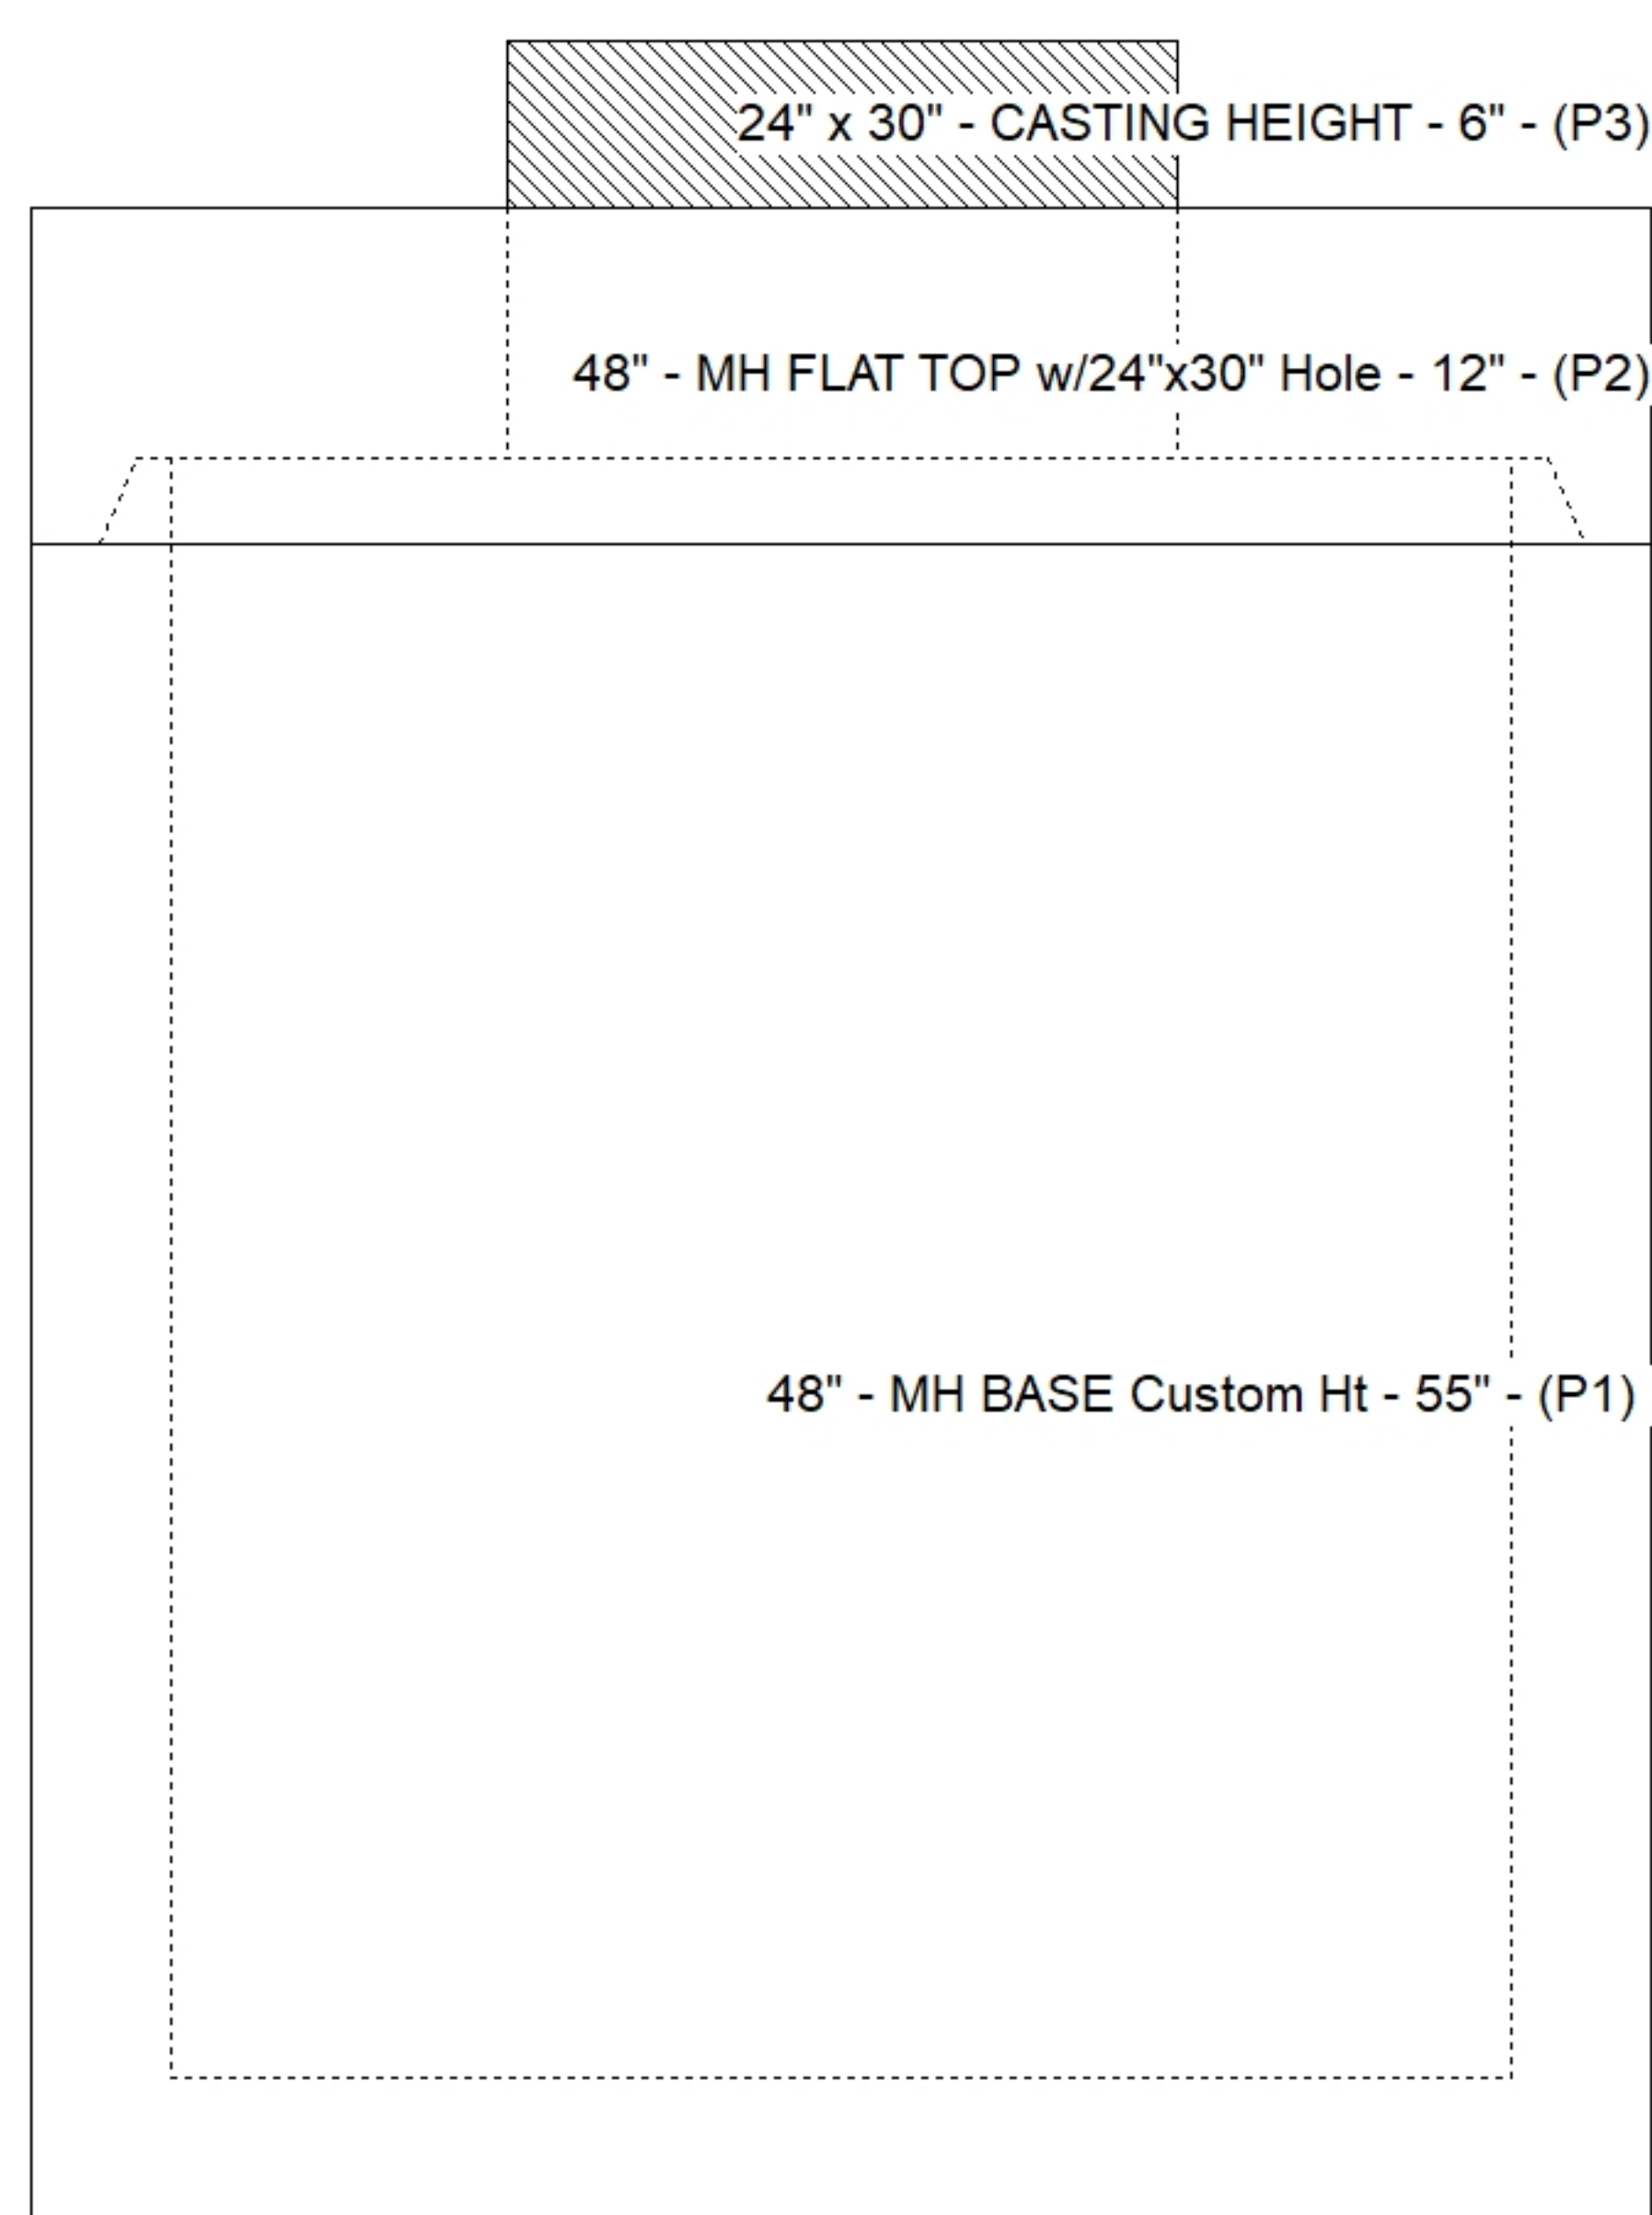

Default - Interior Dimensions

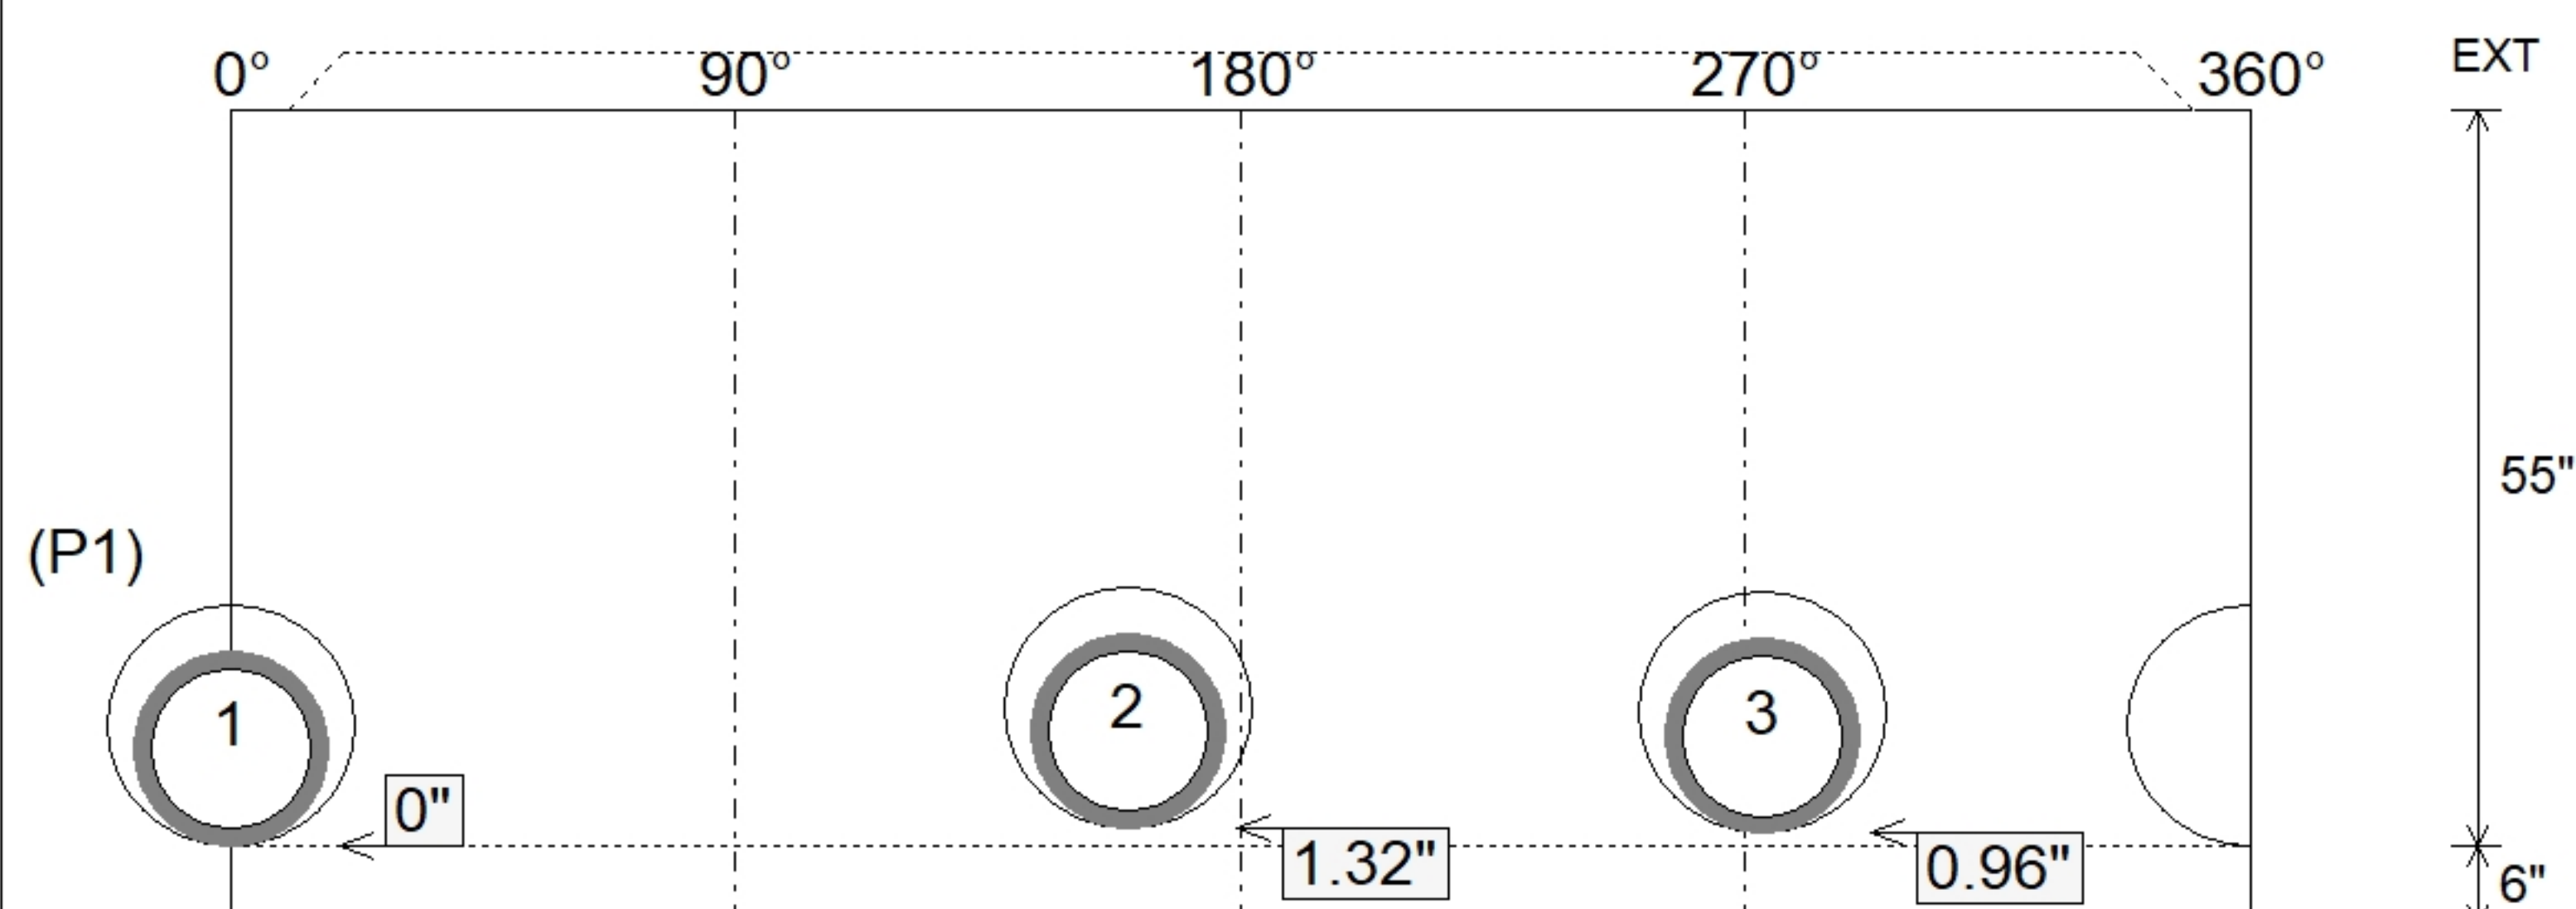

Submittal Drawing
8/3/2026 9:28:00 AM

SUBMITTAL
APPROVED BY:
