

Contractor: Scotty's Contracting & Stone, LLC

Plant: Beaver Dam



Size: 72"

Rim to Invert: 7.68'

Floor Height: 8"

Slack: 0.66"


REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .18)
- FLOOR (As .37) #5 BARS AT 10" C.C.E.W.


6) MH Step ML-10-TDS-NCR - 10"

0 lb
4561 lb
12552 lb
421 lb
0 lb
0 lb
0 lb
0 lb
0 lb


Structure Total: 17534 lb

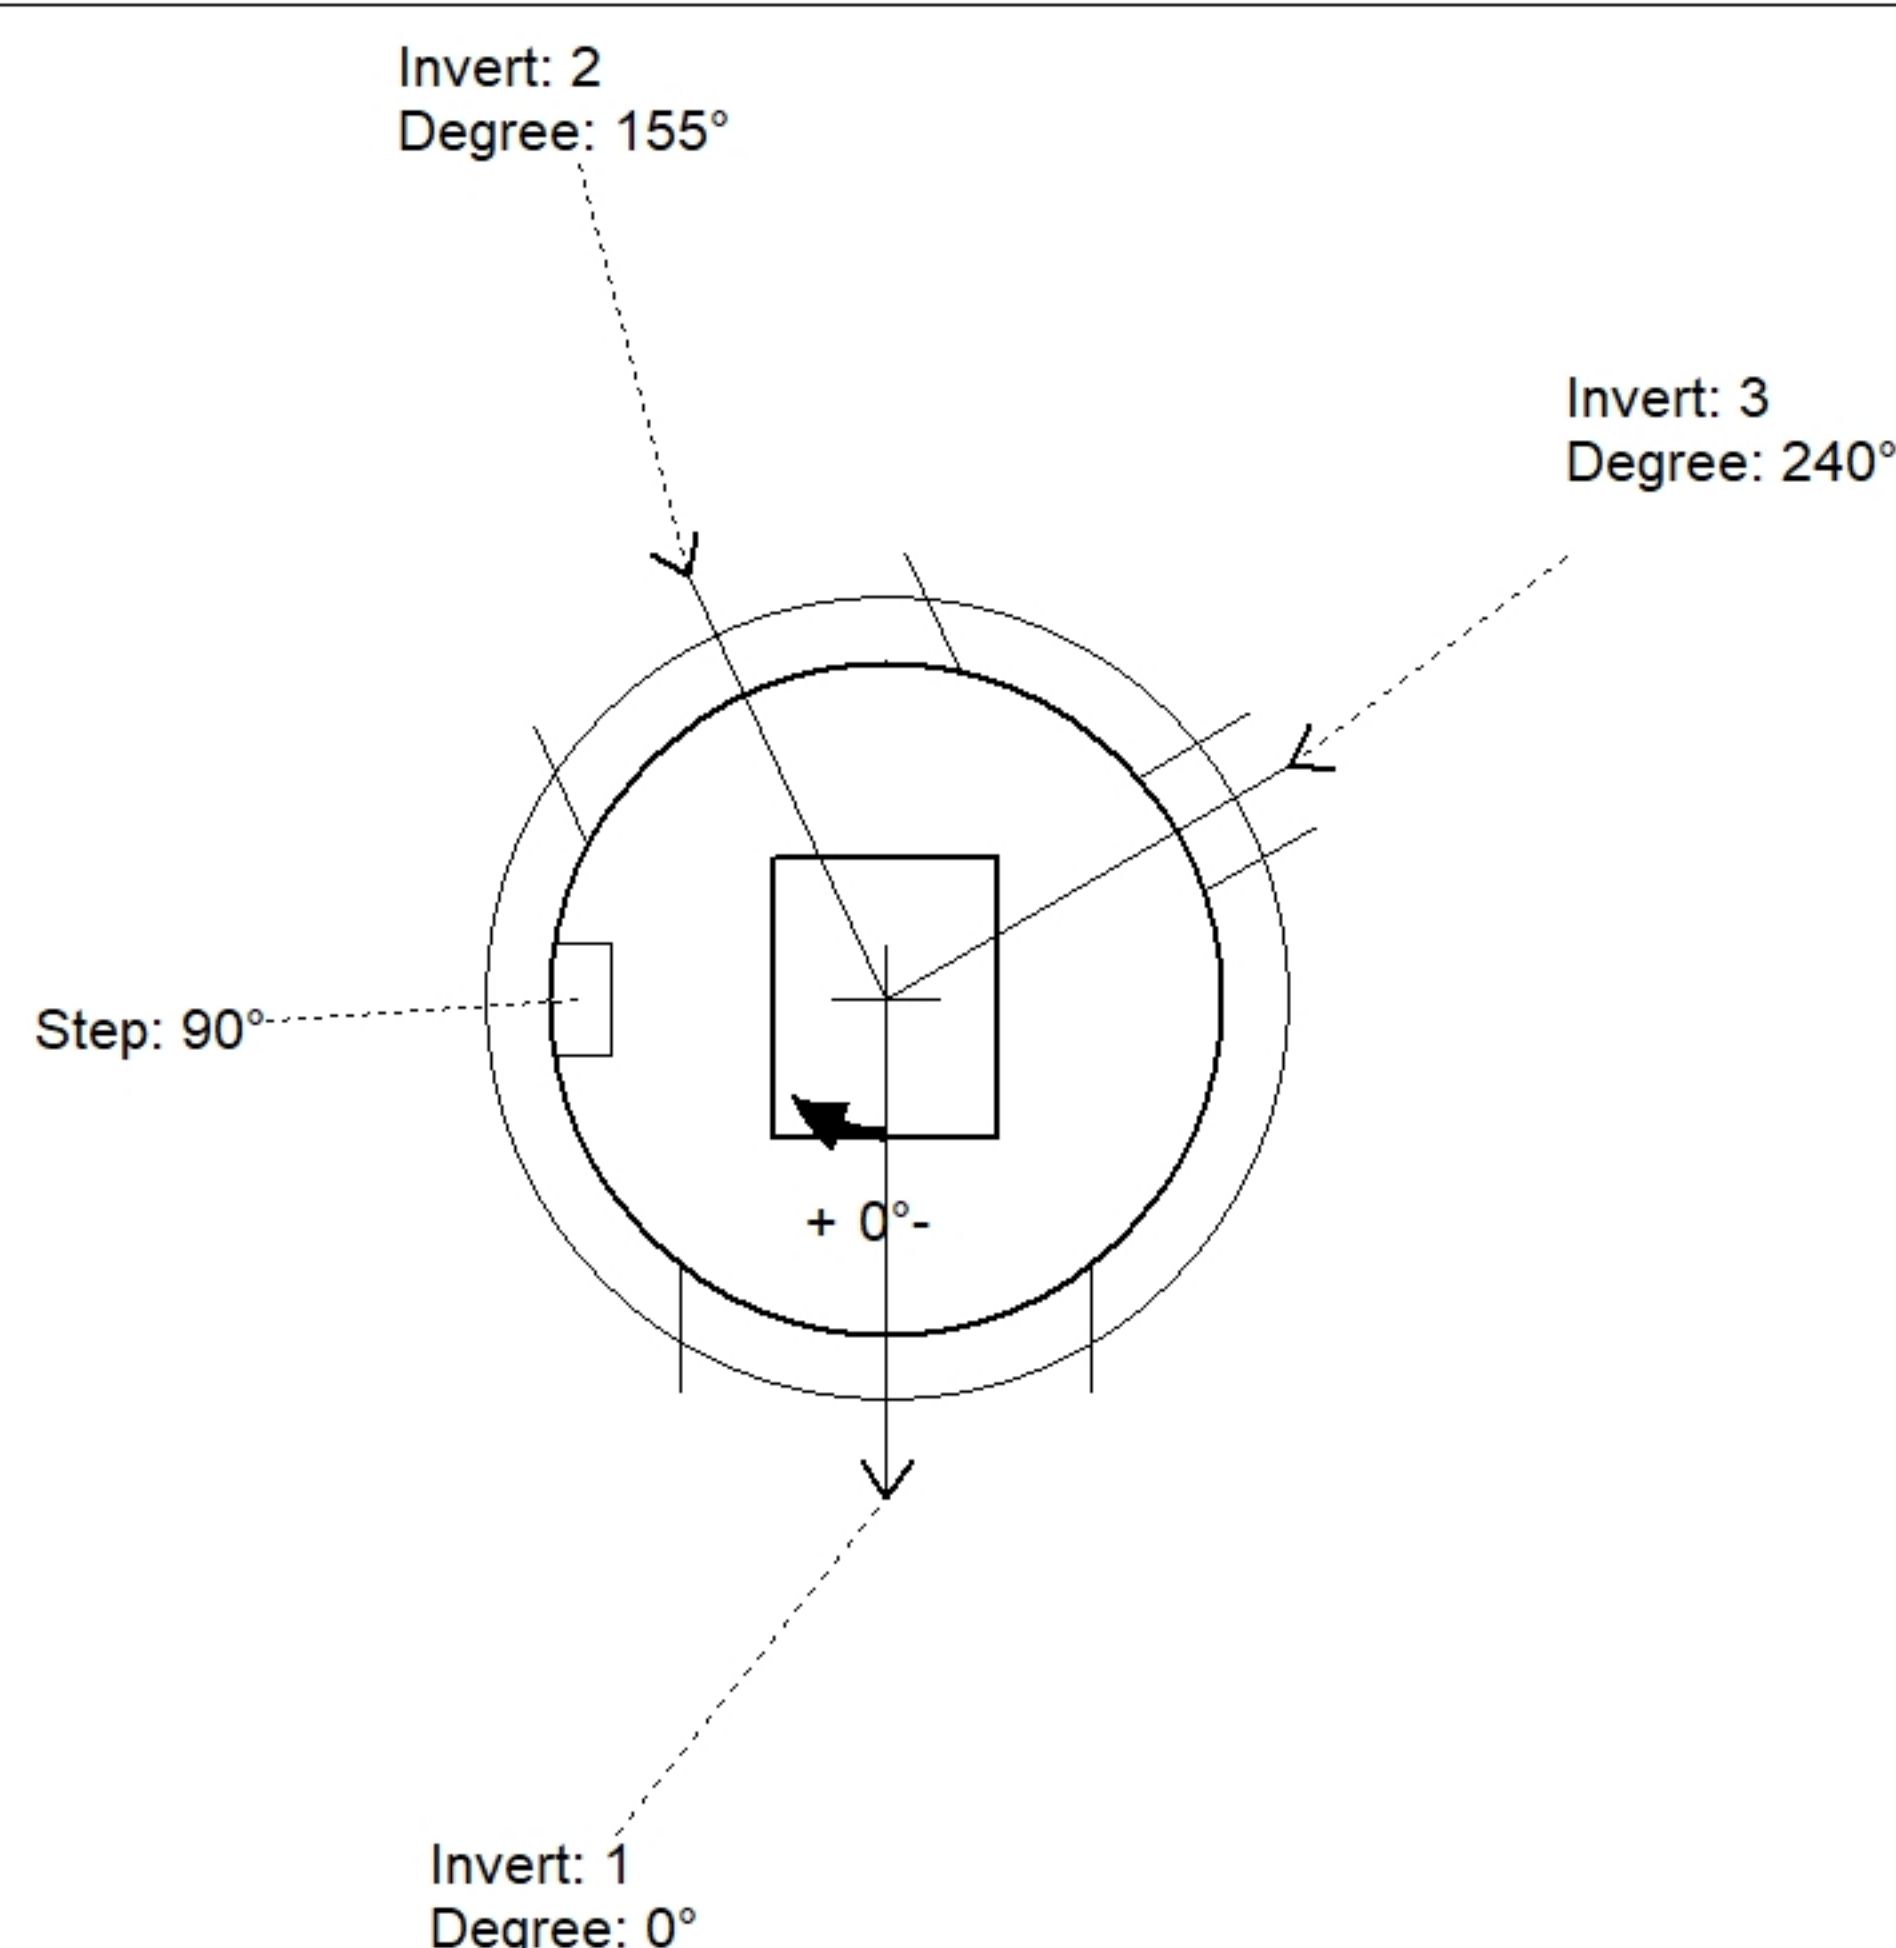

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	586.8'							
Reducer								
Invert 1	579.12'	0°	36" HDPE	41.7"	44"	Hole 44	-2.85"	P1
Invert 2	579.12'	155°	36" HDPE	41.7"	44"	Hole 44	-2.85"	P1
Invert 3	579.12'	240°	10" PVC SDR35	10.5"	14"	Hole 14	-0.25"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

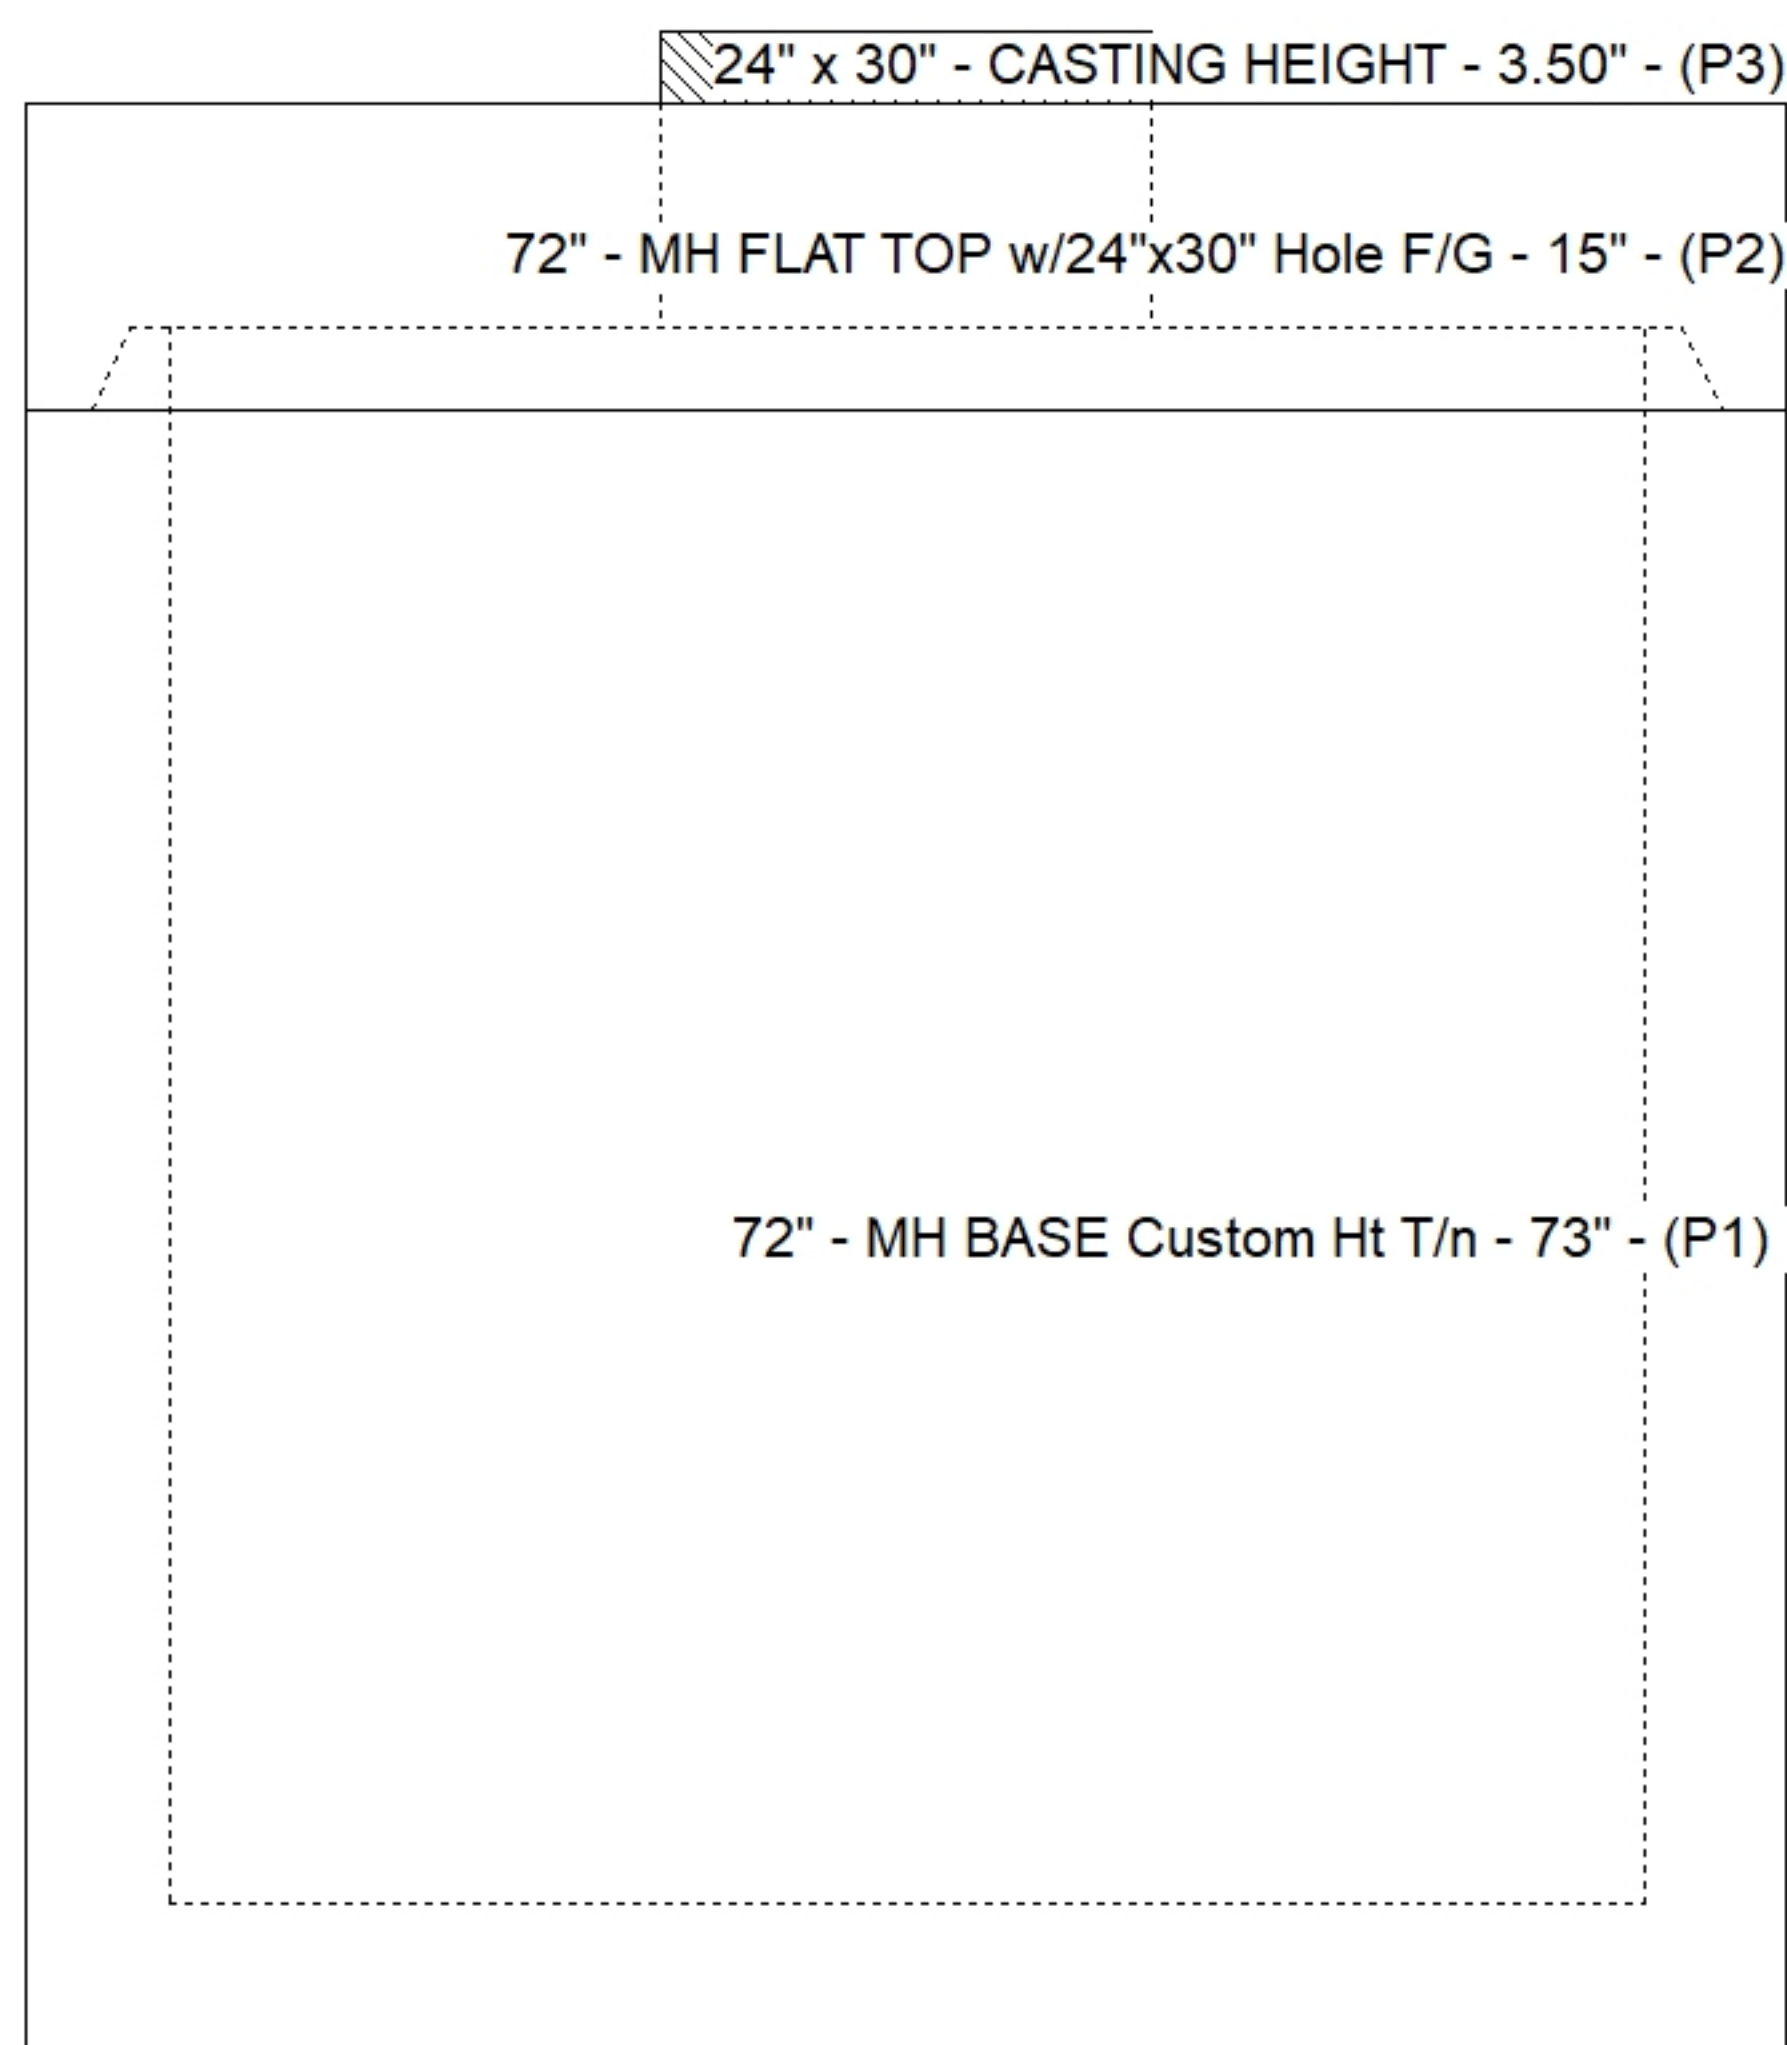

Default - Interior Dimensions

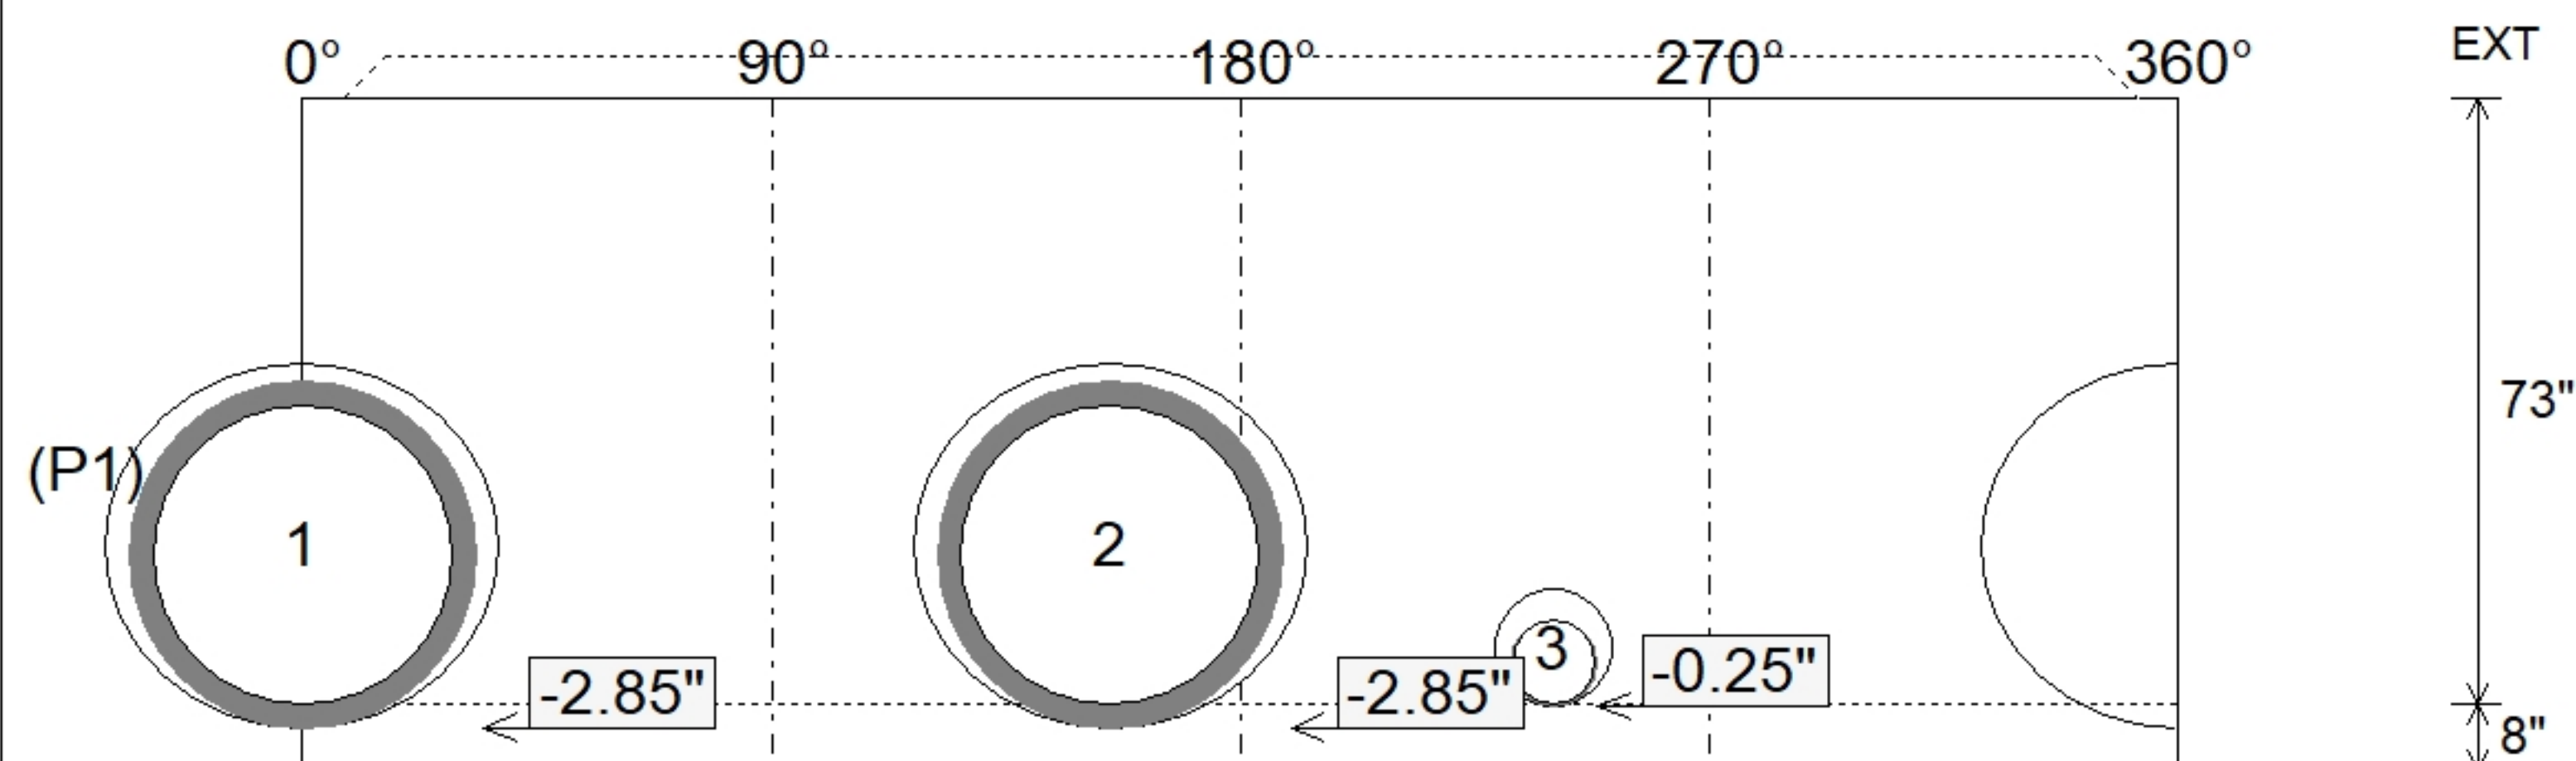

SUBMITTAL
APPROVED BY:
