

Contractor: Mick-Murf Construction Inc.

TECH: Jared - F

Plant: 100



Size: 36" x 36"

Rim to Invert: 2.47'

Floor Height: 8"

Slack: 0.64"

1. PER KYTC DBI TYPE 3 / ASTM C913 SPEC'S.
2. CONCRETE = 4,000 PI AT 28 DAYS.
3. STUB #5 BARS 20" OUT TOP OF WALLS (SPA@12"C/C)
4. CASTING SUPPLIED BY OTHERS (HOE KY-328 SET (DBI 3)).


REINFORCING PER ASTM A615 (GRADE 60).

- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

P2) 36" x 36" - P.I.P. - BY OTHERS - 8"
P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 21"
1) 36" x 36" - Conseal CS-102 1.00"
1) Hole - 18

0 lb
4125 lb
0 lb
0 lb



Structure Total: 4125 lb

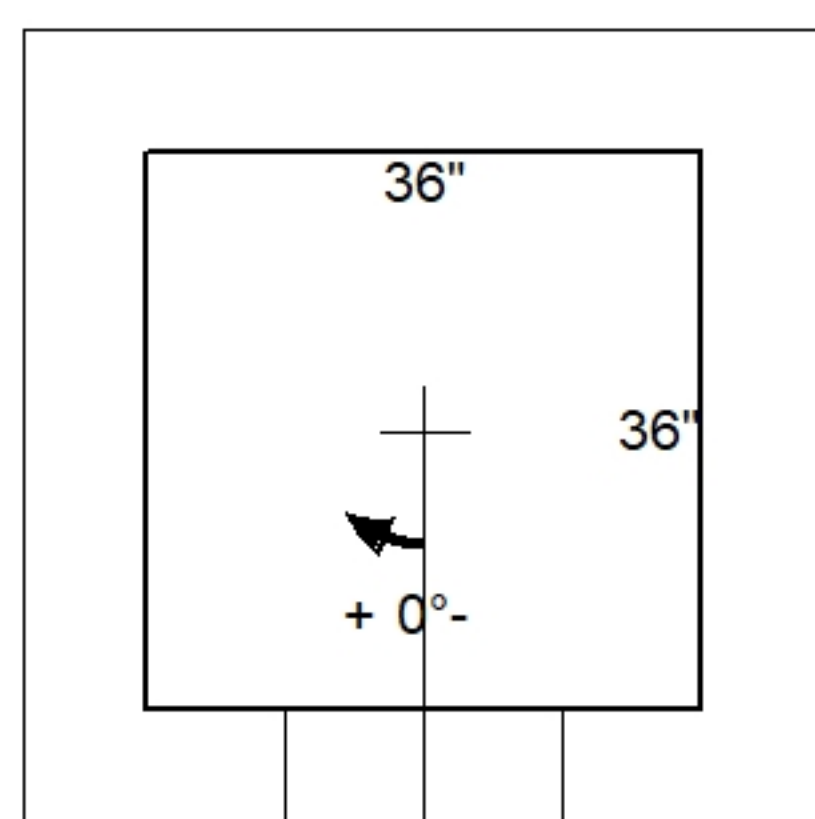

Invert: 1
Degree: 0°

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	530.88'							
Reducer								
Invert 1	528.41'	0°	15" CMP	16"	18"	Hole 18	-1.5"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

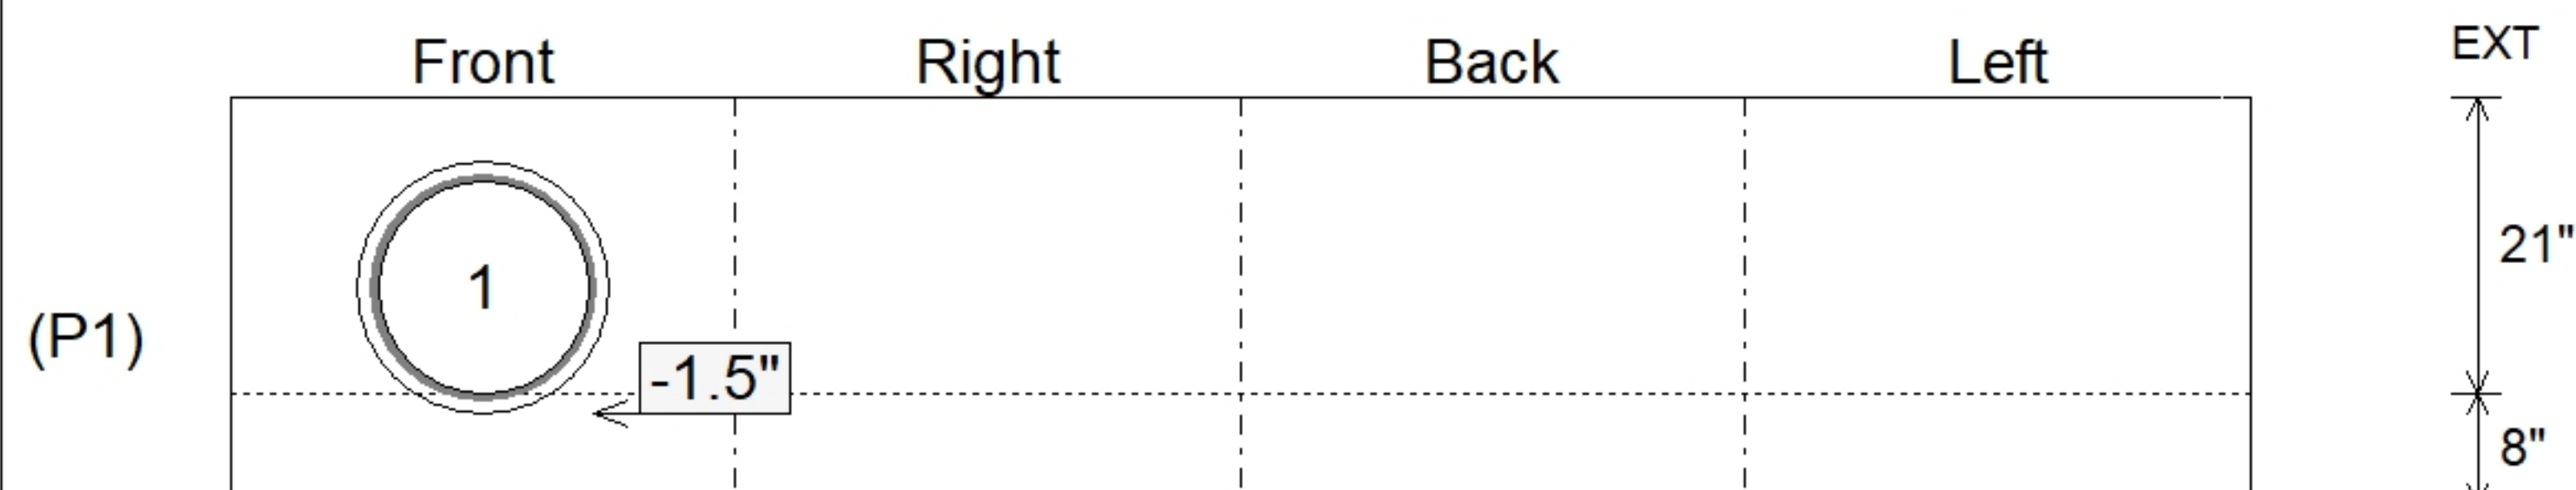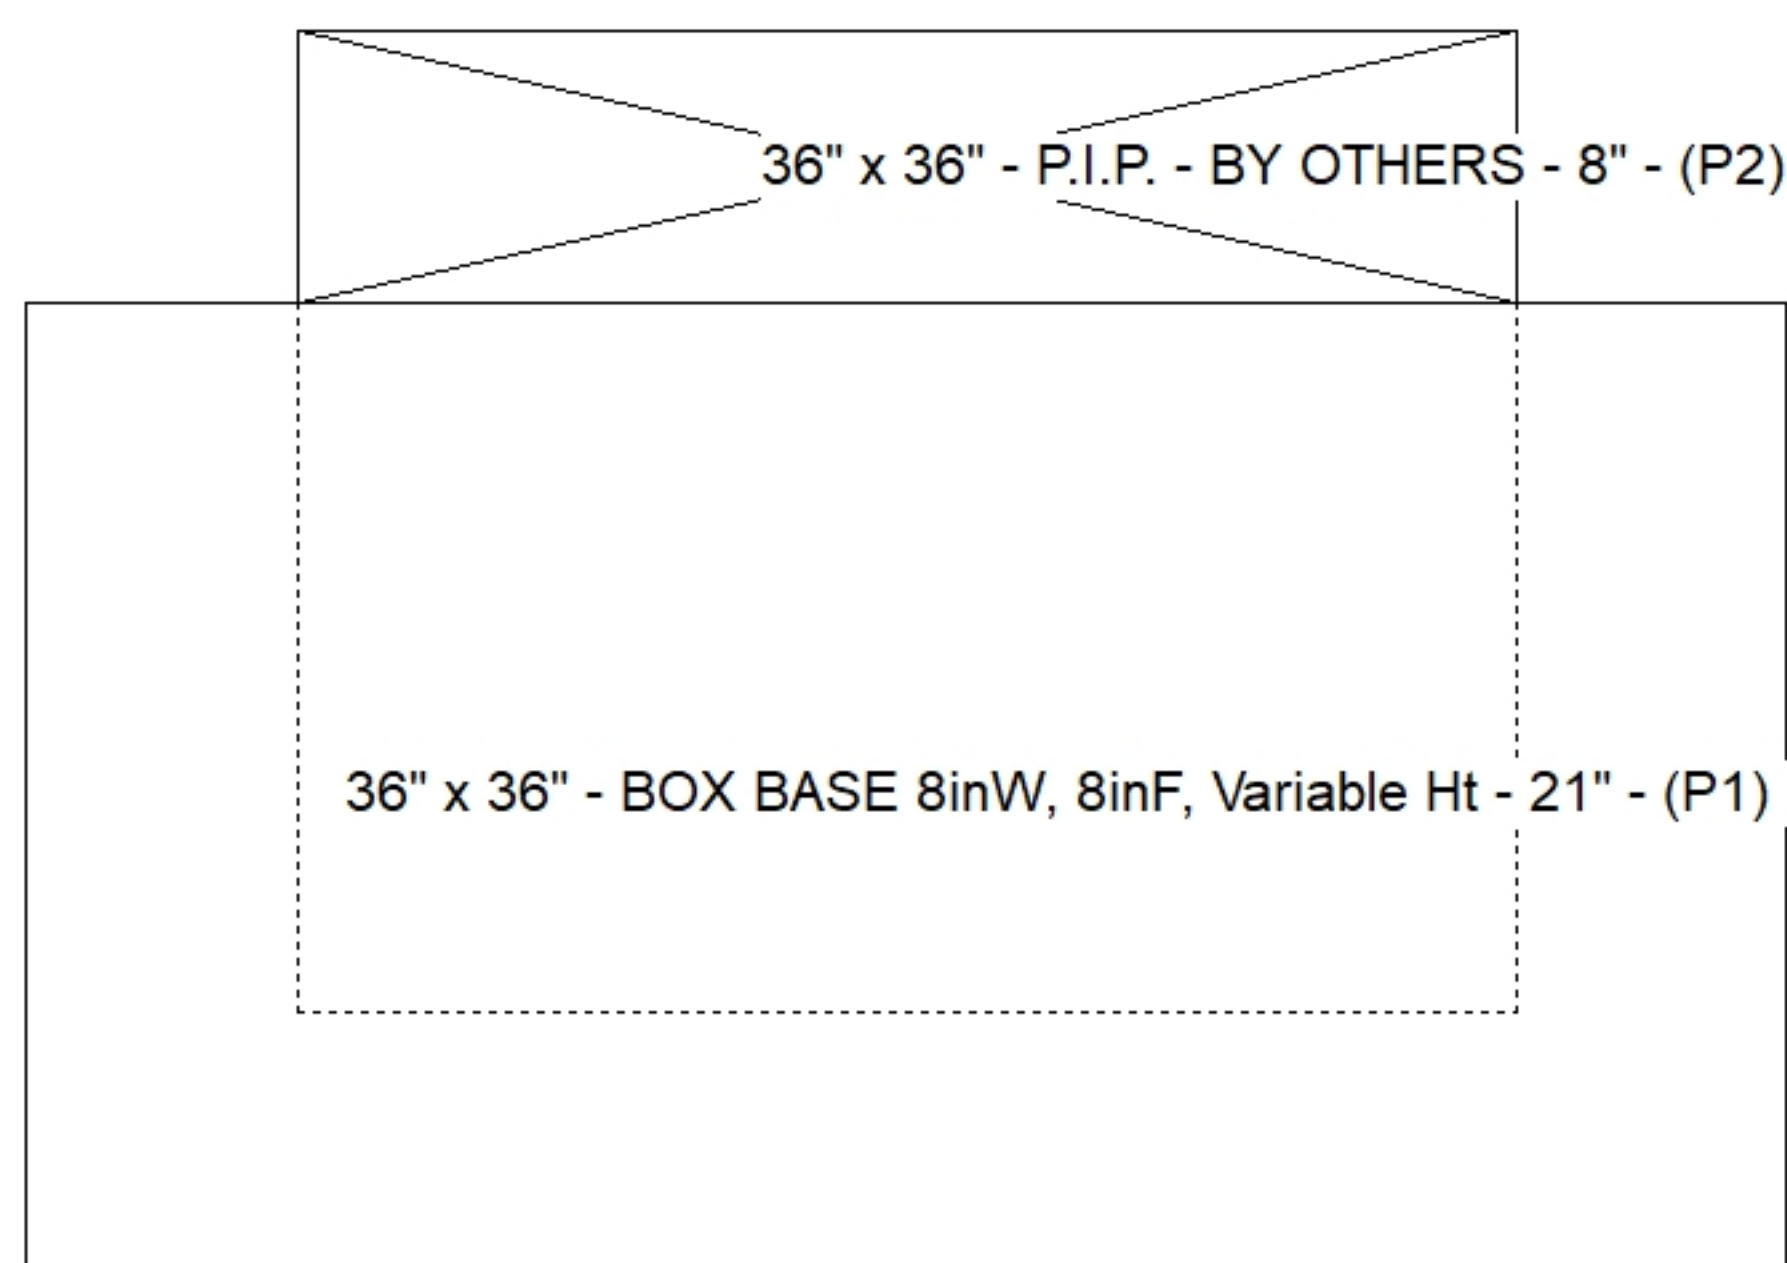

Submittal Drawing
9/8/2026 3:32:58 PM

SUBMITTAL
APPROVED BY:
