

Contractor: Mick-Murf Construction Inc.

TECH: Jared - F

Plant: 100




Slack: 4"

1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY ICAST (HOE KY -206 F/C (KY CBI A))
REINFORCING PER ASTM A615 (GRADE 60).
- TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W.
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

P3) 24" x 120" - CB INLET KY A 10' TOP LEFT - 10"	3400 lb
P2) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT - 18"	5270 lb
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 25"	3776 lb
1) CASTING - HOE KY-206 F/C (KY CBI A)	206 lb
1) 24" x 36" - Conseal CS-102 1.00"	0 lb
1) Hole - 18	0 lb

Structure Total: 12652 lb

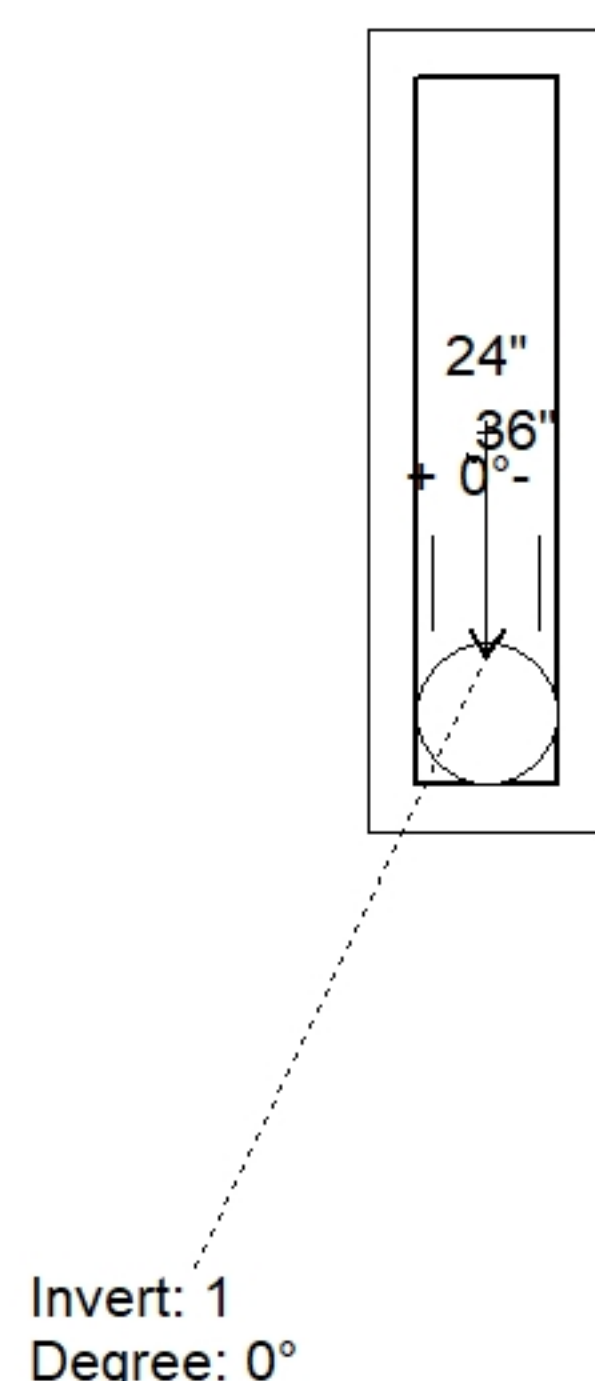


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	536.71'							
Reducer								
Invert 1	531.96'	0°	15" CMP	16"	18"	Hole 18	-1.5"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" x 120" - CB INLET KY A 10' TOP LEFT - 10" - (P3)

24" x 120" - CB INLET KY A 10' BOTTOM LEFT - 18" - (P2)

24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 25" - (P1)

Default - Interior Dimensions

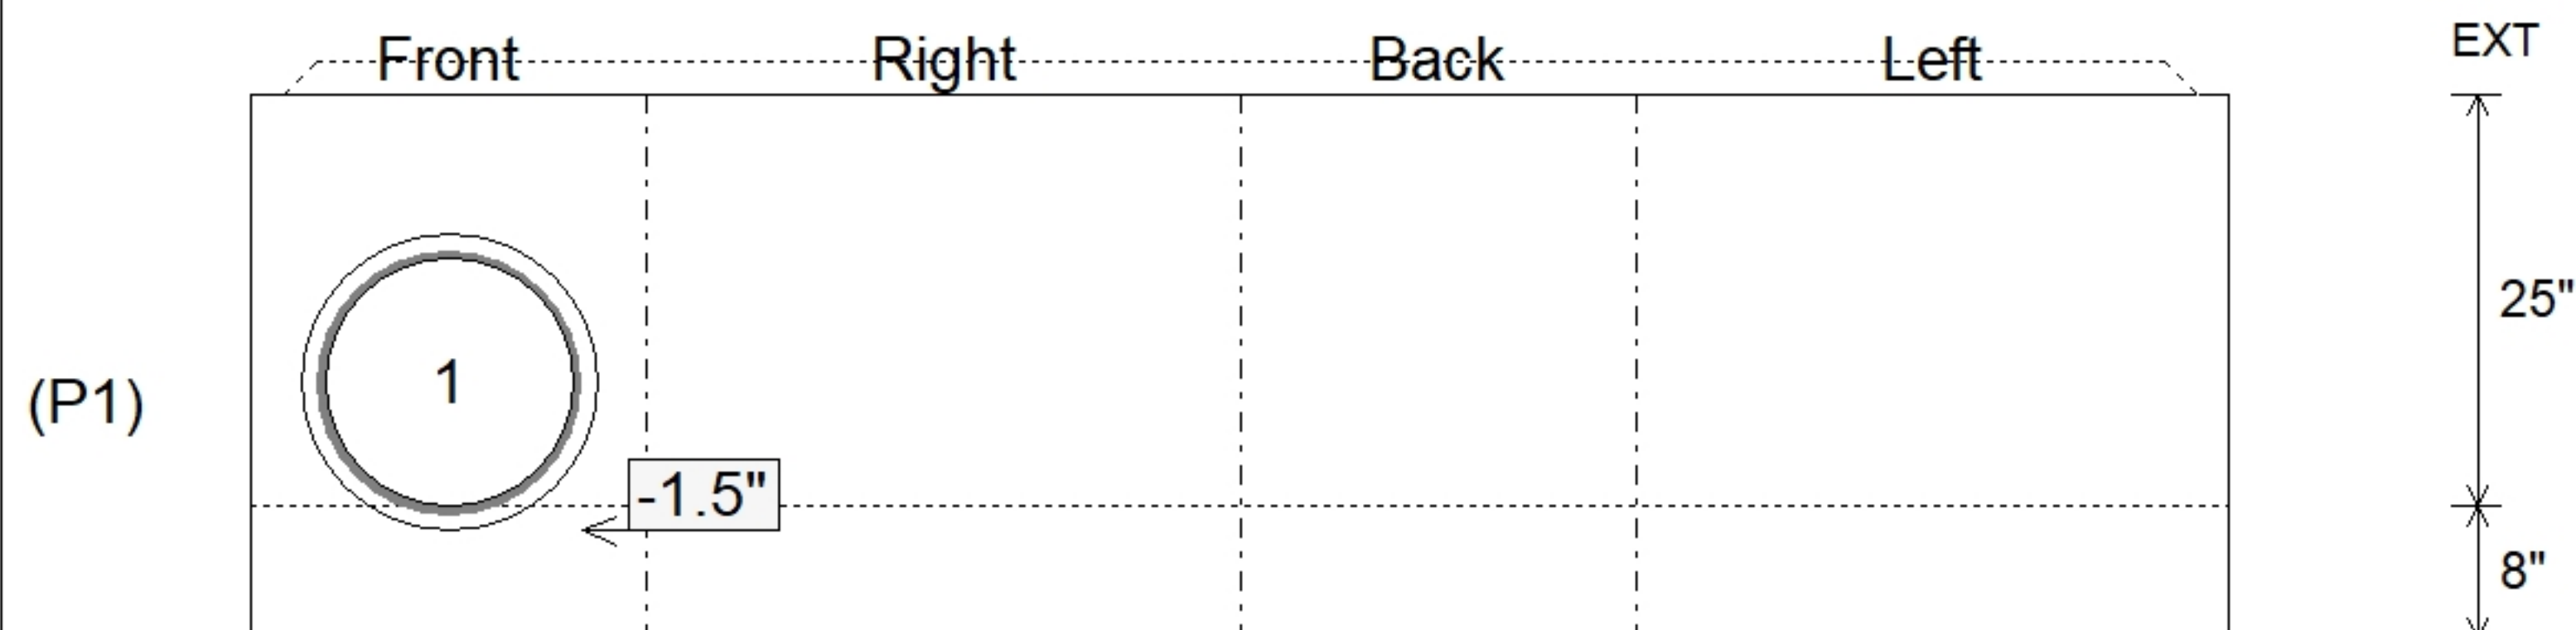

Submittal Drawing
9/8/2026 3:32:55 PM

SUBMITTAL
APPROVED BY:
