

Contractor: Garney Companies, Inc.

Plant: 100




Slack: 0.82"

8. FUTURE RIM ELEVATION - 415.93'


2) A-Lok - 1840

2 lb

Structure Total: 85432 lb

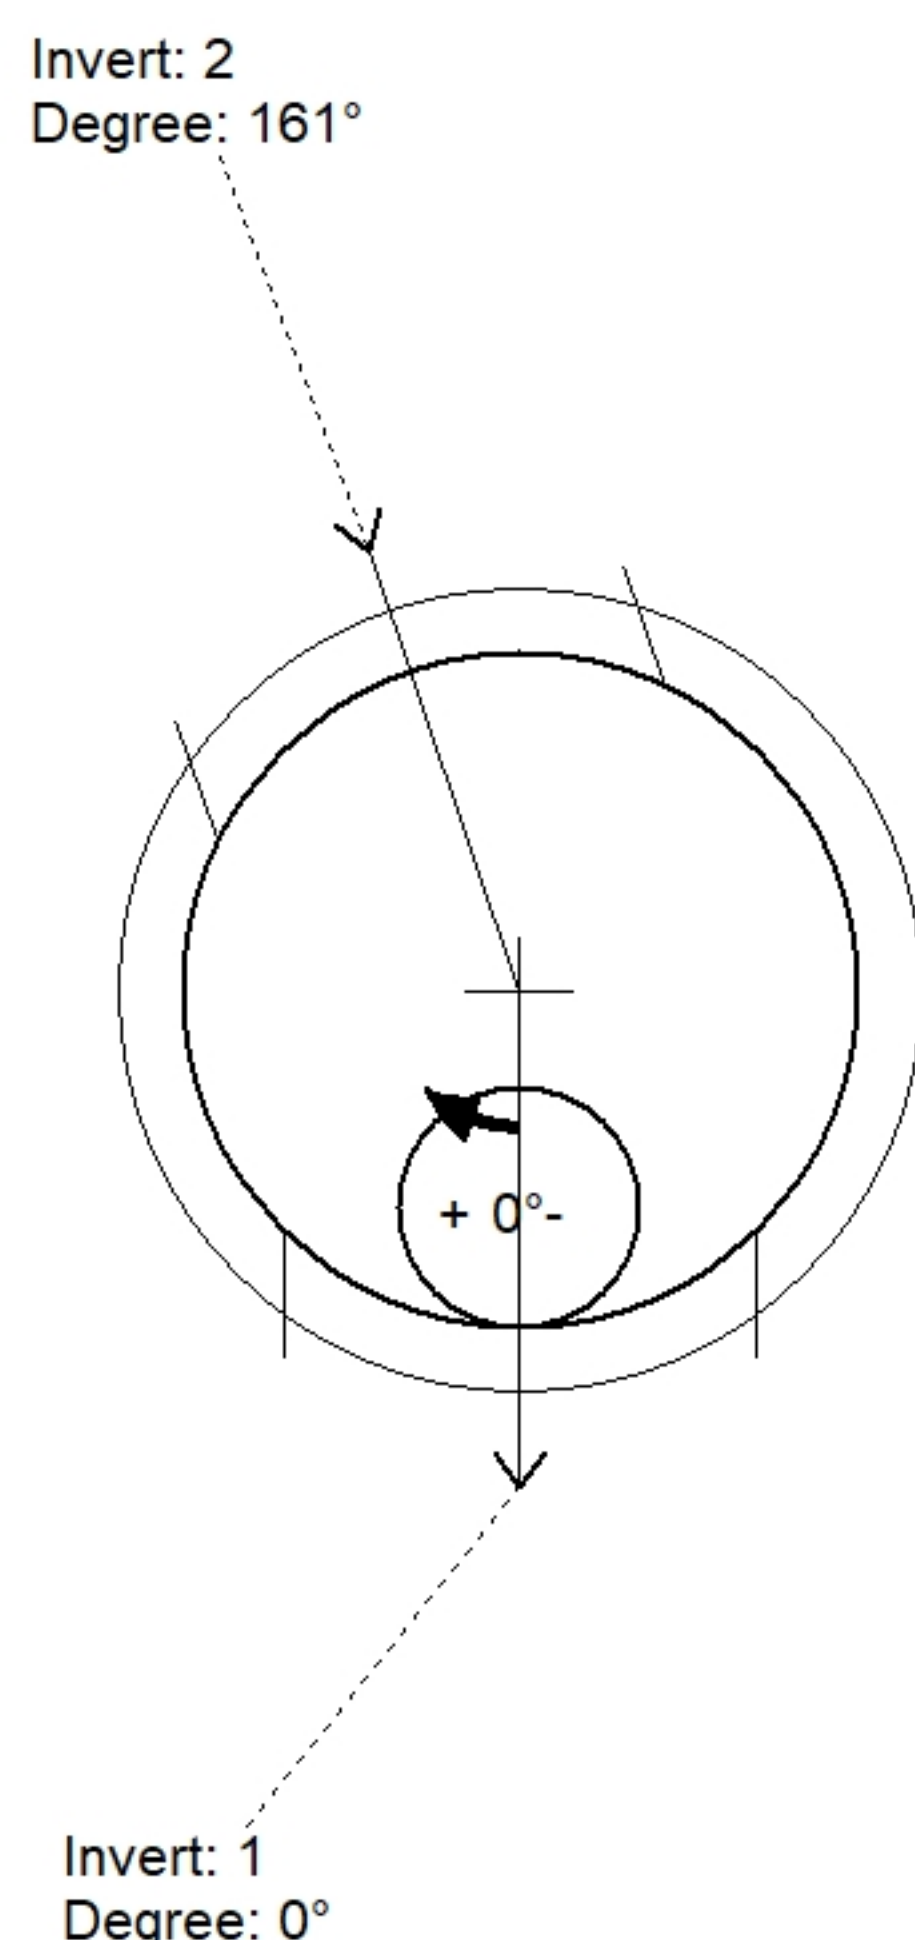

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	414.67'							
Reducer								
Invert 1	383.31'	0°	54" DI	57.5"	59"	A-Lok 1840	0"	P1
Invert 2	383.41'	161°	54" DI	57.5"	59"	A-Lok 1840	1.2"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

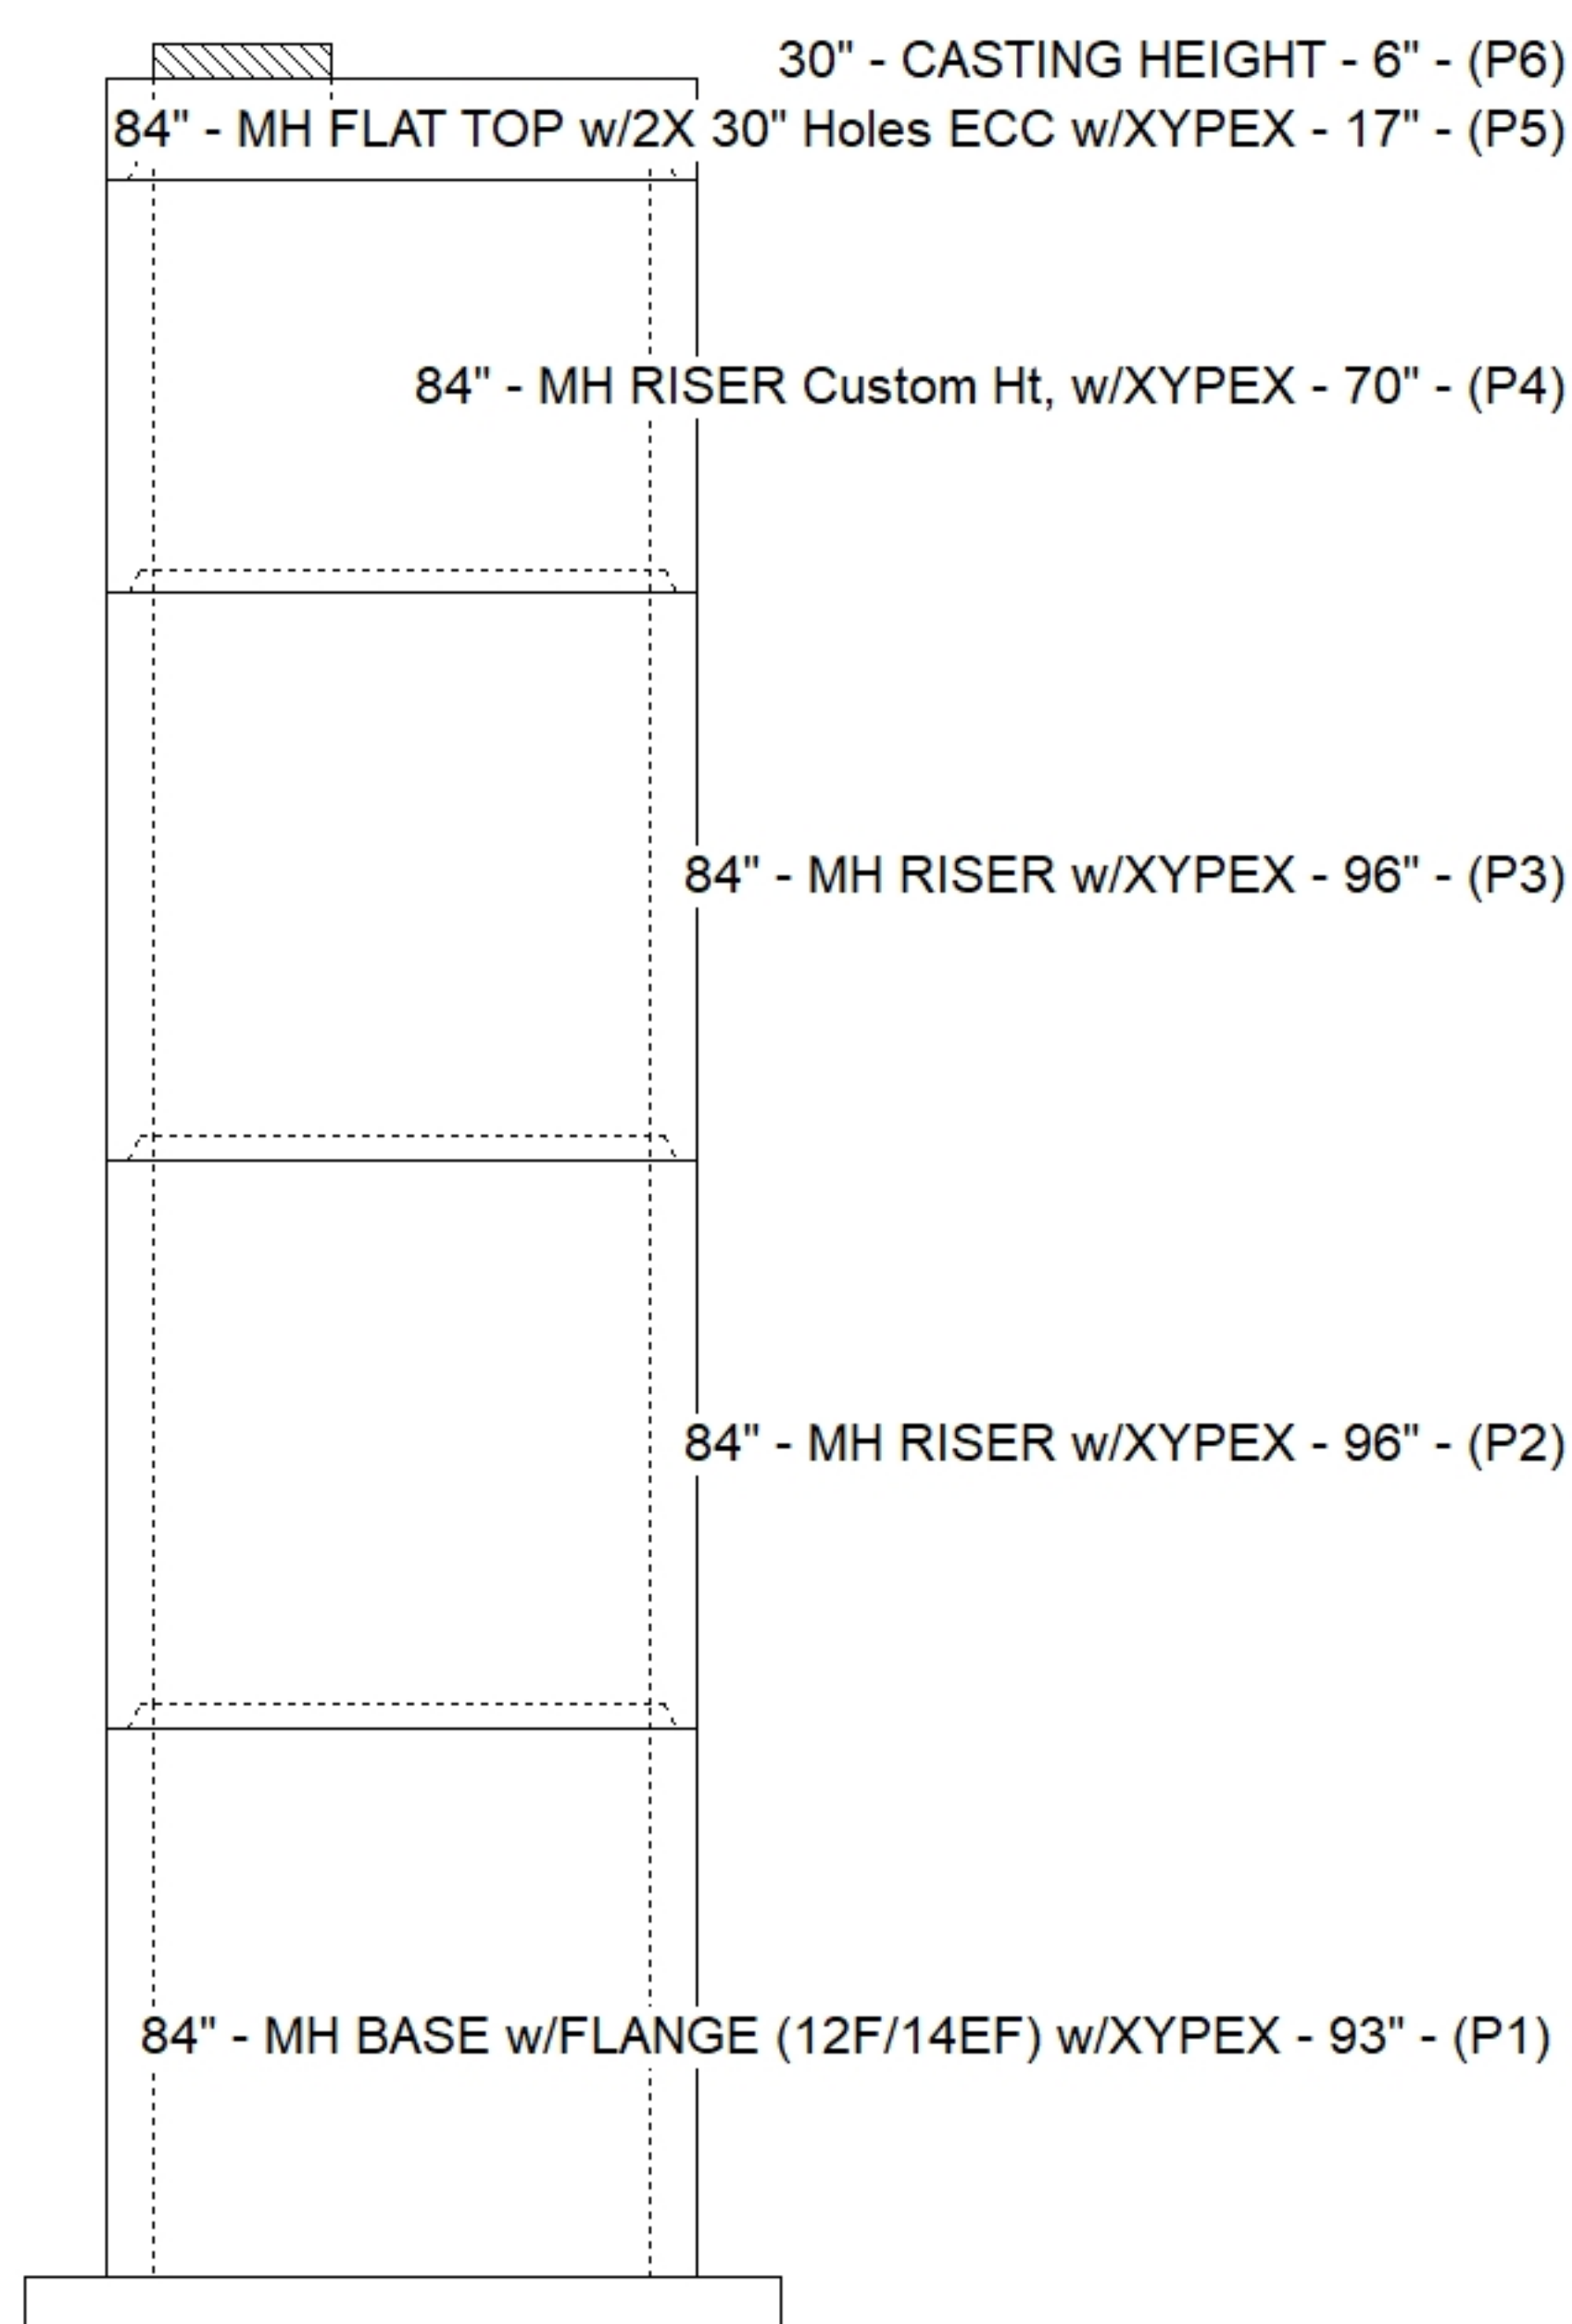

SUBMITTAL
APPROVED BY:
