




Structure ID: HW-03-4 HW

P1 HWPC4368


68" x 43" - PIPE CULVERT HEADWALL (ELL.RCP) F/F

- NOTES:**
1. CONCRETE: 4500 PSI @ 28 DAYS.
 2. REINFORCING: #5 BAR @ 12" C/C E.W.-GRADE 60, (WITH 2" CONCRETE COVER MINIMUM)
 3. REINFORCING BARS TO BE TACK WELDED OR TIED.
 4. DRAWING TO BE USED IN CONJUNCTION WITH KYTC STD. DRAWING RDH-110-02, RDH-210-03 AND THE STANDARD SPECIFICATIONS FOR ROAD AND BRIDGE CONSTRUCTION.
 5. $\frac{3}{8}$ " CHAMFER ON ALL EXPOSED EDGES.
 6. WEIGHT: 16052 LBS.

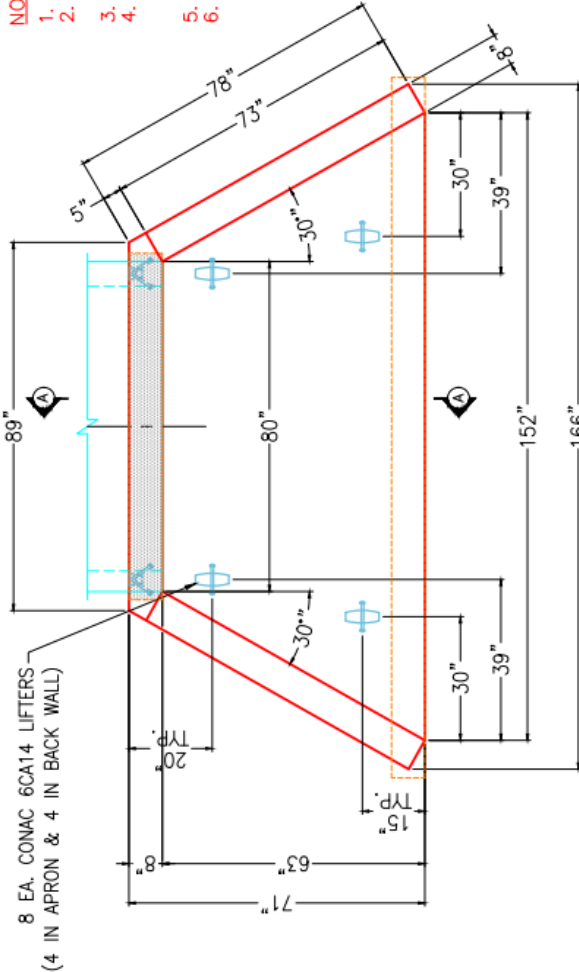


PLAN VIEW


84" WD x 58" HT ELLIPTICAL HOLE
FOR 68"x43" ERCP
RECESSED 6" INTO FLOOR

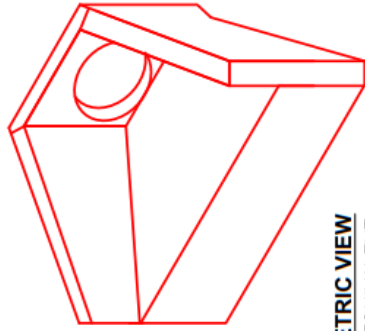

ISOMETRIC VIEW
54"Ø EQUIVALENT
HEADWALL

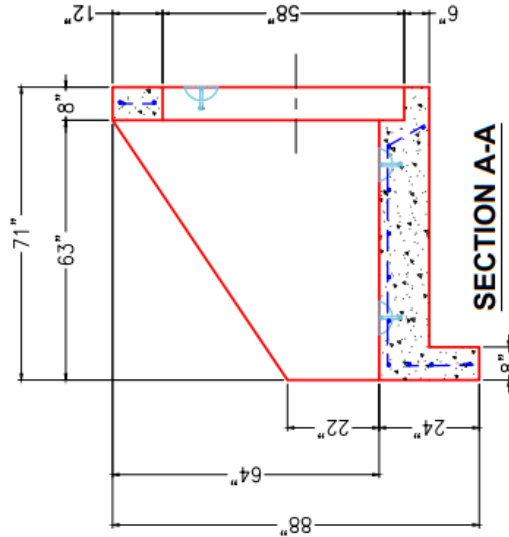

SECTION A-A

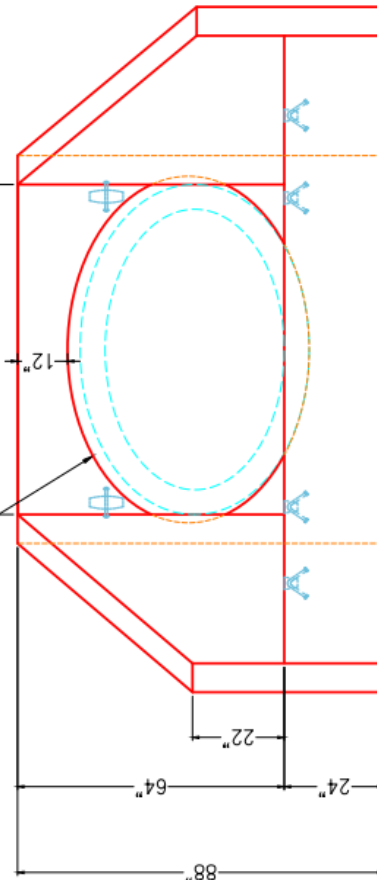

FRONT ELEVATION

PRODUCTION WORK ORDER

- QUALITY CONTROL CHECKLIST
- ☐ ALL DIMENSIONS CORRECT.
 - ☐ LIFTERS INSTALLED.
 - ☐ STEPPED HF CORRECT SIZE.
 - ☐ REINFORCING CORRECT.
 - ☐ HOLE RECESSED CORRECTLY.
 - ☐ EDGES CHAMFERED.
 - ☐ ALL PATCHWORK ACCEPTABLE.



PRODUCT I.D.: HWPC4368

PRODUCT VIEW: RIGHT SIDE UP

PLANT: BEAVER DAM, KY.

WEIGHT: 16,052 LBS.

TOP SECTION JOINT: N/A

BASE SECTION JOINT: N/A

QC CHECK INITIALS:

DESCRIPTION: 54" EQ PC HW

CUSTOMER: WALKER BUILDING GROUP

PROJECT: RHINE DRIVE STORMWATER SYSTEM IMPROVEMENTS

STRUCTURE ID.: HW-03-4 HW

SALES ORDER NO: 26-1609

P.C.: TLEWIS

DRAWING: FMT

DATE: 5/4/26

SCALE: NTS

PG.: 1 of 1
