



Job Name: 26-1822 - Project Versailles Job Location: Versailles, KY Contractor: KY Earthworks					Plant: 100 9/28/2026 2:16:45 PM		Tech: Jared - F PC: E. Bradley			
Structure ID: F4 ST-YD										
P1 MH072BA84					MH BASE T/n					
P4) 24" x 24" - CASTING HEIGHT - 4" P3) 24" x 24" - GRADE RING F/F - 3" P2) 72" - MH FLAT TOP w/24"x24" Hole F/G - 15" P1) 72" - MH BASE T/n - 84" 1) CASTING - HOE 280T F/G 1) 72" - Conseal CS-102 1.00" 2) 24" x 24" - Conseal CS-102 1.00" 1) Hole - 50 1) Hole - 44 1) Hole - 46 7) MH Step ML-10-TDS-NCR - 10"					0 lb 258 lb 4772 lb 12898 lb 182 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 18110 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 280T F/G) REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. (DOUBLE MAT) - RISER/WALLS (As .18) - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.			
Rim: 934.52' Rim to Invert: 8.67' Slack: 1.68' Sump: 3.64' Step Position: 90°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	925.85'	0°	0"	42" HDPE	47.7"	Hole 50	50"	55.271"	0.5"	0"
Invert 2	925.85'	156°	117.125"	36" HDPE	41.7"	Hole 44	44"	47.337"	0.75"	0"
Invert 3	925.88'	265°	198.875"	36" RCP B WALL	44"	Hole 46	46"	49.9"	0"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

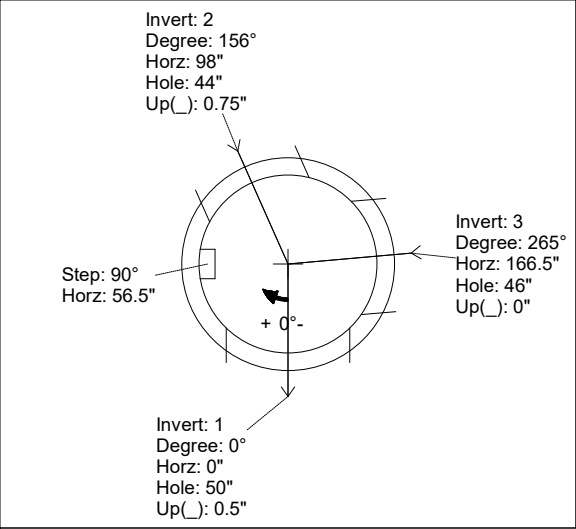

UPSIDE-DOWN VIEW (int. dimensions)

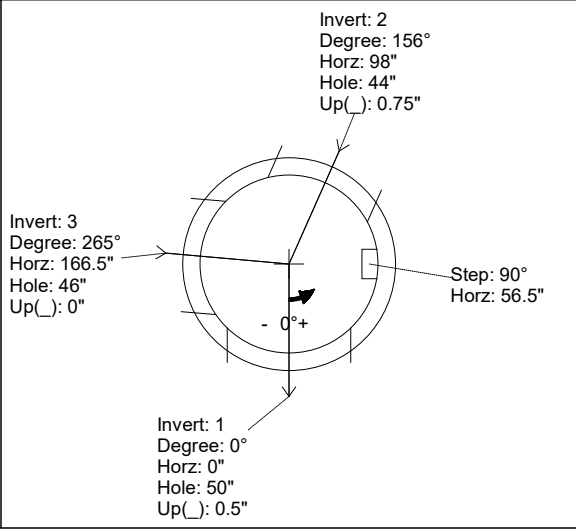

INSIDE WALL DIMENSIONS

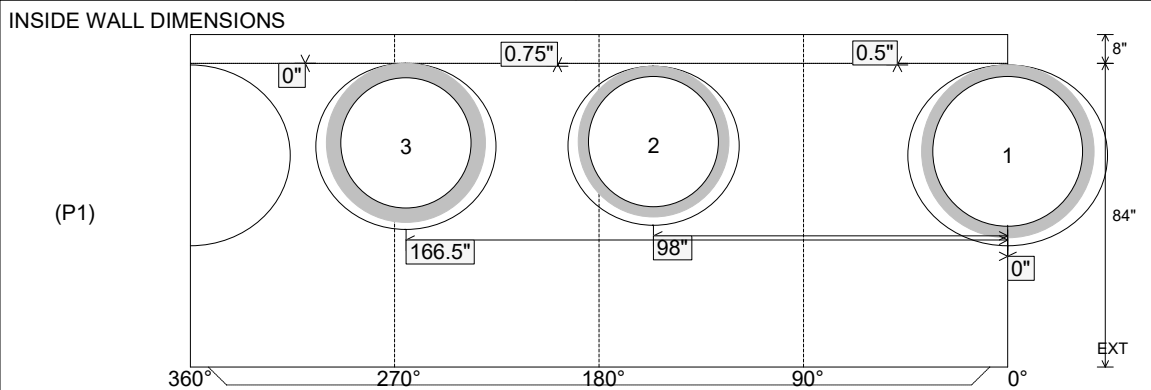

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 7" Floor Height: 8"	Height (Int): 84" Height (Ext): 92"	Weight (Net): 12898 lb Volume (Net): 3.3cu.yd
----------------------------------	---------------------------------	--	--	--
