



Job Name: 26-2025 - KYTC Warren Co (261510) Job Location: Bowling Green, KY Contractor: Mick-Murf Construction Inc.				Plant: 100 8/25/2026 12:58:57 PM		Tech: Jared - F PC: T. Lewis					
Structure ID: DB2 DBI3											
P1 BX3636-08BAVF				BOX BASE 8inW, 8inF, Variable Ht F/n							
P2) 36" x 36" - P.I.P. - BY OTHERS - 8" P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 27" 1) CASTING - HOE KY-328 SET (DBI 3) 1) 36" x 36" - Conseal CS-102 1.00" 1) Hole - 18"				0 lb 4834 lb 328 lb 0 lb 0 lb ----- Structure Total: 5162 lb		Structure Notes: **KYTC STATE PROJECT** 1. KYTC DBI TYPE 3 / ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. STUB #5 BARS 20" OUT TOP OF WALLS (SPA@12"C/C) 4. CASTING BY ICAST (HOE KY-328 SET (DBI 3)) REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W					
Rim: 566'				Rim to Invert: 3'		Slack: 1"		Sump: 0"		Step Position:	
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	563'	0°	26"	15" CMP	16"	Hole 18	18"	18"	-1.5"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


#5 DOWELS @ 12" O.C.
STUBBED 20" OUT THE
TOP OF THE WALLS

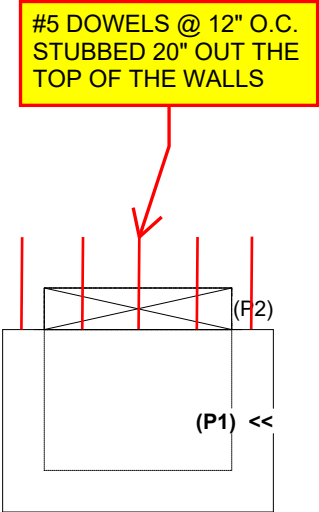


RIGHT-SIDE UP VIEW (int. dimensions)

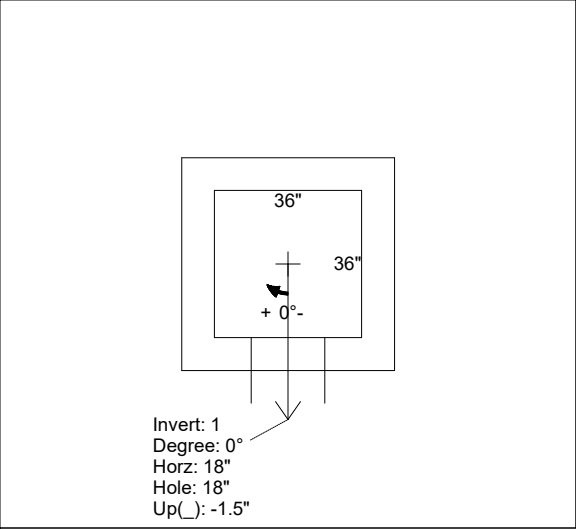

UPSIDE-DOWN VIEW (int. dimensions)

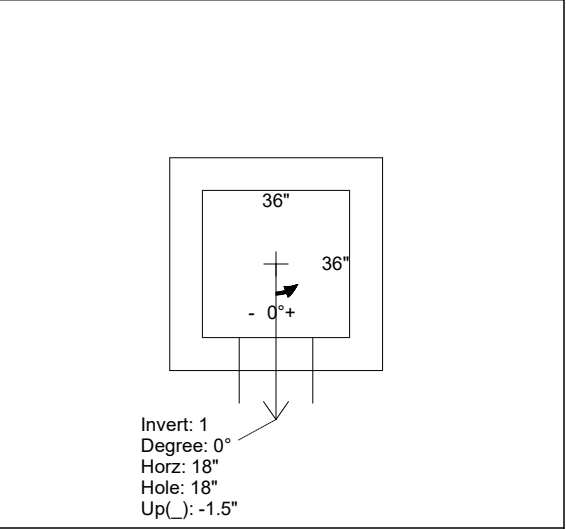

INSIDE WALL DIMENSIONS

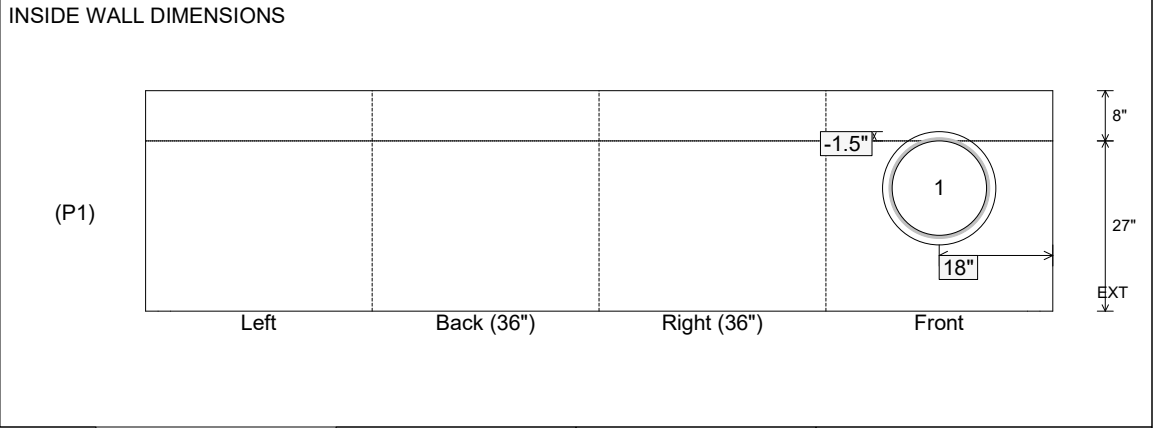

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 27" Height (Ext): 35"	Weight (Net): 4834 lb Volume (Net): 1.24cu.yd
----------------------------------	-------------------------------	--	--	--
