

Job Name: 26-2030 - KYTC McCracken Co. Call 111 (ID 264505)
Job Location: Paducah, KY
Contractor: Jim Smith Contracting Co, LLC

Plant: 100

6/12/2026 7:53:30 AM

Tech: J. Horsley

PC: J. Jarvis



Structure ID: 151+99 S-7 ST-JB

P2 BX048084-08LD08S

BX FLAT LID 8inW SOLID F/F

- P2) 48" x 84" - BX FLAT LID 8inW SOLID F/F - 8"
P1) 48" x 84" - BOX RISER 8inW, Variable Ht FTB F/F - 94"
1) CASTING - HOE KY-345 SET (CBI B)
1) 48" x 84" - Conseal CS-102 1.00"
2) DOGHOUSE - 70"x70"
1) Hole - 22
1) Hole - 26

4296 lb
12382 lb
290 lb
0 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 16968 lb

Structure Notes:



- ** KYTC STATE PROJECT **
1. KYTC JUNCTION BOX / PER ASTM C913 SPEC'S.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. SOLID TOP SLAB - NO CASTING.

REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As. 62) #5 BARS AT 6" C.C.E.W.
- WALLS (As. 31) #5 BARS AT 12" C.C.E.W.

ADDITIONAL COMMENTS:

1. CONTRACTOR TO FIELD CORE HOLE FOR 4" PERF PIPE.
2. LEAVE 1 HORIZONTAL BAR ACROSS THE BOTTOM & STYROFOAM IN THE DOGHOUSE CUTS FOR SHIPPING & HANDLING.

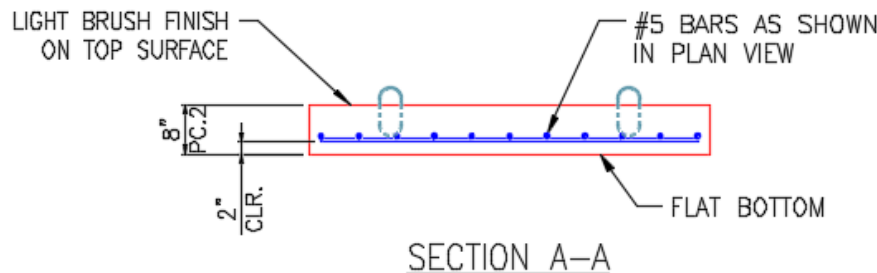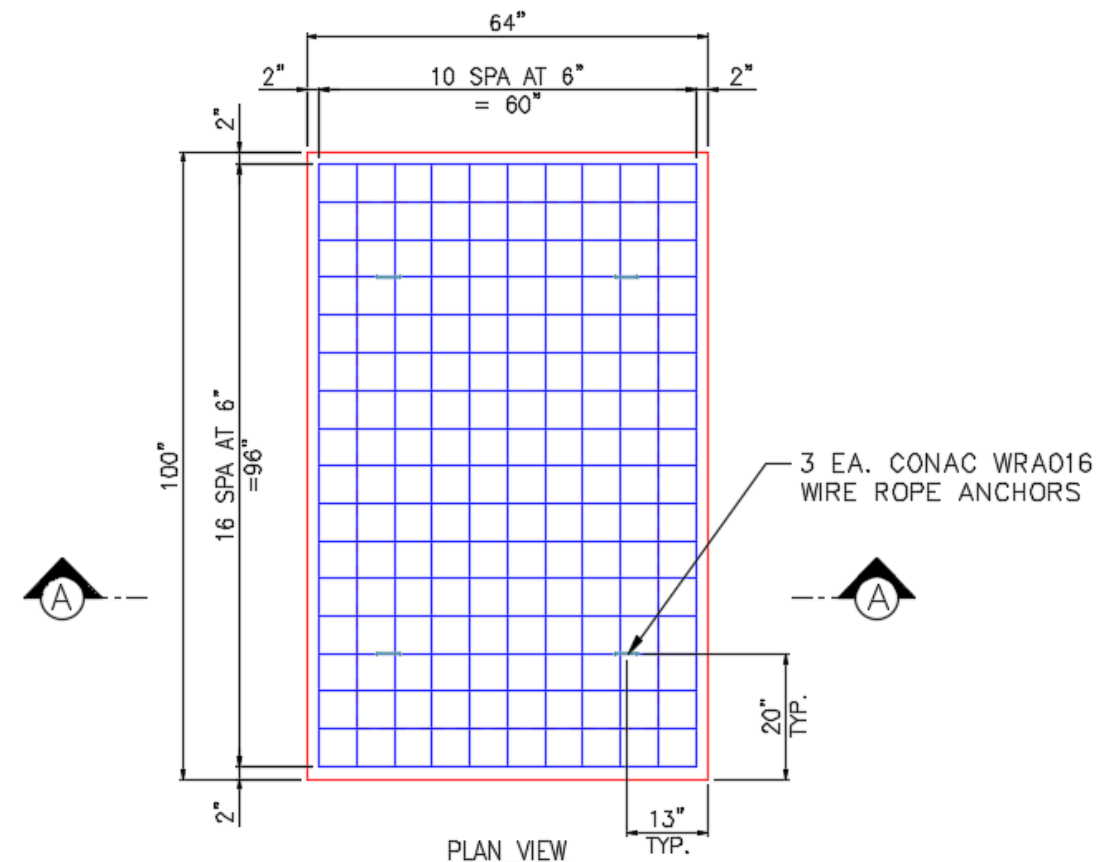

#5 BAR CUT LIST
11 EA. @ 96"
17 EA. @ 60"

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 4296 lb
Volume (Net): 1.1cu.yd
