

Job Name: 26-2217 Kroger COB
Job Location: Bowling Green, KY
Contractor: Stewart Richey

Plant: Beaver Dam

7/28/2026 9:26:14 AM

Tech: J. Coppage

PC: T. Lewis



Structure ID: QL5 MMV


P2 BX072090-06LD08S

BX FLAT LID 6"W w/24"x24" HATCH

- P3) 24" x 24" - HATCH (CAST FLUSH) - 3"
P2) 72" x 90" - BX FLAT LID 6"W w/24"x24" HATCH - 8"
P1) 72" x 90" - BOX BASE 6inW, 8inF, Variable Ht - 96"
1) This Structure Includes a Cast-in Item - 24" x 24" Hatch
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) SECONDARY POUR - WALLS
1) HATCH (Alum.) - USF FAB. THS 24"x24"
2) PSX - 12M NYLO
7) MH Step ML-10-TDS-NCR - 10"



Structure Total:

100 lb	Structure Notes:
5365 lb	1. USF THS 24" X 24" HATCH BY ICAST.
22458 lb	2. HATCH TO BE CAST INTO THE TOP SLAB.
0 lb	3. PER ASTM C913 SPECIFICATIONS.
0 lb	4. CONCRETE = 4,000 PSI AT 28 DAYS.
0 lb	5. REINFORCING PER ASTM A615 (GRADE 60).
0 lb	- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
266 lb	- WALLS (As .31) #5 BARS AT 8" C.C.E.W.
16 lb	- FLOOR (As .31) #5 BARS AT 8" C.C.E.W.
0 lb	
28205 lb	

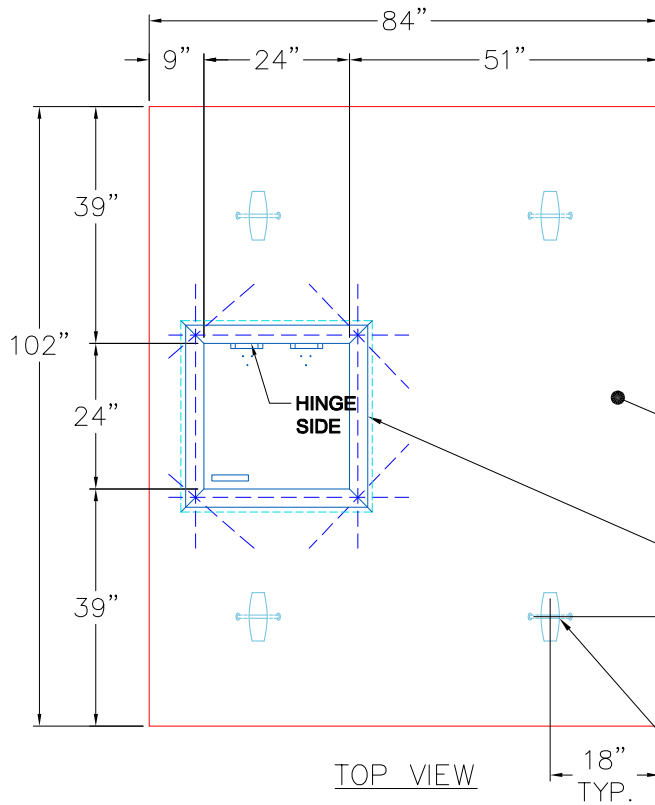

GENERAL NOTES:

1. MANUFACTURED TO ASTM C-913 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" C.C.E.W. (GRADE 60).
4. USF THS 24" X 24" HATCH BY ICAST.
5. HATCH TO BE CAST IN TOP SLAB.

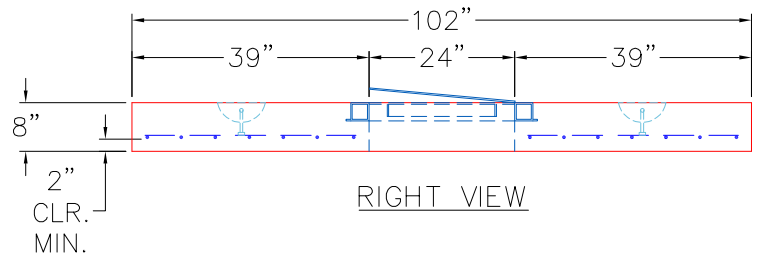

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 6"

Height (Ext): 8"

Weight (Net): 5365 lb
Volume (Net): 1.37cu.yd
