

Contractor: R.A. Alexander & Sons, Inc.

Plant: 100




Slack: 1.06"

1. HOE MC-375 F/C STORM PROVIDED BY ICAST.
2. PER ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60).
 - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
 - RISER/WALLS (As .12)
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


P3) 24" - CASTING HEIGHT - 7"
P2) 48" - MH FLAT TOP w/ 24" ECC Hole - 12"
P1) 48" - MH BASE - 30"
1) CASTING - HOE MC-375 F/C Storm
1) 48" - Conseal CS-102 1.00"
1) 24" - Conseal CS-102 1.00"
2) Hole - 22

0 lb
1561 lb
3097 lb
271 lb
0 lb
0 lb
0 lb

Structure Total: 4929 lb




Invert: 1
Degree: 0°

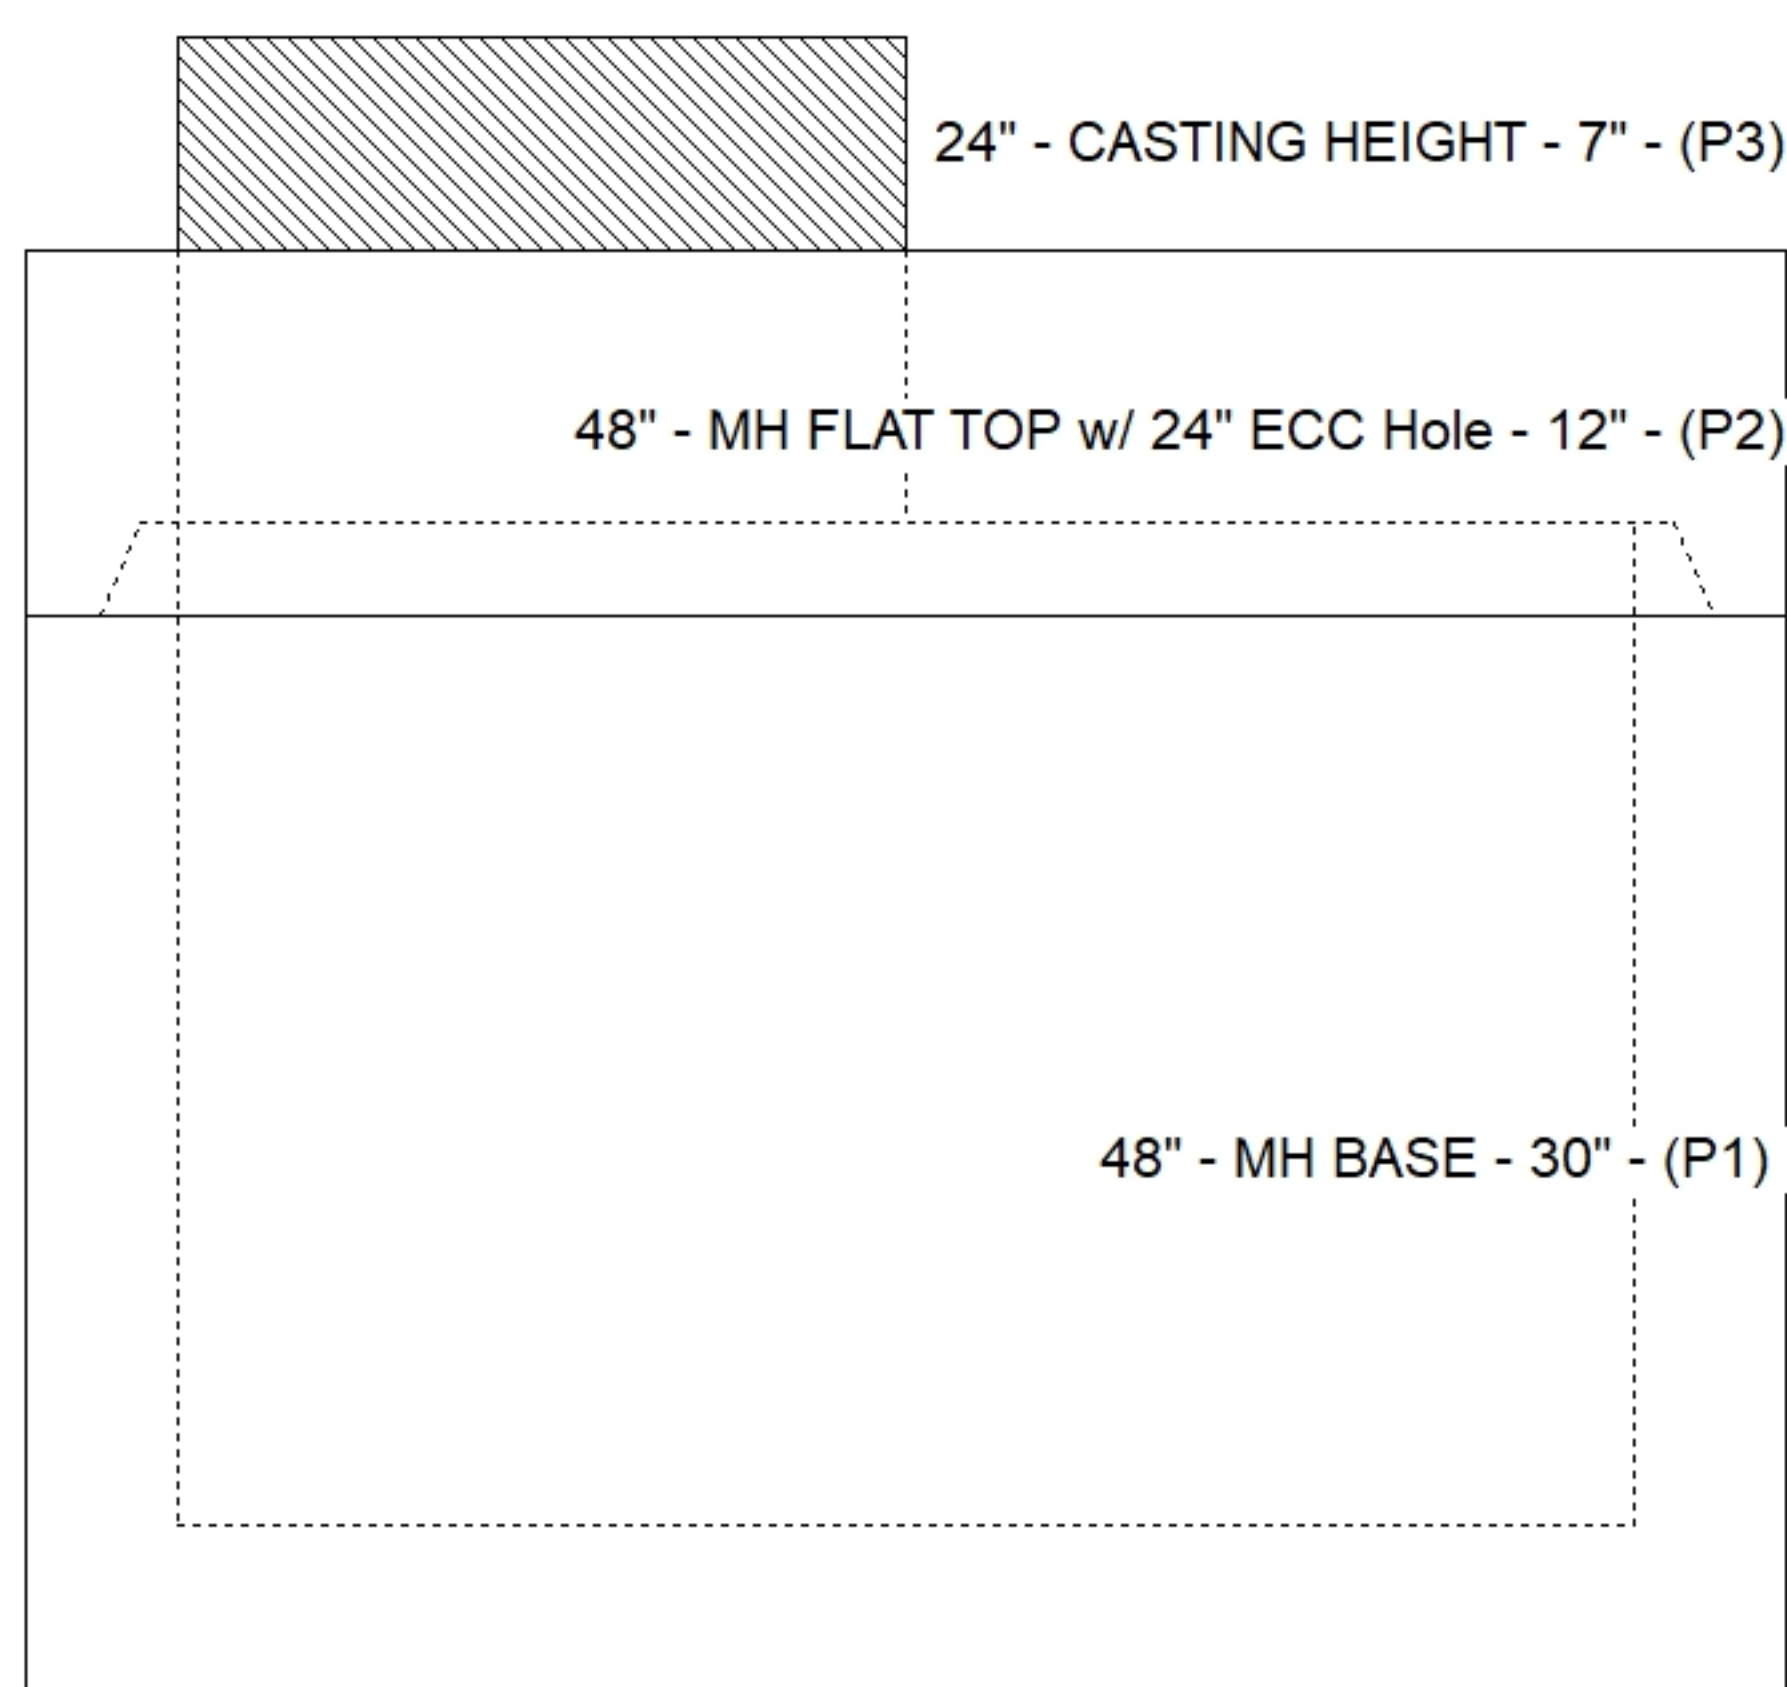

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	560.59'							
Reducer								
Invert 1	556.46'	0°	18" CMP	19"	22"	Hole 22	0"	P1
Invert 2	556.46'	267°	18" CMP	19"	22"	Hole 22	0"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

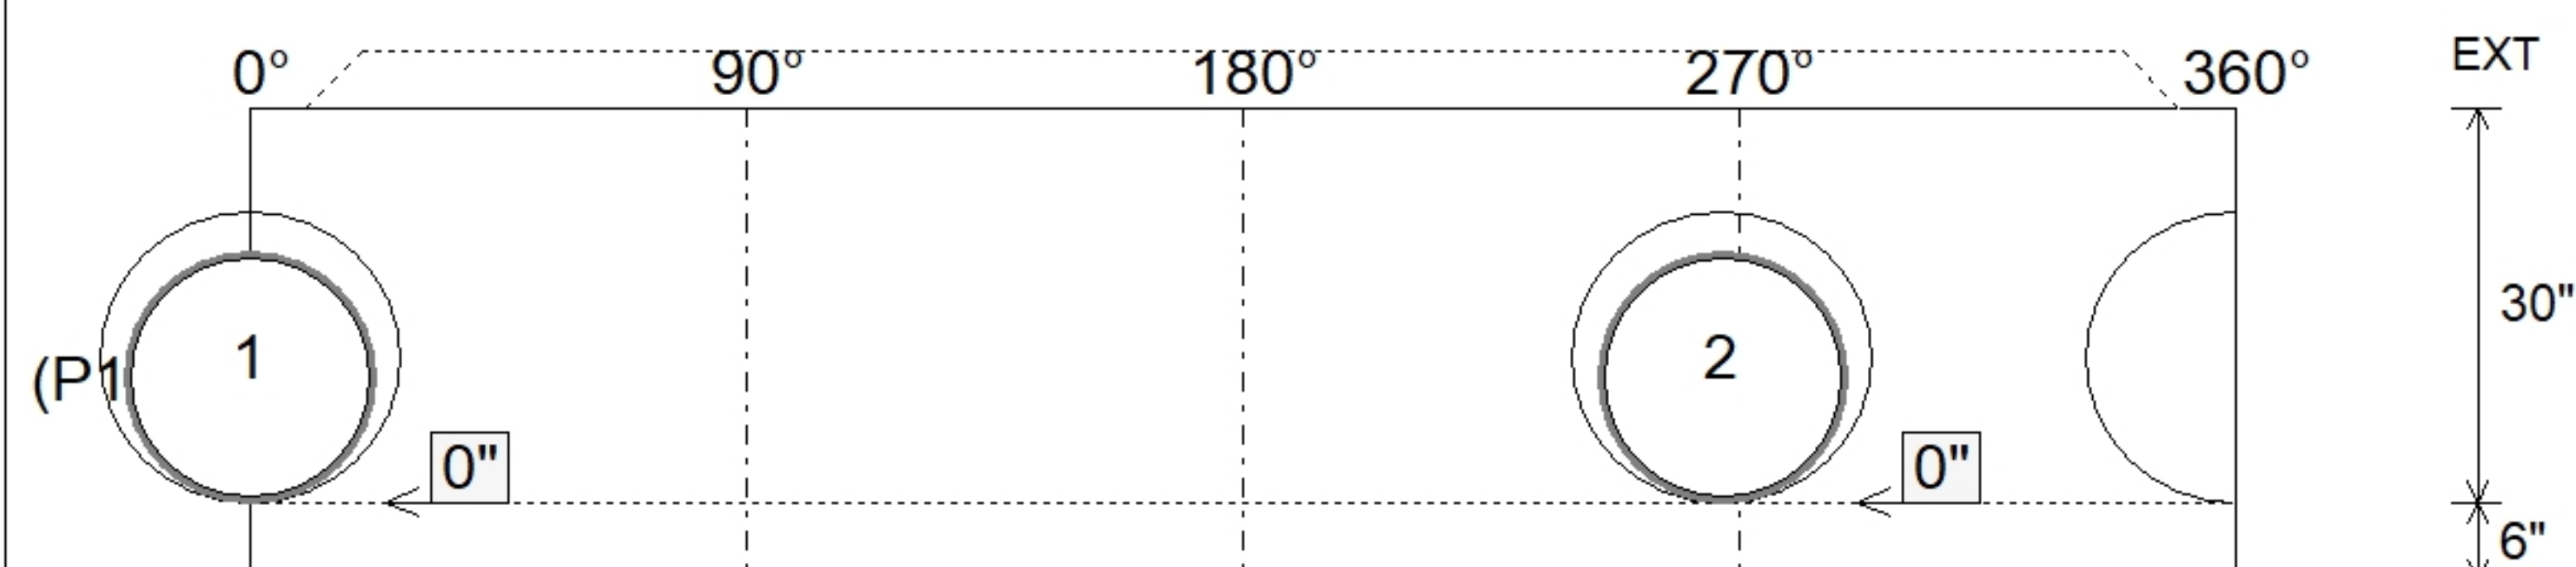

SUBMITTAL
APPROVED BY:
