

Contractor: The Allen Company, Inc.

Plant: Beaver Dam



Slack: 1"

1. KYTC DBI TYPE 3 / ASTM C913 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO STEPS & NO INVERT CHANNEL.
4. CASTING BY OTHERS
5. STUB #5 BARS 20" OUT TOP OF WALLS (SPA@12"C/C)
6. RAILING BY OTHERS


REINFORCING PER ASTM A615 (GRADE 60).

- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

P2) 36" x 36" - P.I.P. - BY OTHERS - 8"
P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 60"
1) CASTING - HOE KY-328 SET (DBI 3)
1) 36" x 36" - Conseal CS-102 1.00"
1) Hole - 34
1) Hole - 20



0 lb
8084 lb
328 lb
0 lb
0 lb
0 lb

Structure Total: 8412 lb

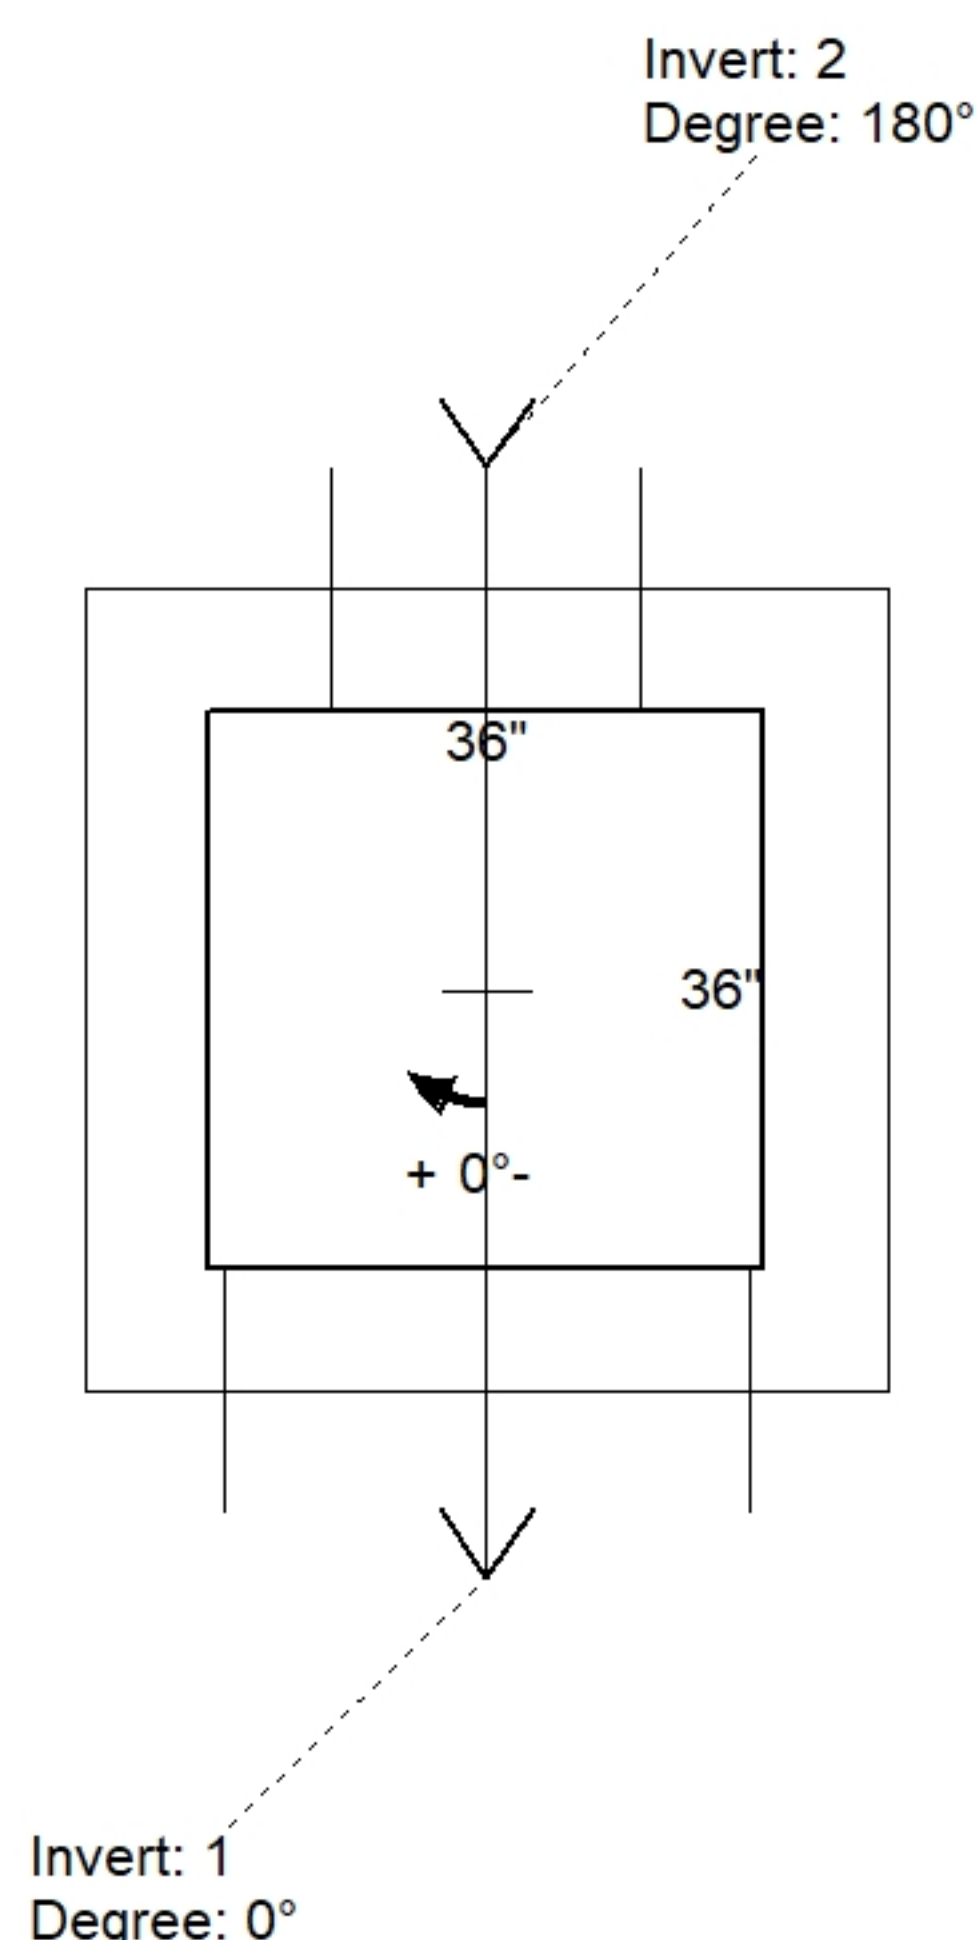

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	935.5'							
Reducer								
Invert 1	929.75'	0°	24" RCP B WALL	30"	34"	Hole 34	-5"	P1
Invert 2	929.85'	180°	12" RCP B WALL	16"	20"	Hole 20	-2.8"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

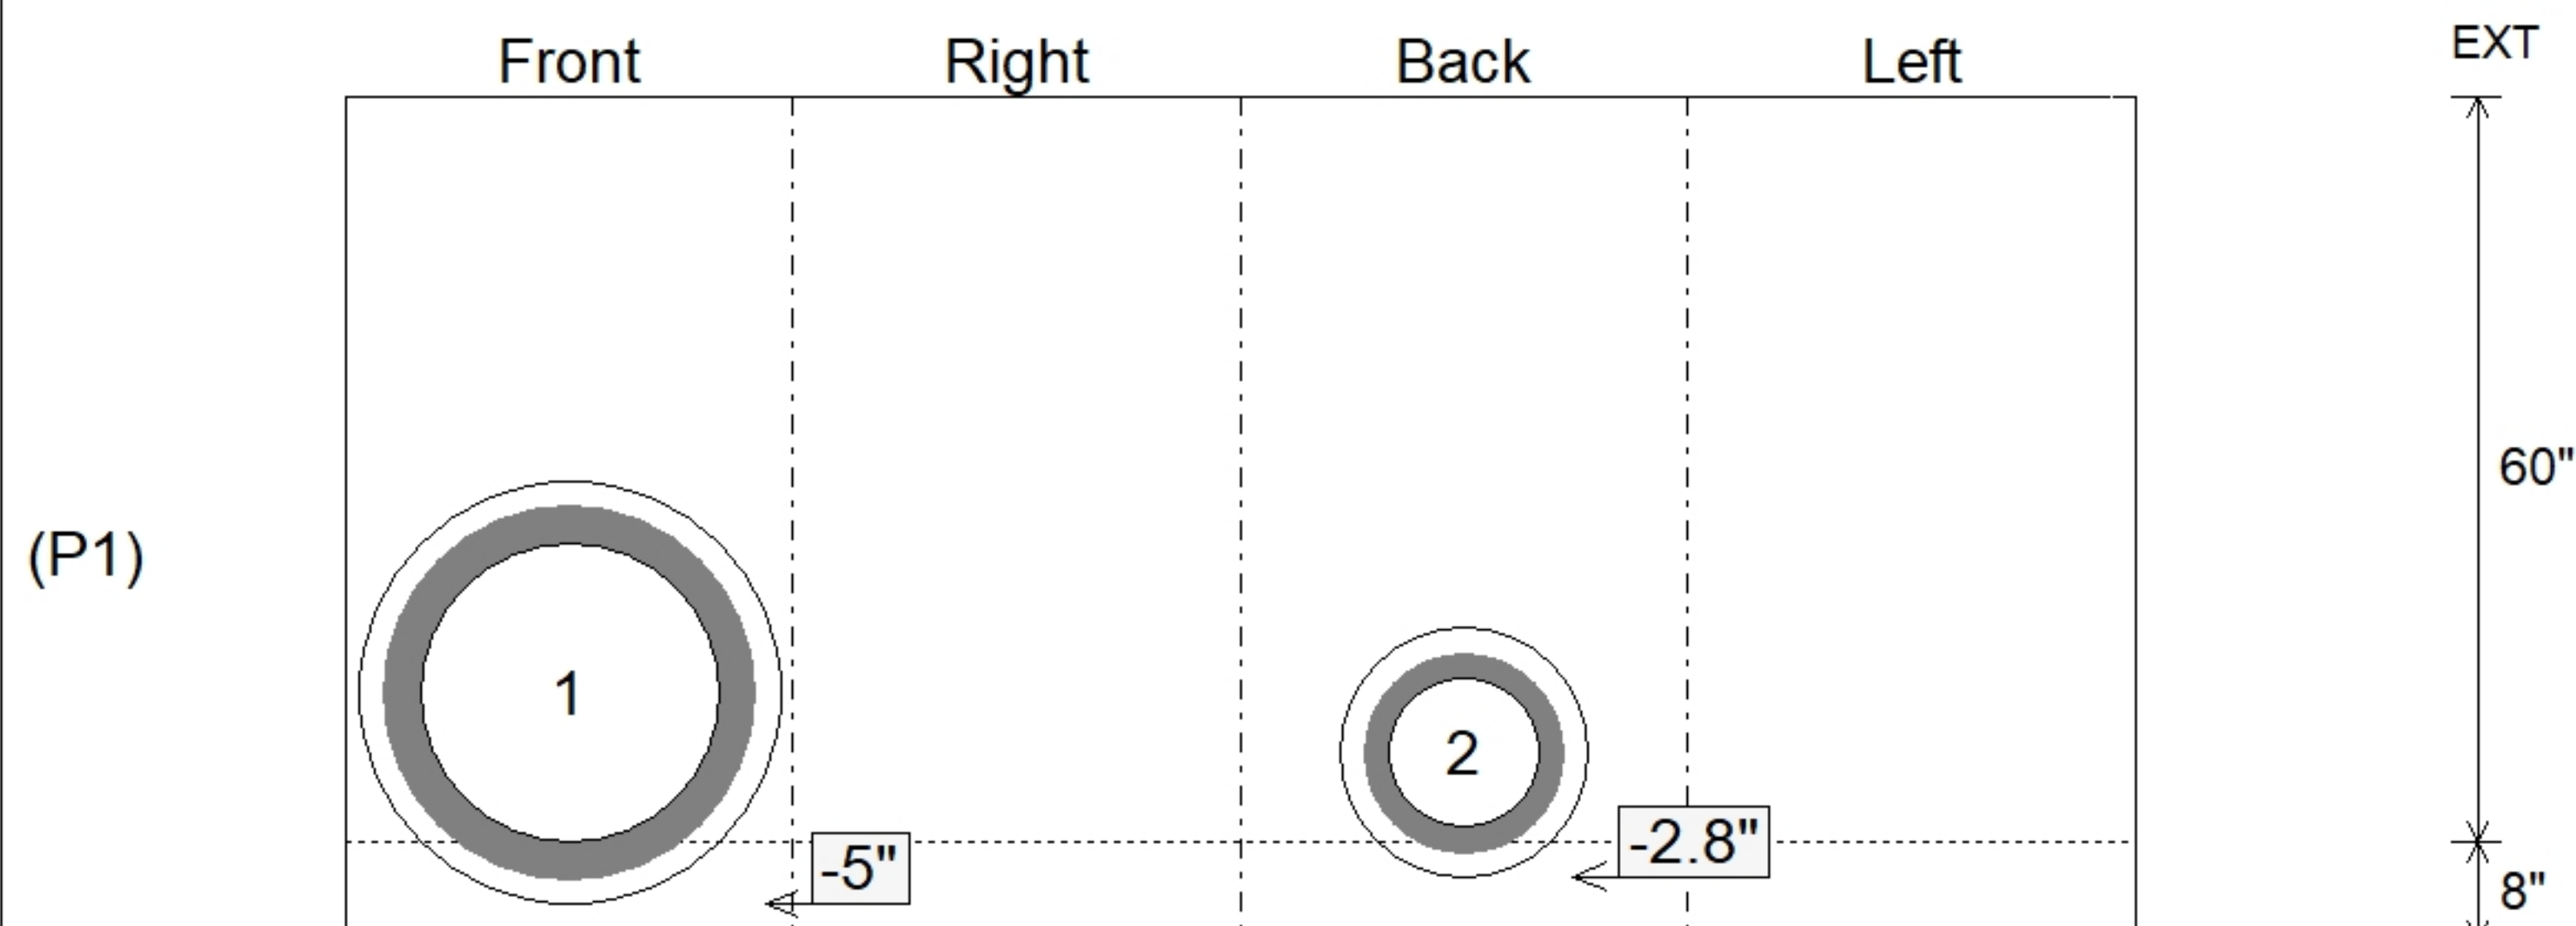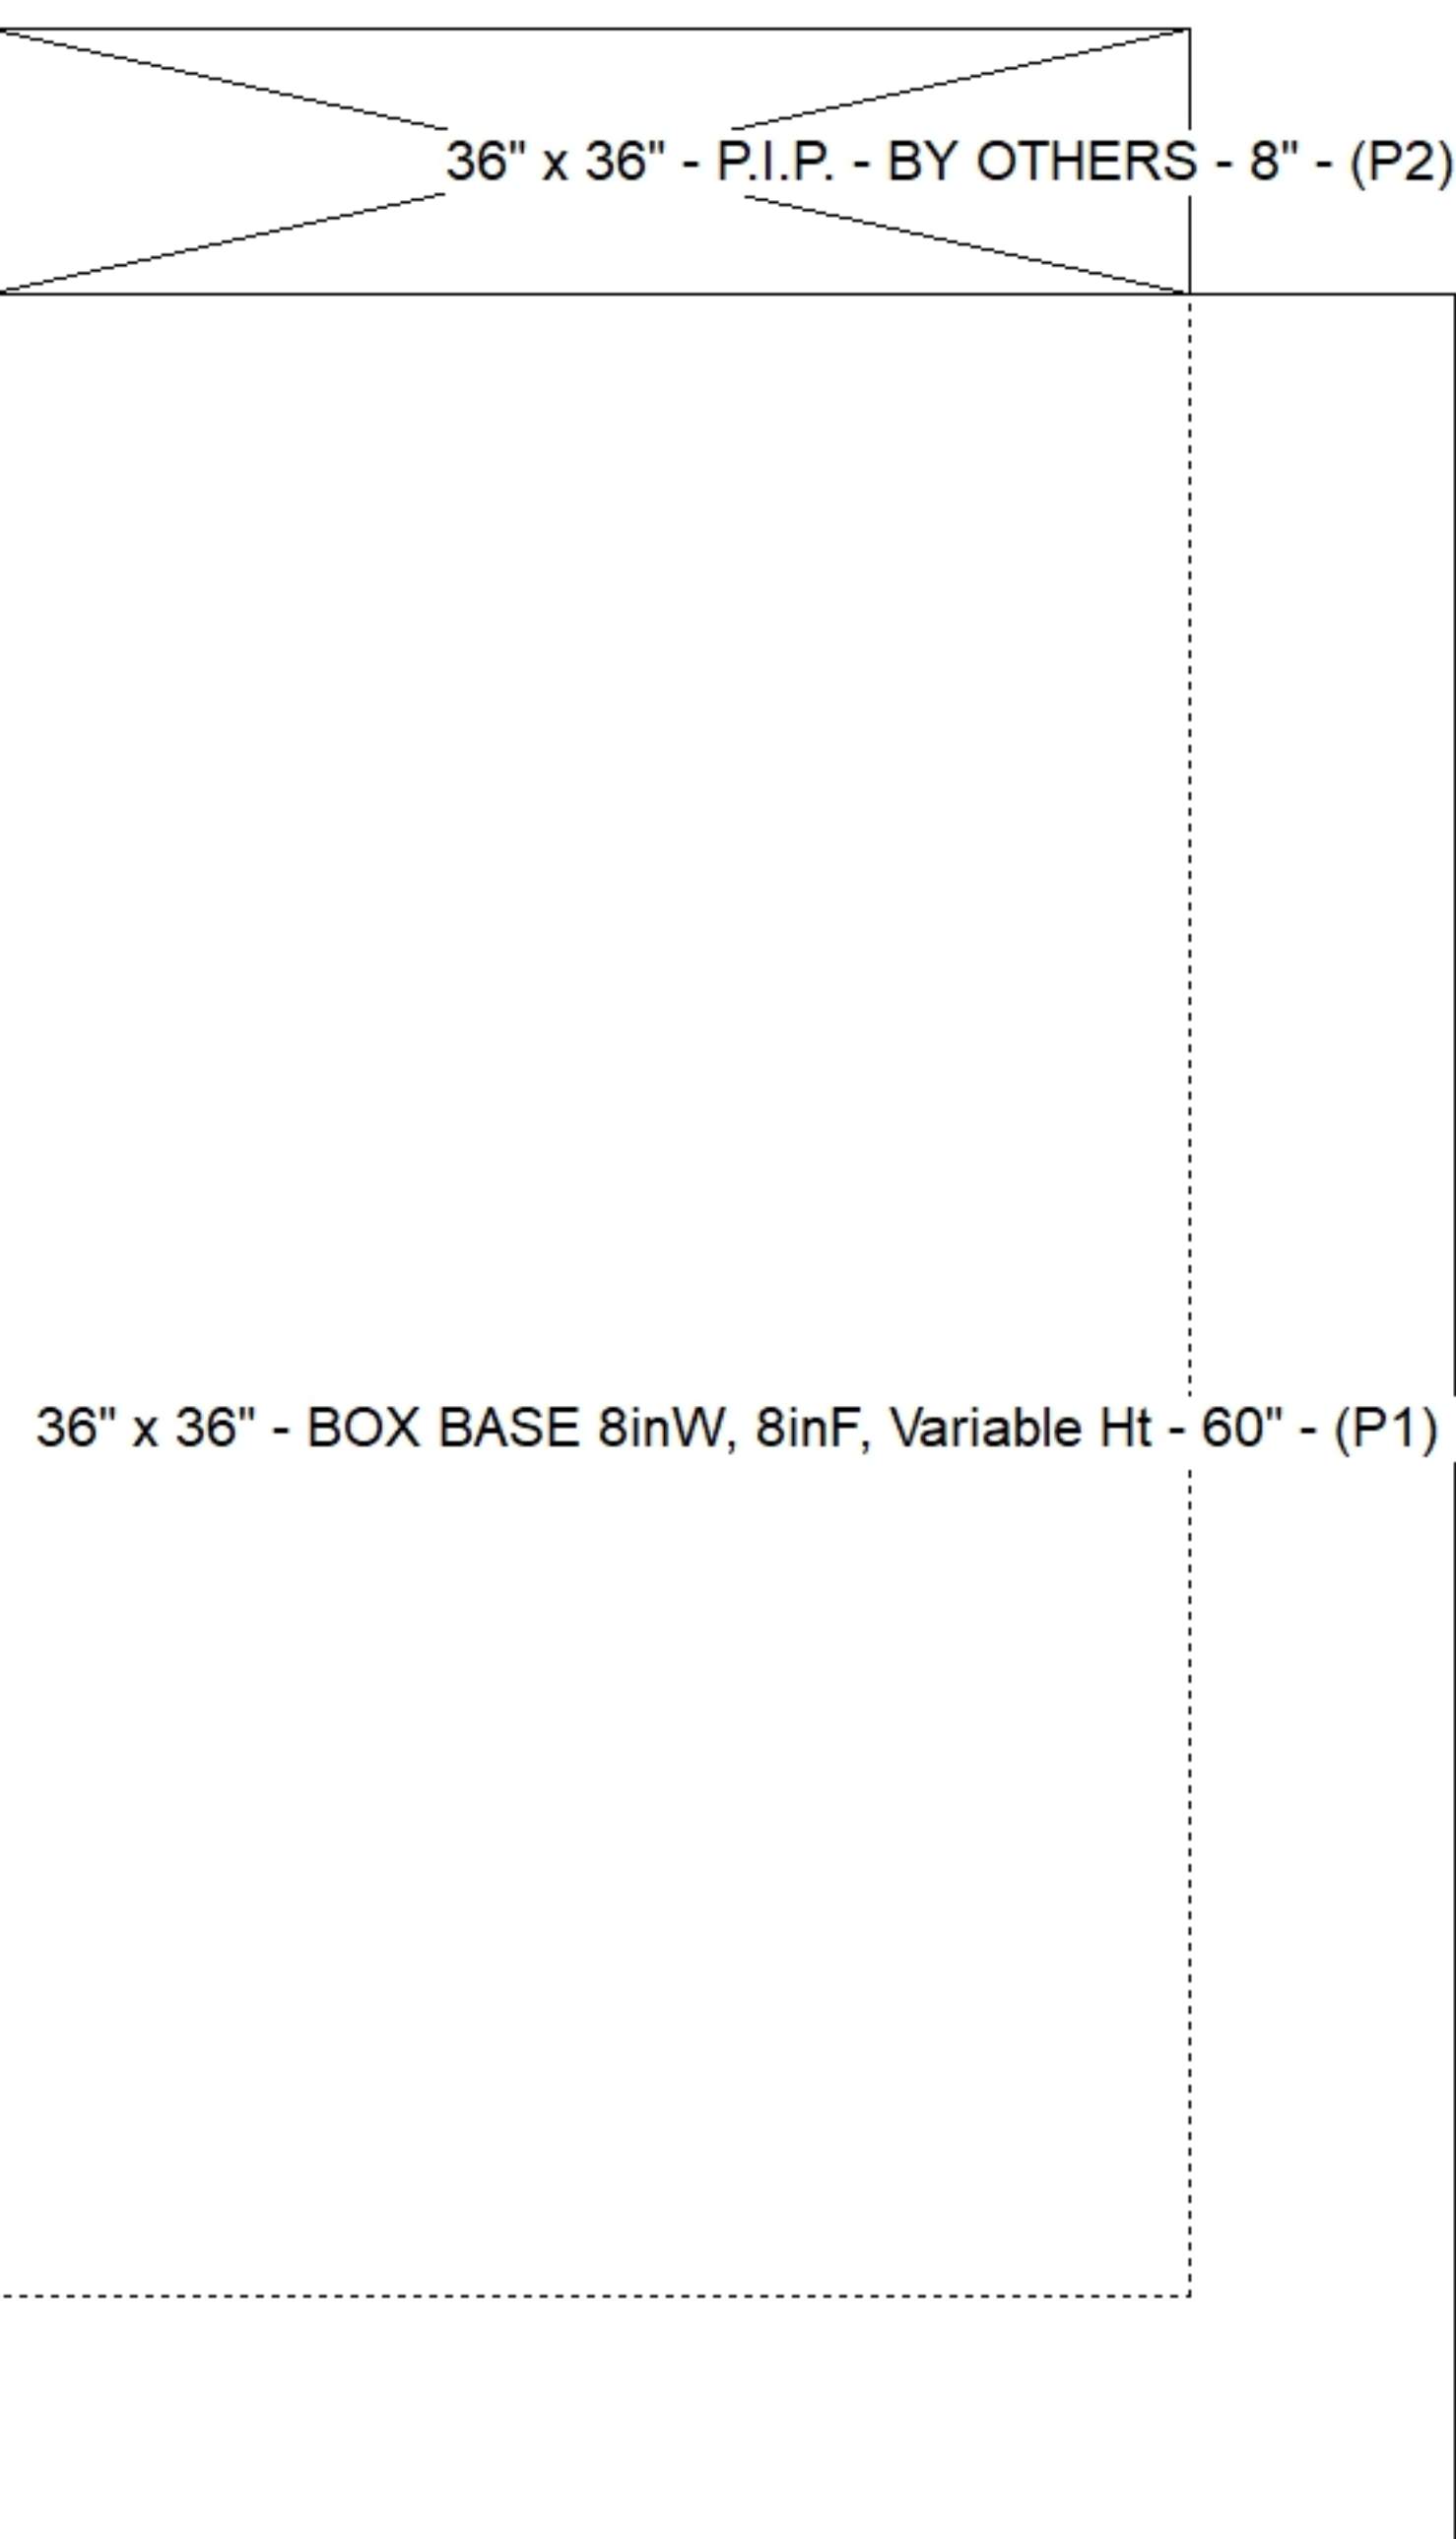

Submittal Drawing
8/26/2026 3:34:04 PM

SUBMITTAL
APPROVED BY:
