

Contractor: Lagco Inc.

Plant: Beaver Dam




Slack: 0"

1. JR HOE HOE-525 LV SET PROVIDED BY ICAST
2. PER LEFUCG CBI TYPE D/ ASTM C913 SPEC'S.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (grade 60).
 - WALLS (As .31) #5 BARS AT 12" C.C.E.W.
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

P2) 24" x 36" - CASTING HEIGHT - 6"
P1) 24" x 36" - BOX BASE 8inW, 8inF - 36"
1) CASTING - HOE 525 LV SET (F/G/H)
1) 24" x 36" - Conseal CS-102 1.00"
1) Hole - 16
1) Hole - 14
1) Hole - 6



0 lb
4812 lb
442 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 5254 lb

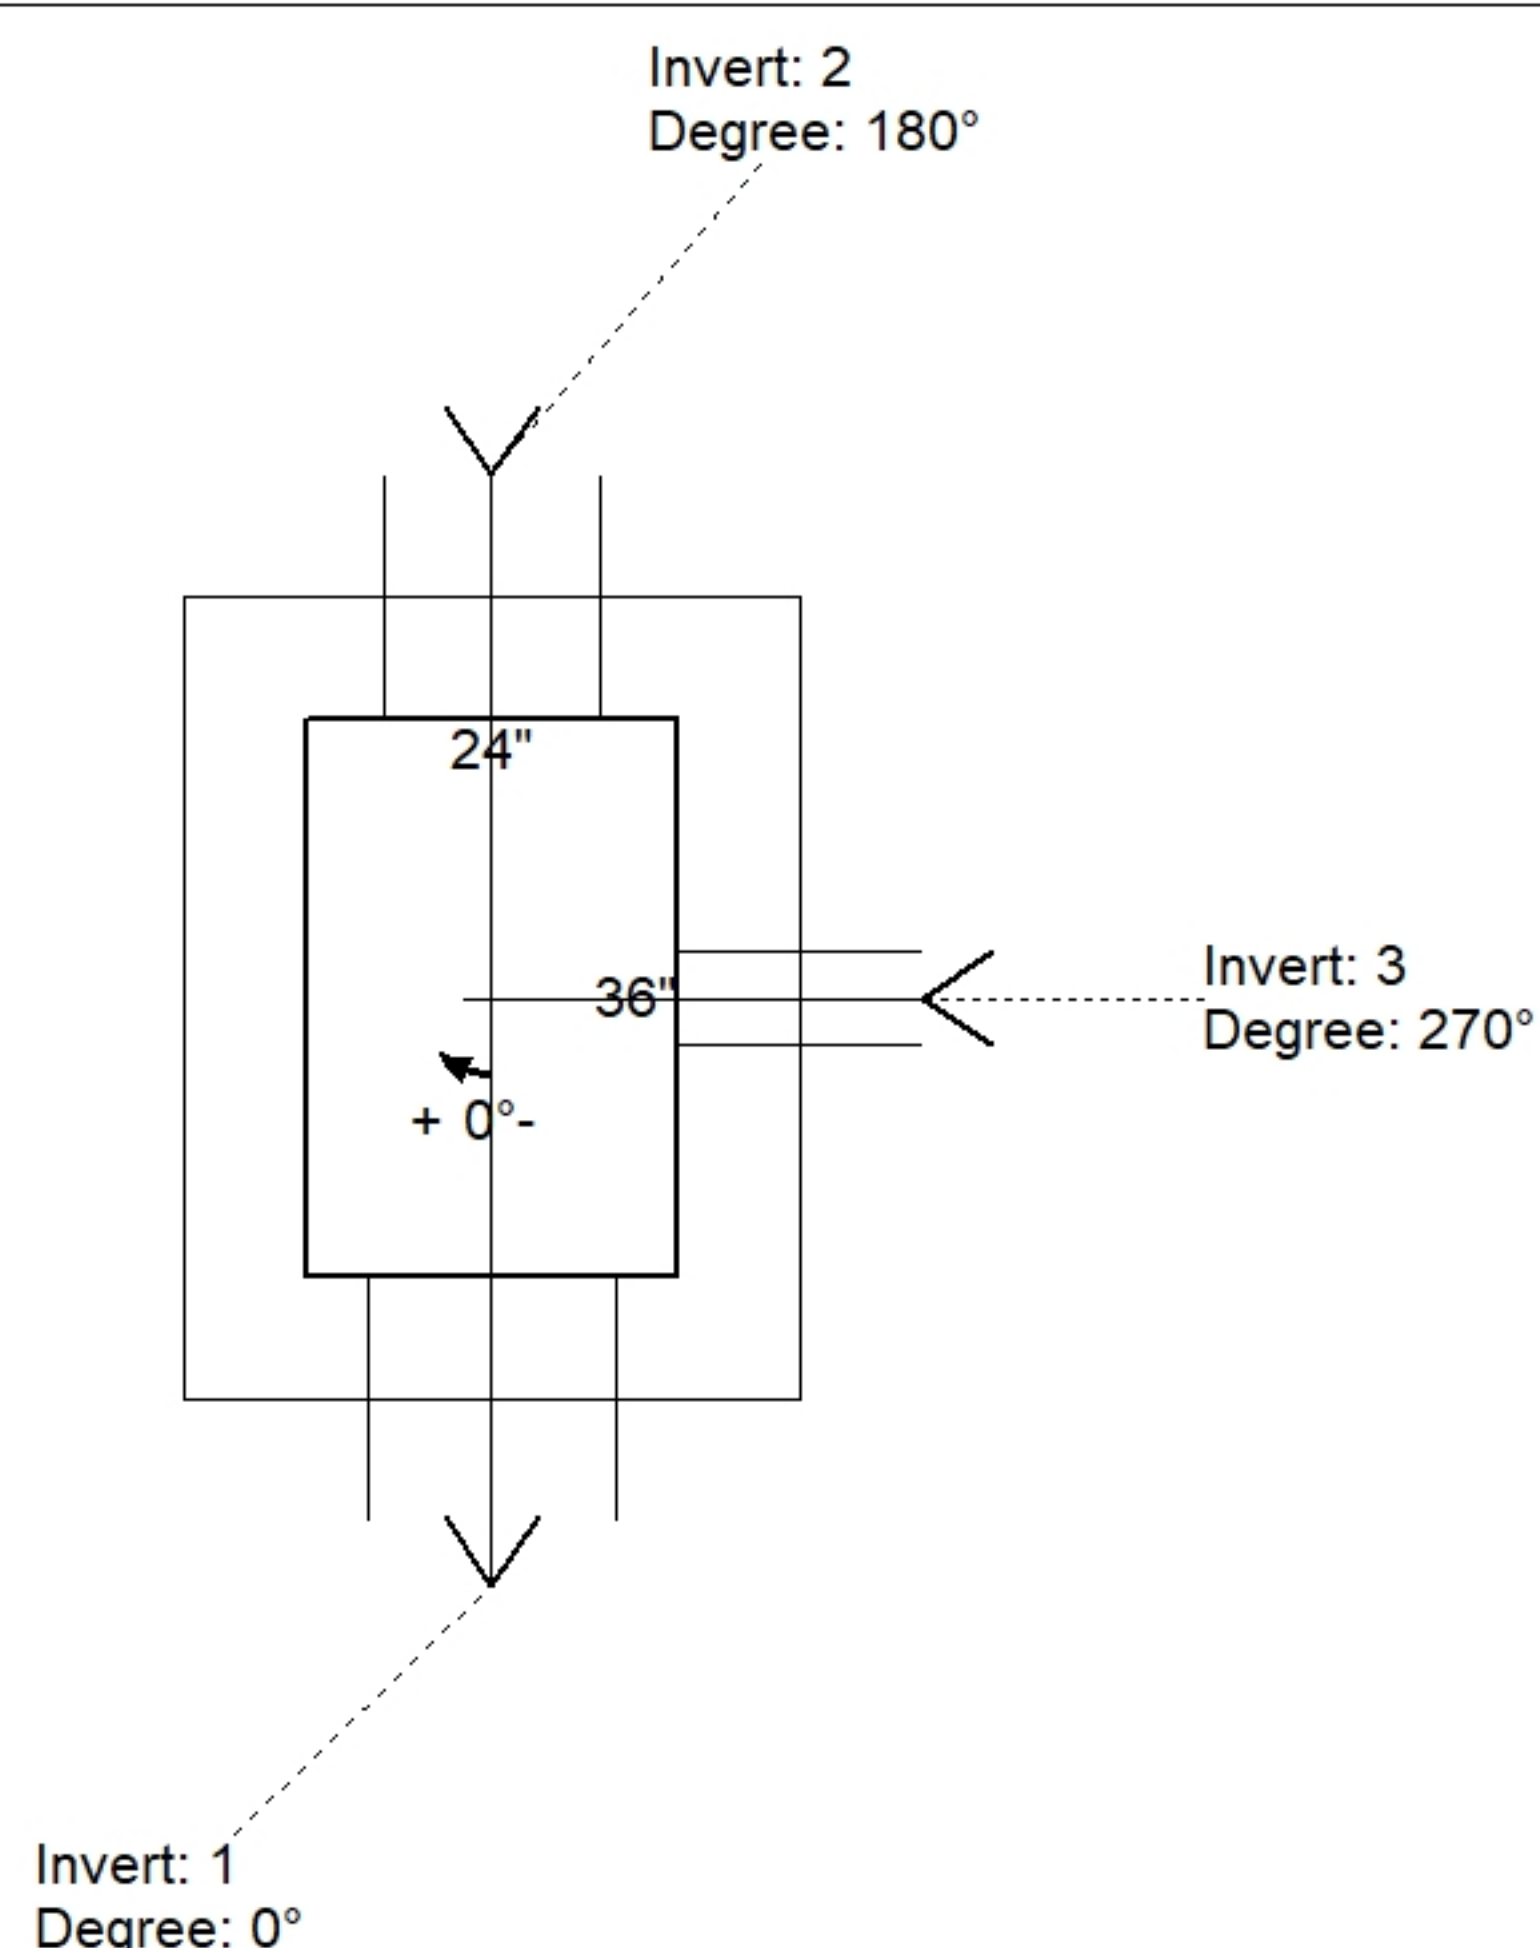

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (␣)	Ref
Rim	850.3'							
Reducer								
Invert 1	846.8'	0°	12" HDPE	14.5"	16"	Hole 16	-1.25"	P1
Invert 2	846.9'	180°	10" HDPE	11.4"	14"	Hole 14	0.5"	P1
Invert 3	848.6'	270°	4" HDPE (perf pipe)	4.8"	6"	Hole 6	21.2"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

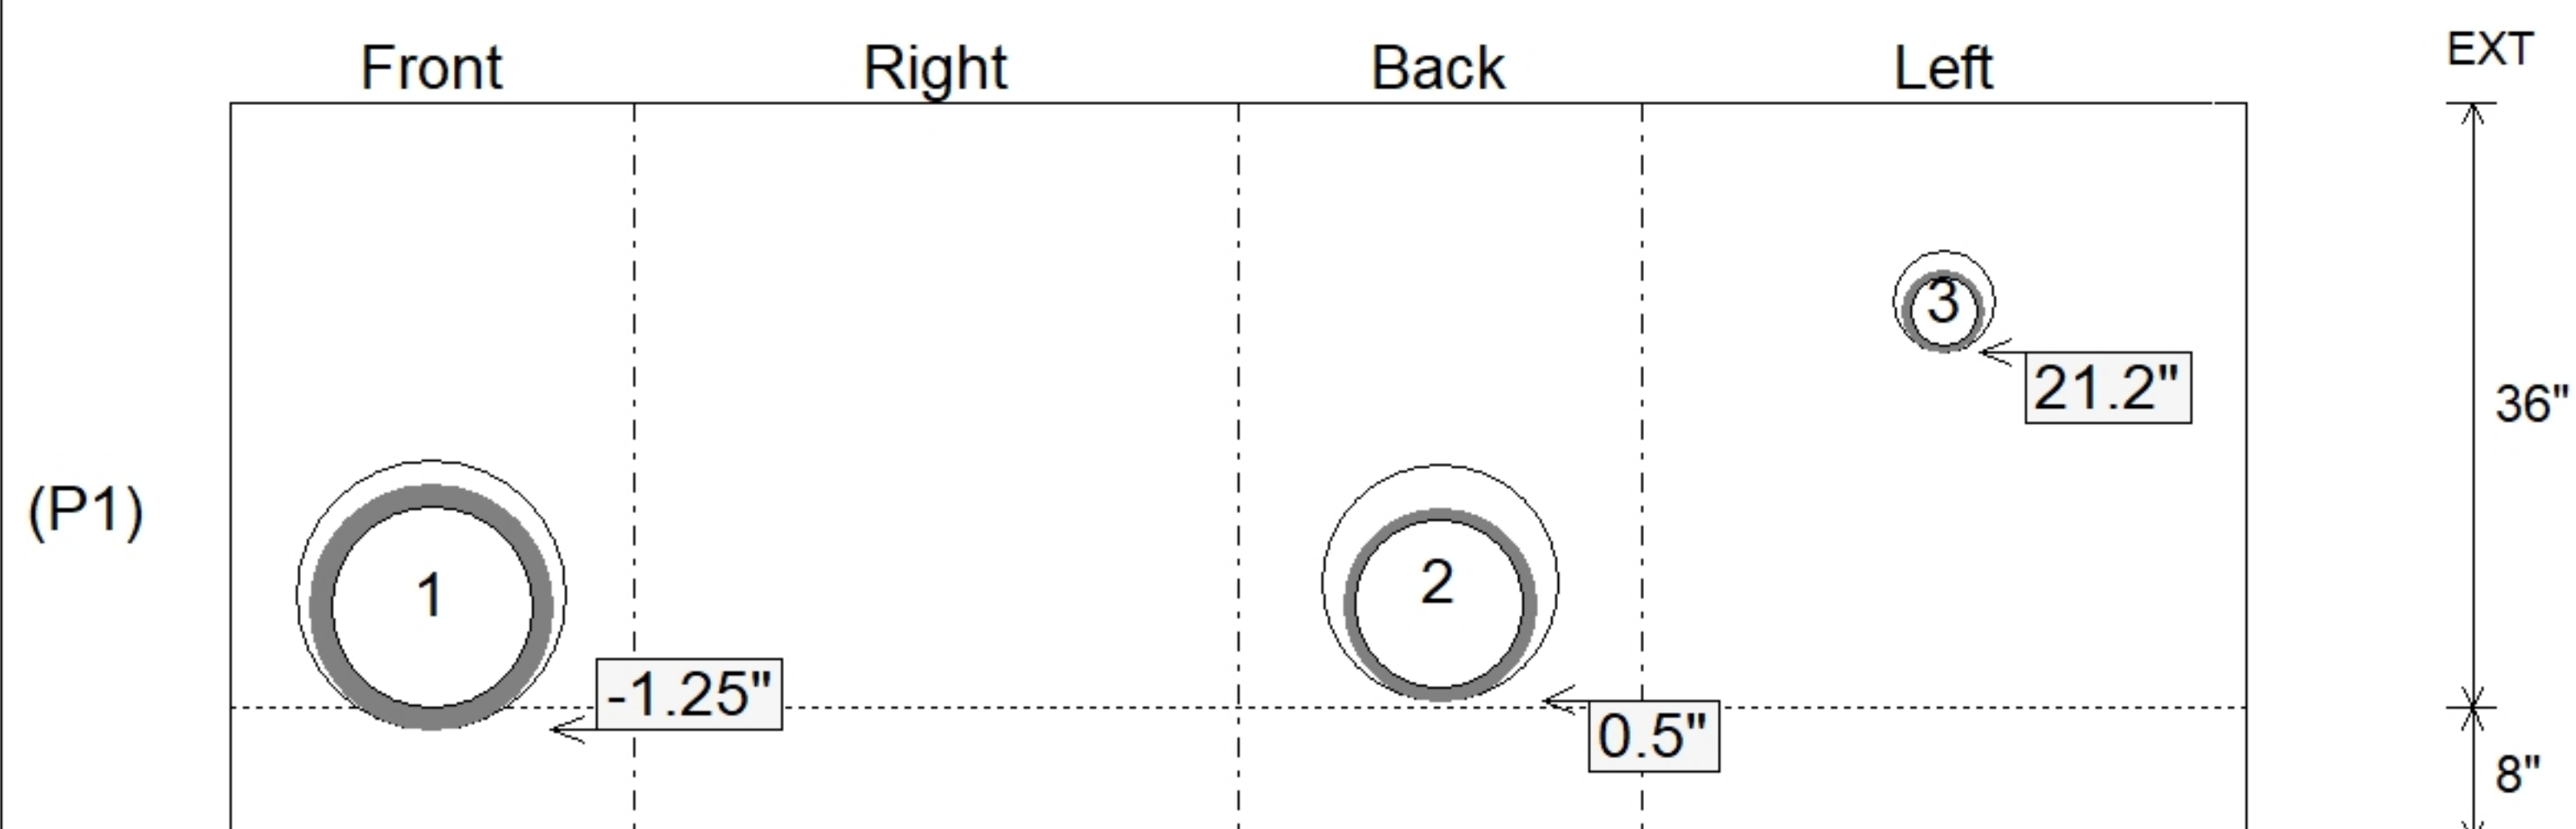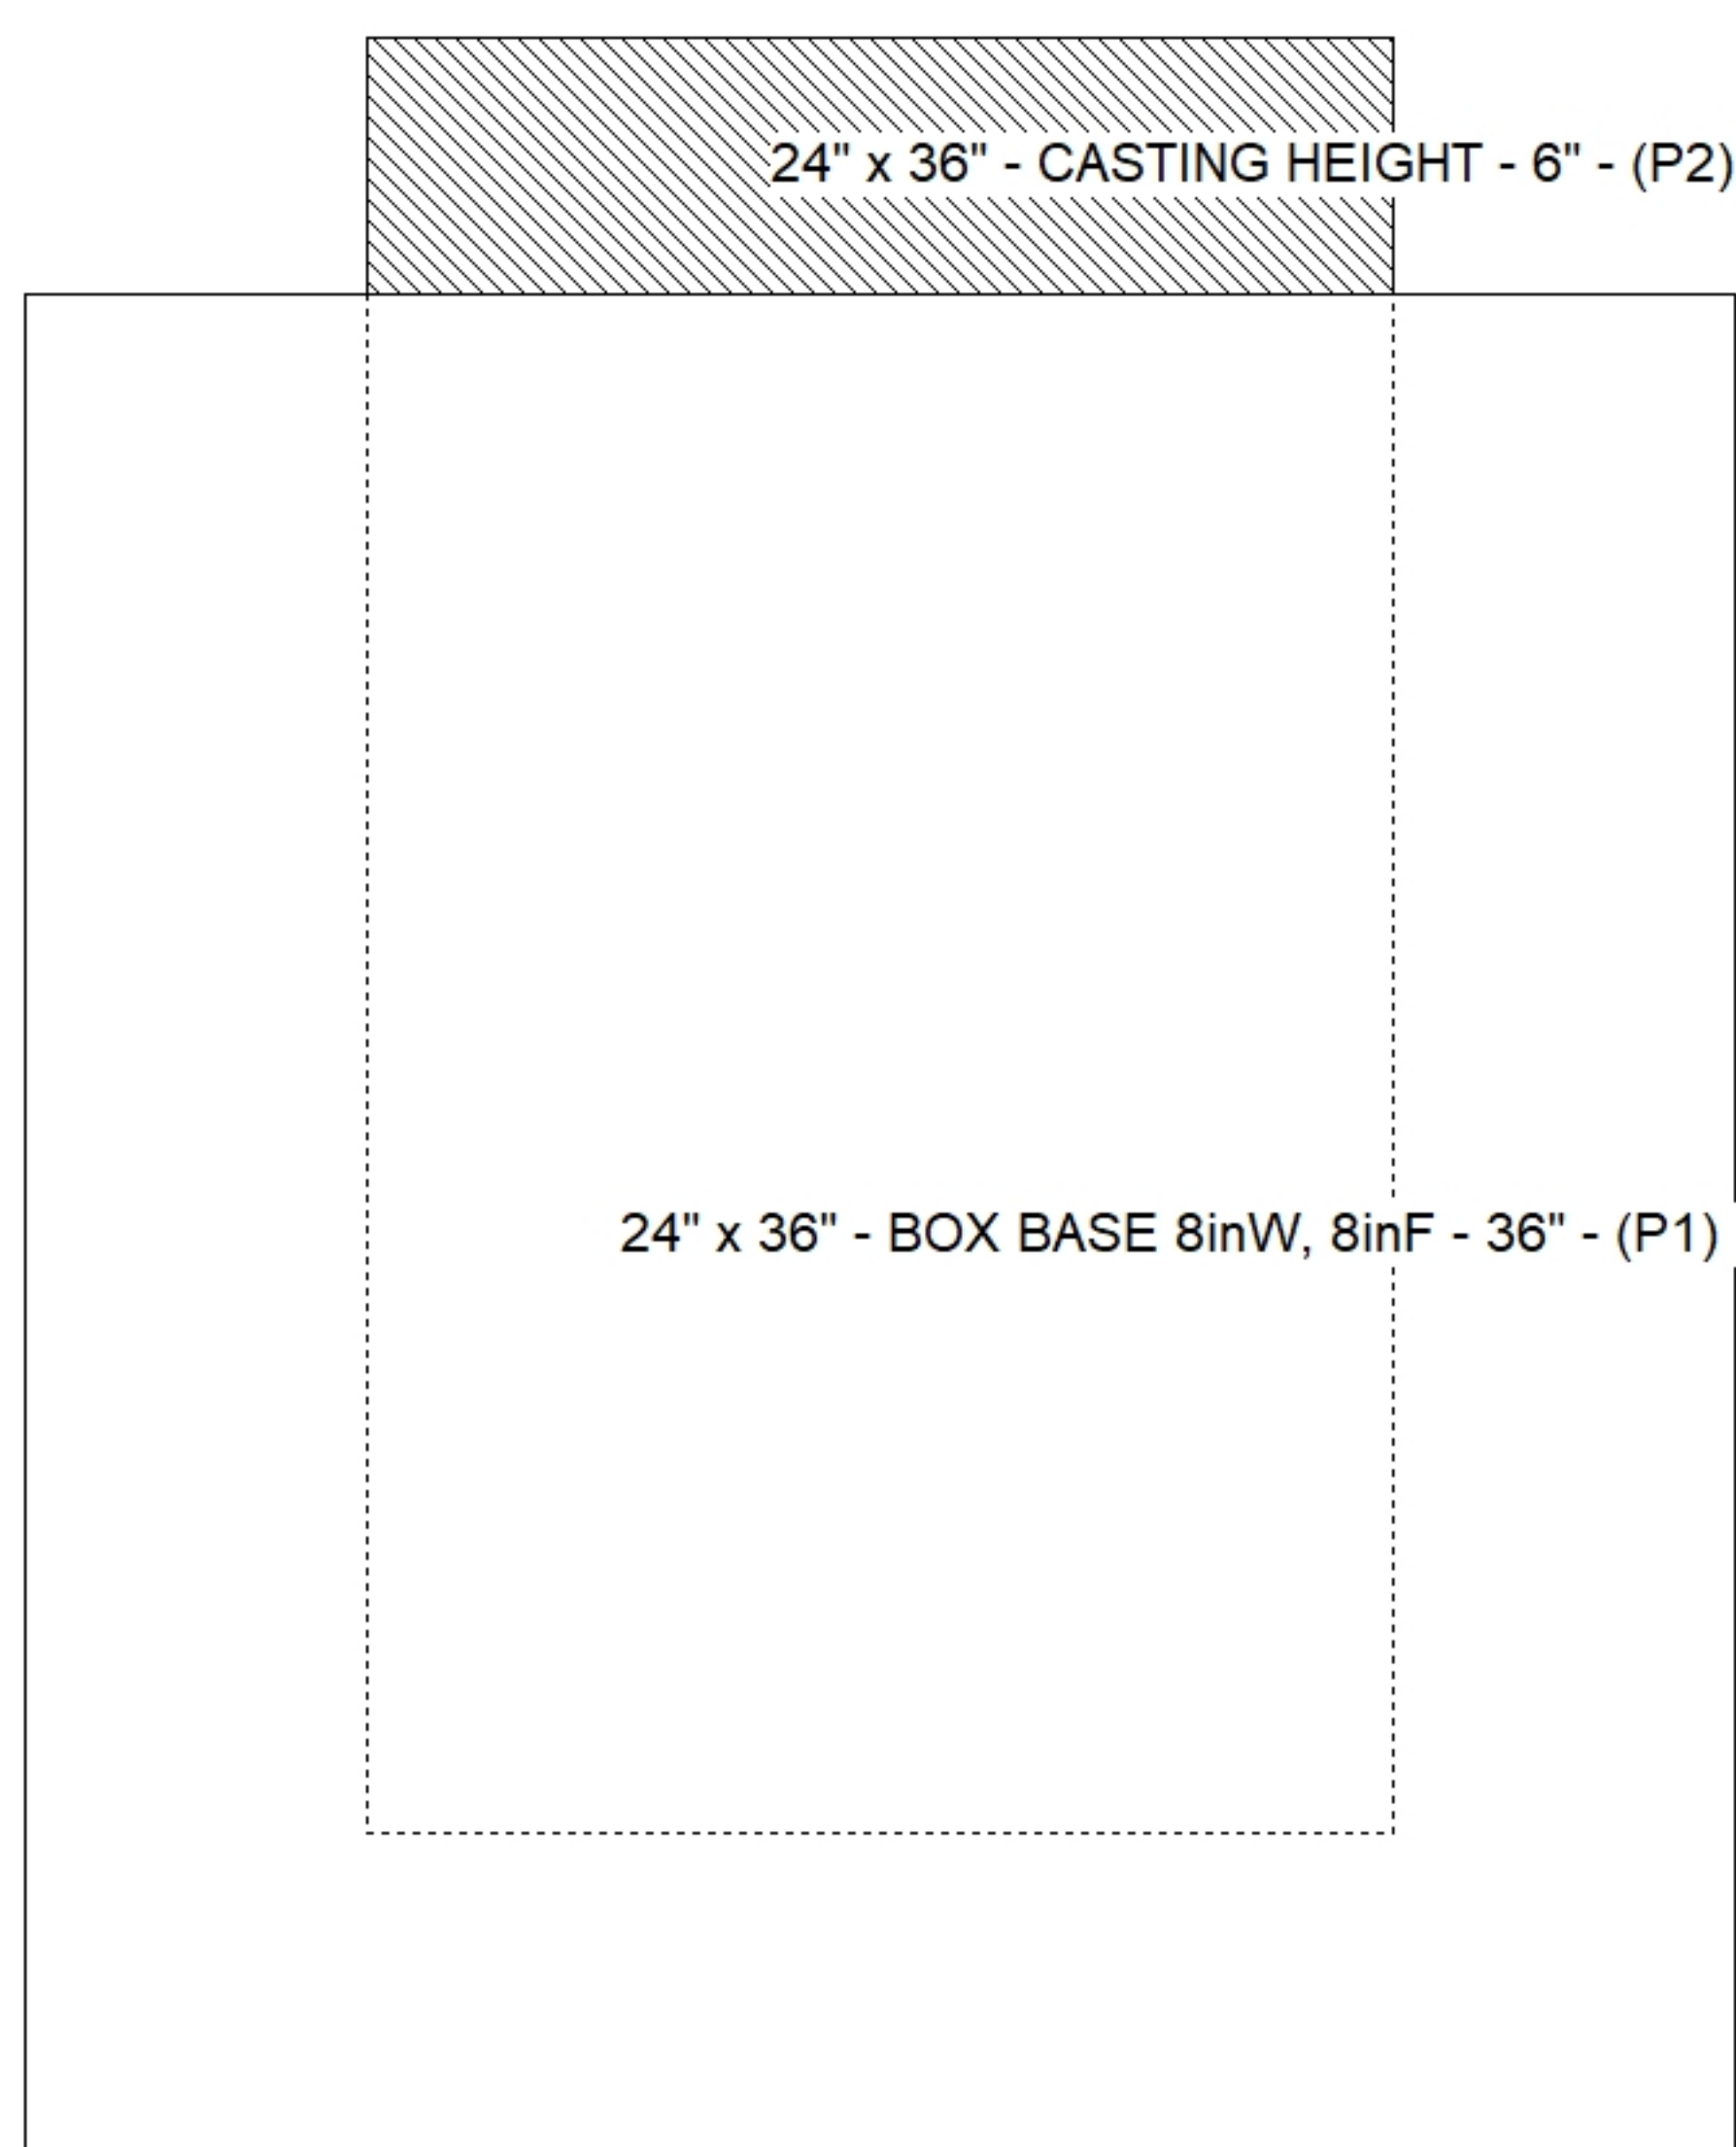

SUBMITTAL
APPROVED BY:
