

Contractor: Walker Building Group

Plant: Beaver Dam




Slack: 0.84"

- FLOOR (As .62) #5 BARS AT 6" C.C.E.W.

1) DOGHOUSE INVRTD - 22"x19"



0 lb

Structure Total: 9075 lb

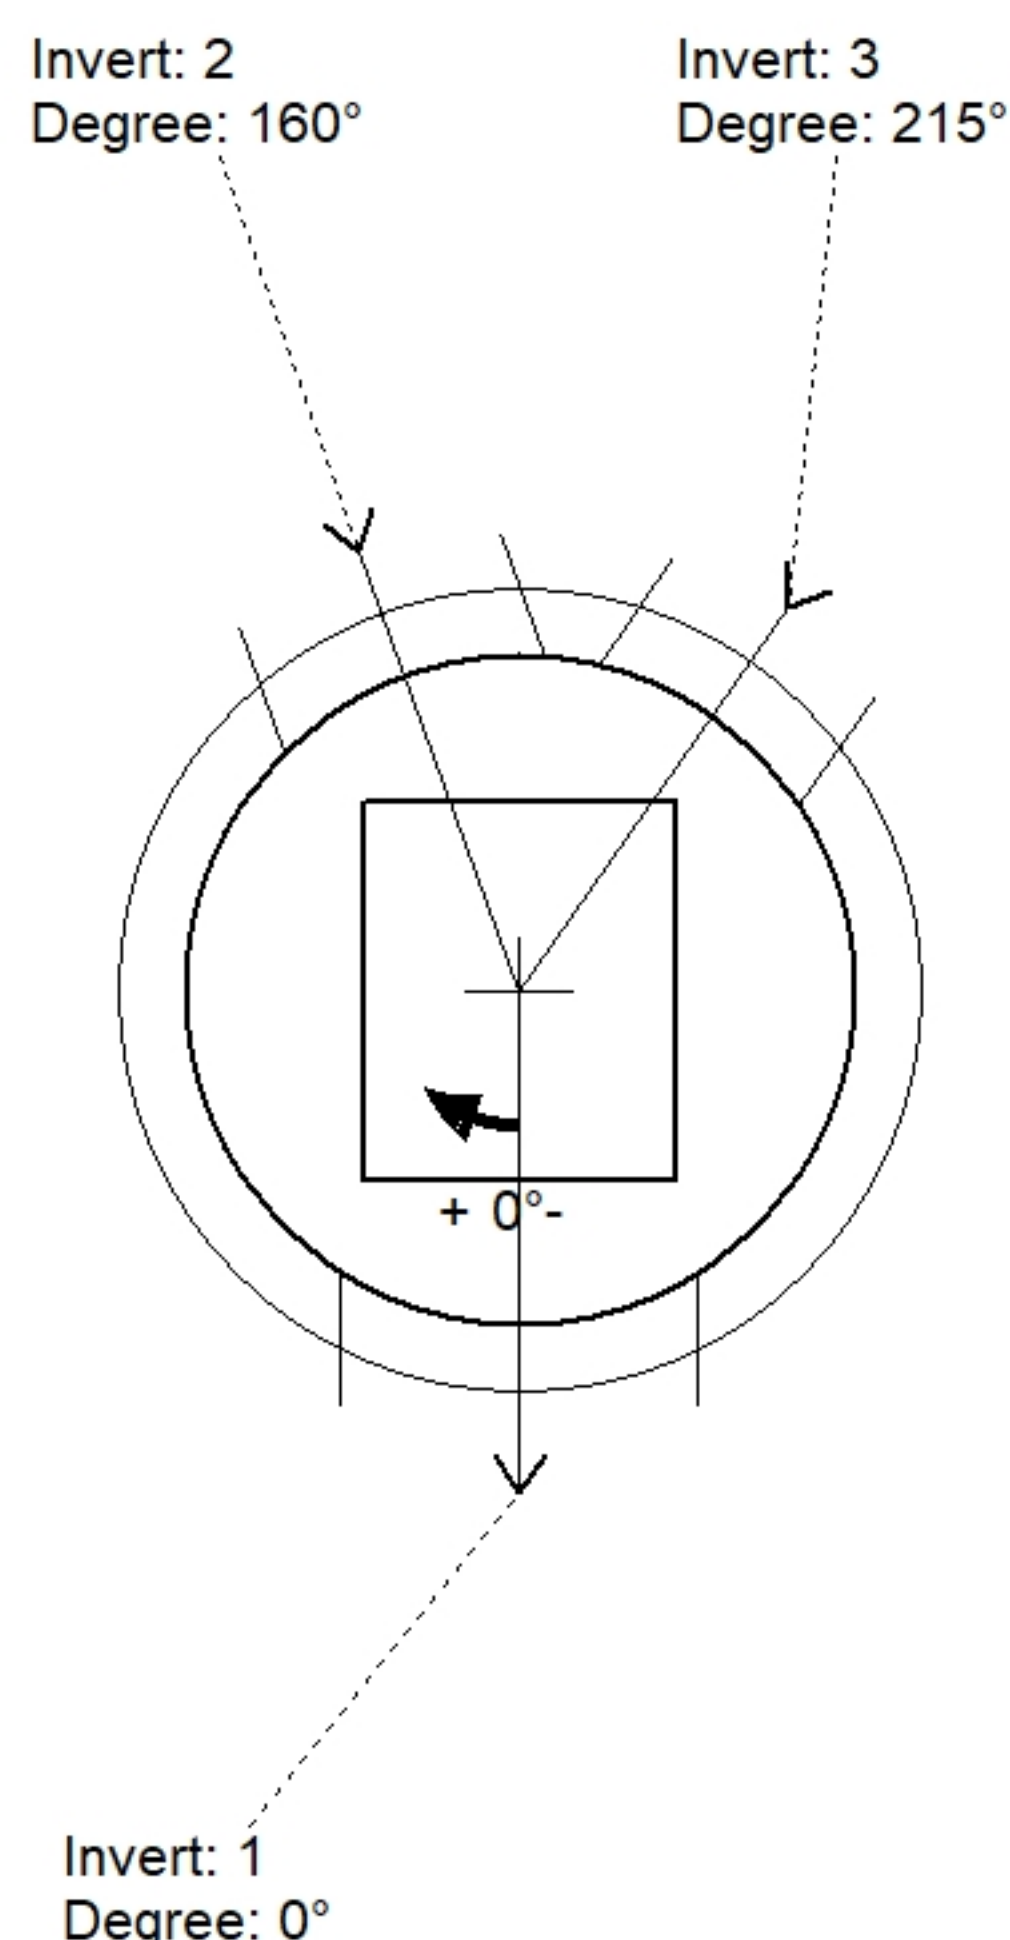

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	554.57'							
Reducer								
Invert 1	550.5'	0°	24" RCP B WALL	30"	32"	Hole 32	0"	P1
Invert 2	551.04'	160°	18" RCP B WALL	23"	25"	Hole 25	6.98"	P1
Invert 3	551.5'	215°	18" CMP	19"	22" x 19"	DOGHOUSE INVRTD 22"x19"	14.5"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

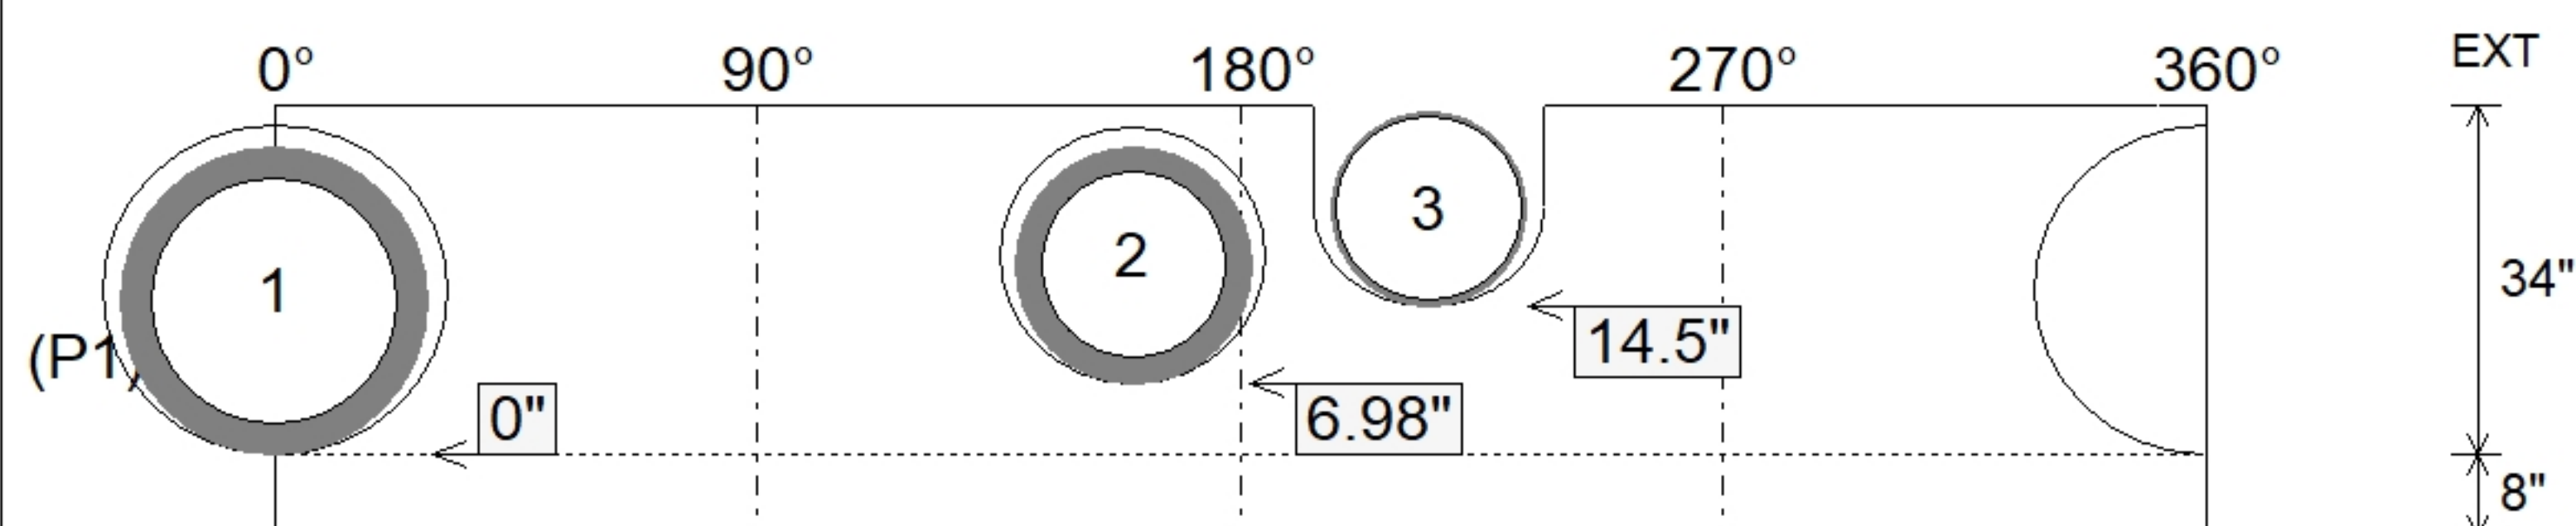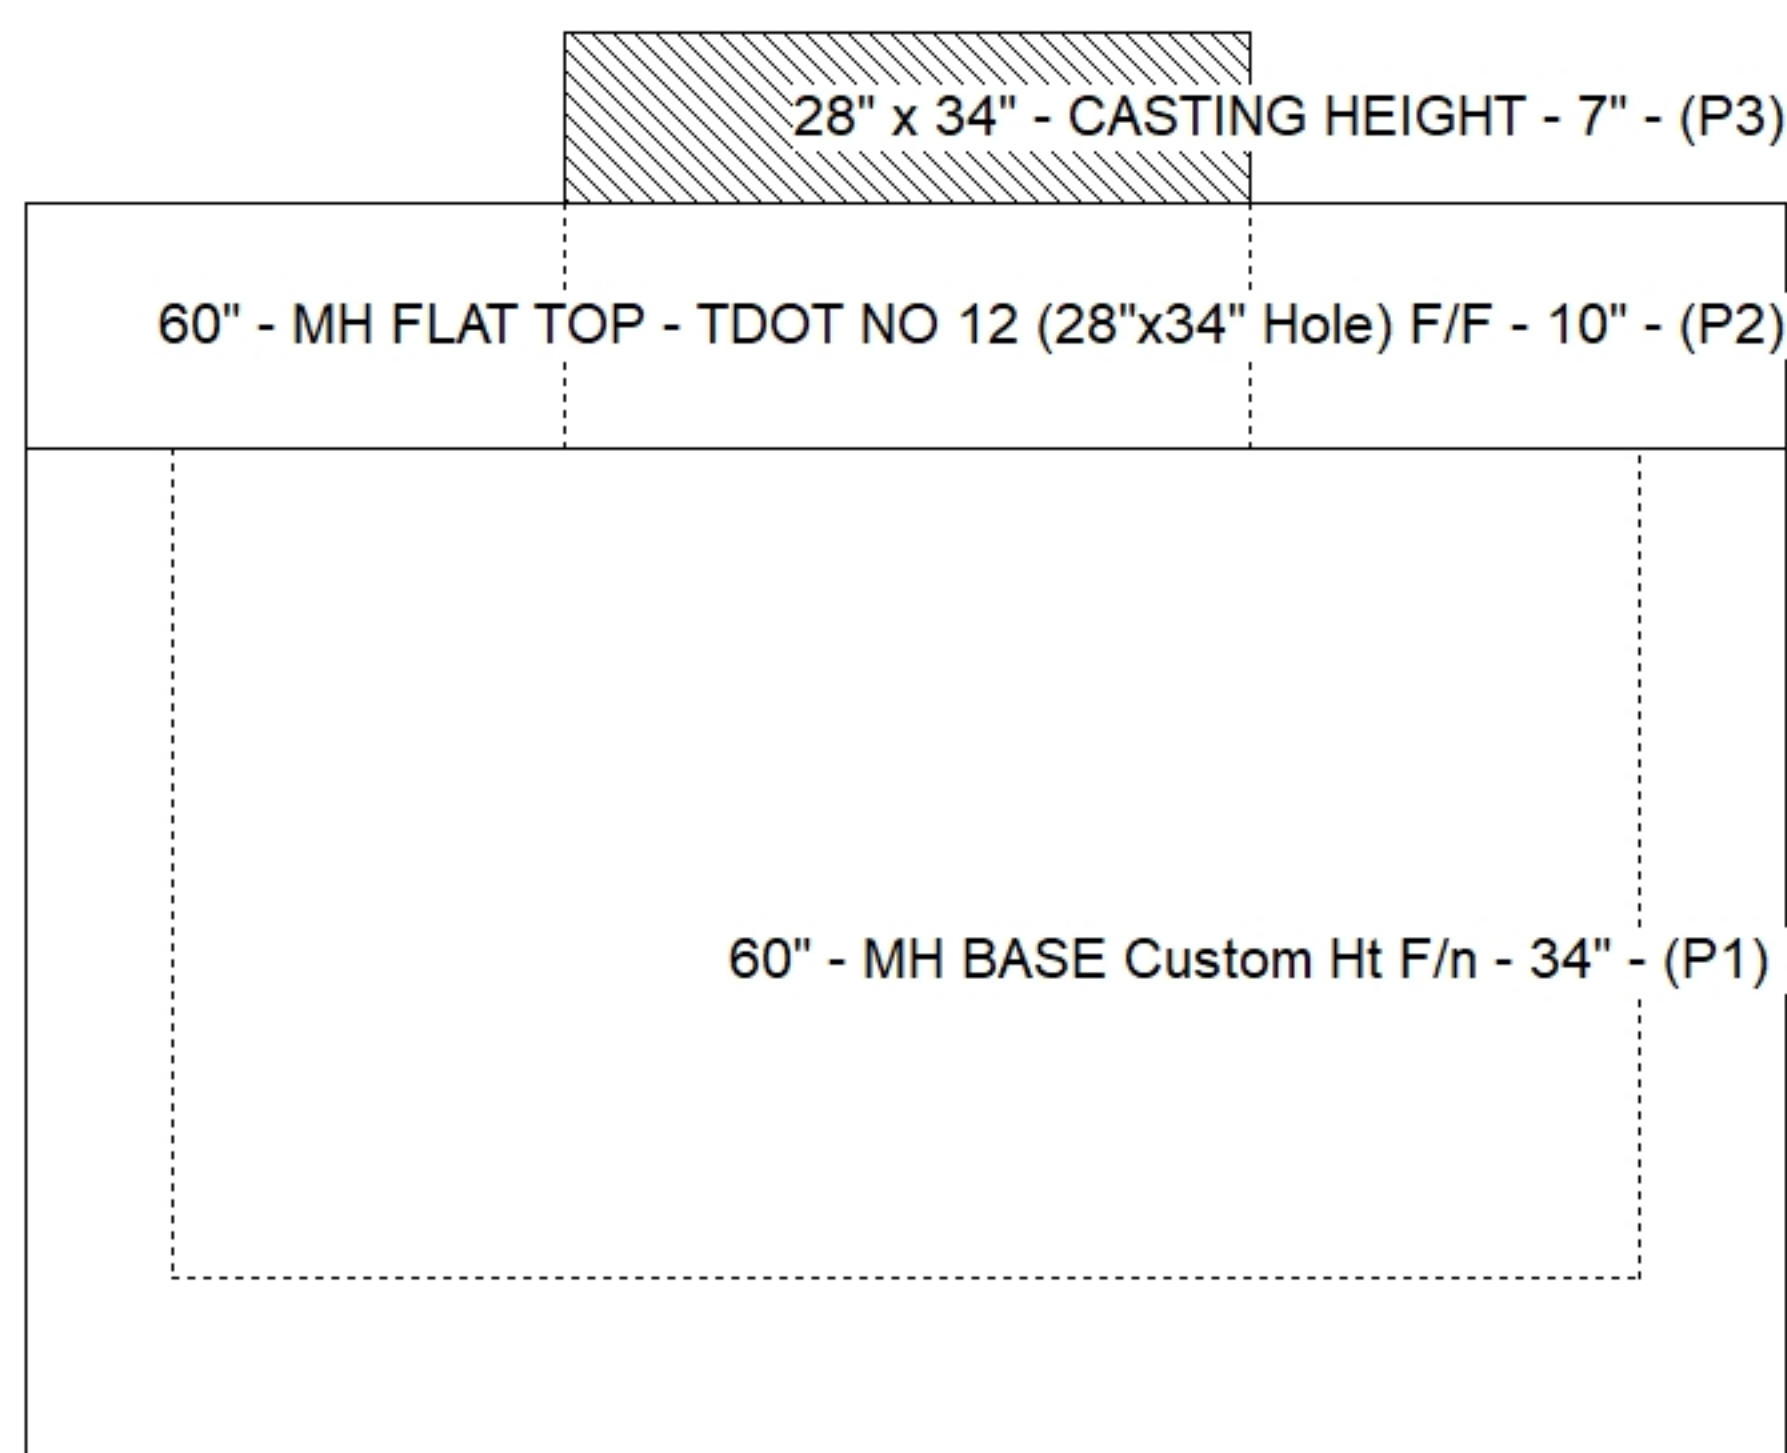

SUBMITTAL
APPROVED BY:
