

Job Name: 26-3166 Rolling Hills PRETX
Job Location: Franklin, TN
Contractor: Convergent Water Technologies

Plant: Beaver Dam
8/7/2026 8:45:41 AM

Tech: J. Coppage
PC: C. Goff



Structure ID: FB1 ST-DBI

P2 BX048048-08LD06S



BX FLAT LID 8inW SPEC. W/ MCS-288

- P3) 24" - CASTING HEIGHT - 0"
P2) 48" x 48" - BX FLAT LID 8inW SPEC. W/ MCS-288 - 6"
P1) 48" x 48" - BOX BASE 8inW, 8inF, Variable Ht - 38"
1) CASTING - HOE MCS-288 F/C Cast-IN
1) SECONDARY POUR - WEIR WALL - *
1) 48" x 48" - Conseal CS-102 1.00"
1) SQ. Hole - 48"x19.75"
1) DOGHOUSE INVRTD - 22"x23.25"

- Structure Notes: .
1. JR HOE MCS-288 F/C BY ICAST.
2. FRAME TO BE CAST INTO THE TOP SLAB.
3. PER ASTM C913 SPEC'S.
4. CONCRETE = 4,000 PSI AT 28 DAYS.
5. REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .40) #4 BARS AT 6" C.C.E.W.
- WALLS (As .40) #4 BARS AT 6" C.C.E.W.
- FLOOR (As .40) #4 BARS AT 6" C.C.E.W..
6. (TRASH SCREEN SUPPLIED & INSTALLED BY OTHERS)

Structure Total:

10020 lb

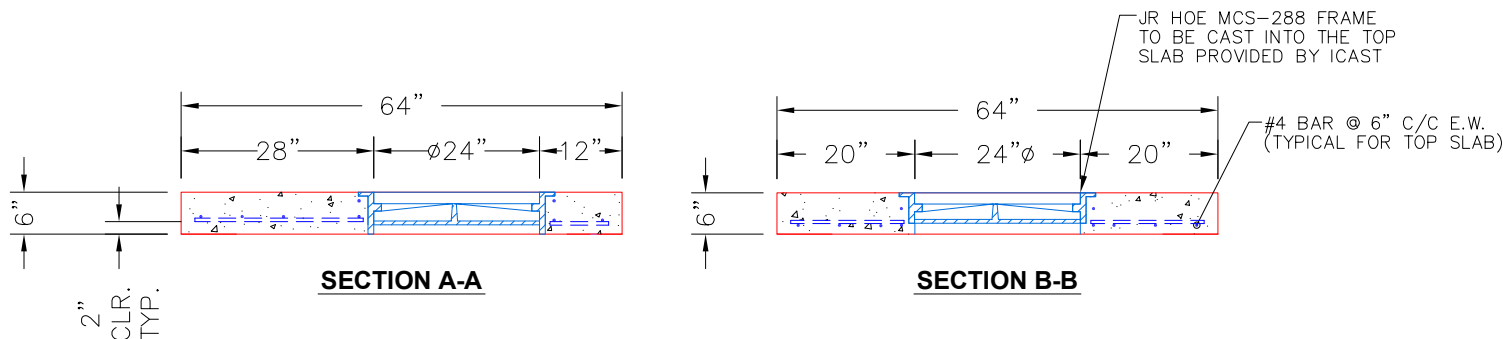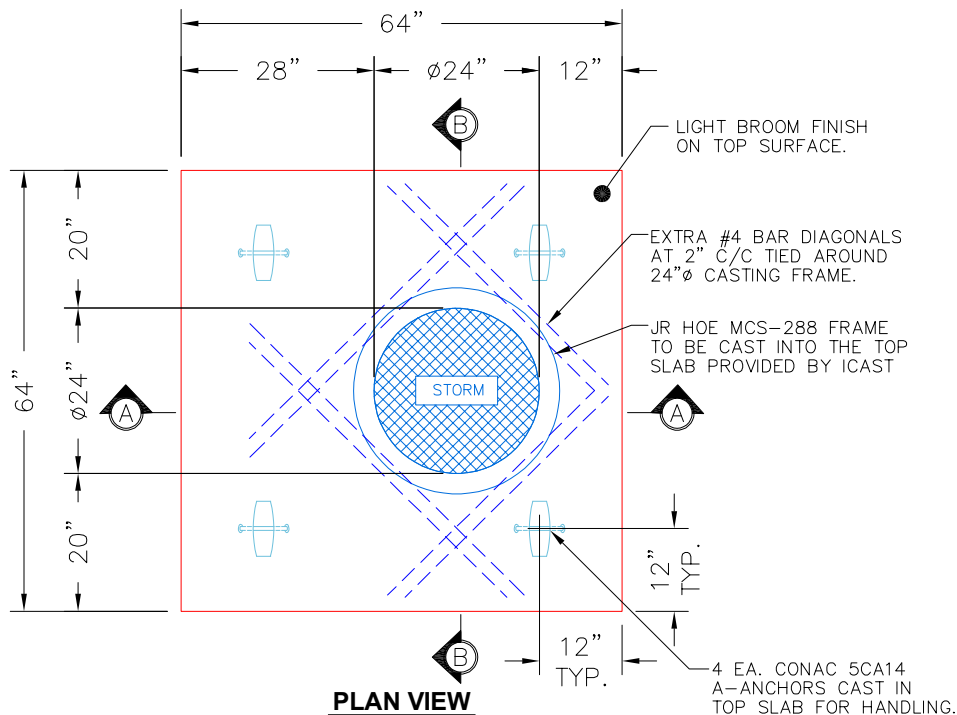

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 6"

Weight (Net): 1829 lb
Volume (Net): 0.47cu.yd
