


Job Name: 26-3805 - Goldfinch Sewer Ph.3 Job Location: Evansville, IN Contractor: CAC Custom Homes				Plant: 100 9/29/2026 7:43:27 AM		Tech: J. Horsley PC: T. Lewis					
Structure ID: SSMH 723											
P2		MH048RS60XS		MH RISER w/XYPEX/NO STEP T/G							
P5) 24" - CASTING HEIGHT - 7" P4) 48" - ECC XYPEX CONE w/ 24" HOLE F/G - 24" P3) 48" - MH RISER w/XYPEX/NO STEP T/G - 36" P2) 48" - MH RISER w/XYPEX/NO STEP T/G - 60" P1) 48" - MH BASE w/XYPEX T/n - 30" 1) 48" - MH INVERT CHANNEL EWSU w/XYPEX - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-315 F/C Sanitary 3) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO					0 lb 1738 lb 2515 lb 4192 lb 3330 lb 1440 lb 0 lb 0 lb 258 lb 0 lb 0 lb 16 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIX = XYPEX C500-NF-RED 4. CASTING BY ICAST (HOE MC-315 F/C "SANITARY") REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 386.4'					Rim to Invert: 13.12'		Slack: 2.44"		Sump: 2"		Step Position:
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

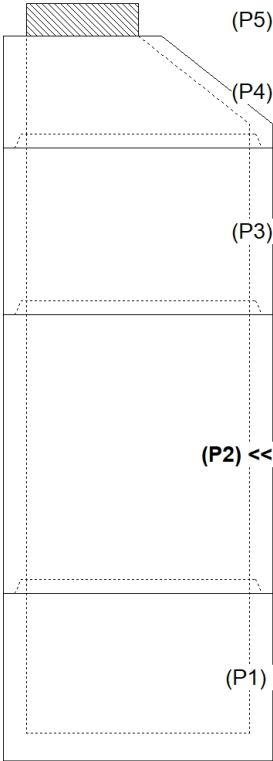

(P5)


(P4)

(P3)

(P2) <<


(P1)

RIGHT-SIDE UP VIEW (int. dimensions)



+ 0°-

INSIDE WALL DIMENSIONS

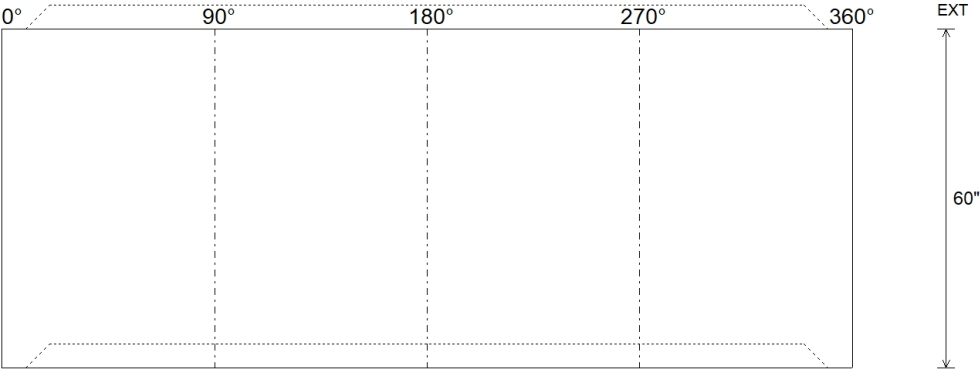

0° 90° 180° 270° 360°

EXT

60"

(P2)

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 60" Height (Ext): 60"	Weight (Net): 4192 lb Volume (Net): 1.07cu.yd
----------------------------------	------------------------------------	--	--	--
