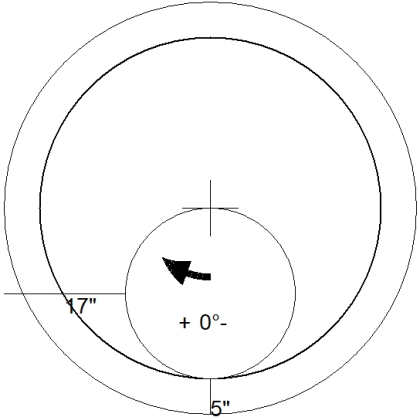



Job Name: 26-3805 - Goldfinch Sewer Ph.3 Job Location: Evansville, IN Contractor: CAC Custom Homes		Plant: 100 9/29/2026 7:43:48 AM	Tech: J. Horsley PC: T. Lewis	
Structure ID: SSMH 726				
P2 MH048CN42X-S		ECC CONE w/ 24" HOLE NO STEP w/ XYPEX F/G		
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE NO STEP w/ XYPEX F/G - 42" P1) 48" - MH BASE w/XYPEX T/n - 24" 1) 48" - MH INVERT CHANNEL EWSU w/XYPEX - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-315 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 1) PSX - 12-08 NYLO		0 lb 3000 lb 2959 lb 1440 lb 0 lb 0 lb 258 lb 0 lb 0 lb 8 lb ----- 7665 lb Structure Total:	<u>Structure Notes:</u> 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIX = XYPEX C500-NF-RED 4. CASTING BY ICAST (HOE MC-315 F/C "SANITARY") REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
				
 48" - ECC CONE w/ 24" HOLE NO STEP w/ XYPEX F/G - 42" - (P2)				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 42"	Weight (Net): 3000 lb Volume (Net): 0.5cu.yd
