

Job Name: 26-3805 - Goldfinch Sewer Ph.3
Job Location: Evansville, IN
Contractor: CAC Custom Homes

Plant: 100

Tech: J. Horsley

9/29/2026 7:43:49 AM

PC: T. Lewis



Structure ID: SSMH 729

P2 MH048CN36X-S

ECC CONE w/ 24" HOLE NO STEP w/ XYPEX F/G

- P3) 24" - CASTING HEIGHT - 7"
P2) 48" - ECC CONE w/ 24" HOLE NO STEP w/ XYPEX F/G - 36"
P1) 48" - MH BASE w/XYPEX T/n - 30"
1) 48" - MH INVERT CHANNEL EWSU w/XYPEX - FULL HEIGHT
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) CASTING - HOE MC-315 F/C Sanitary
1) 48" - Conseal CS-102 1.00" (Double)
1) 24" - Conseal CS-102 1.00" (Double)
1) PSX - 12-08 NYLO

0 lb
3000 lb
3378 lb
1440 lb
0 lb
0 lb
258 lb
0 lb
0 lb
8 lb


Structure Total: 8084 lb

Structure Notes:


1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. ADMIX = XYPEX C500-NF-RED
4. CASTING BY ICAST (HOE MC-315 F/C "SANITARY")

REINFORCING PER ASTM A615 (GRADE 60).

- CONE (As .12)
- RISER (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

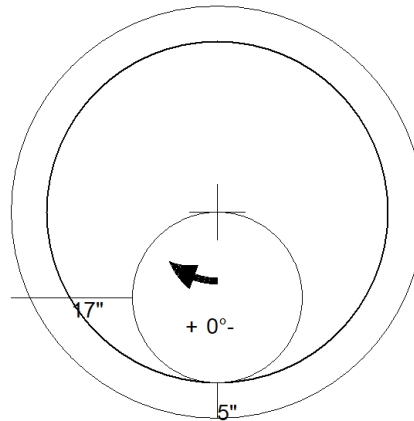

48" - ECC CONE w/ 24" HOLE NO STEP w/ XYPEX F/G - 36" - (P2)



Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 36"

Weight (Net): 3000 lb
Volume (Net): 0.5cu.yd
