

Contractor: Lawrence Construction & Leasing, Inc.

TECH: J.Horsley

Plant: 100



Size: 48"

Rim to Invert: 4.93'

Floor Height: 6"

Slack: 0.16"

1. PER KYTC MH A / ASTM C478 SPEC'S.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. REINFORCING PER ASTM A615 (GRADE 60.)

STRUCTURE SUMMARY:

0 lb

202 lb

1561 lb

3575 lb

510 lb


0 lb

0 lb


0 lb

0.40 lb


Structure Total: 5848 lb

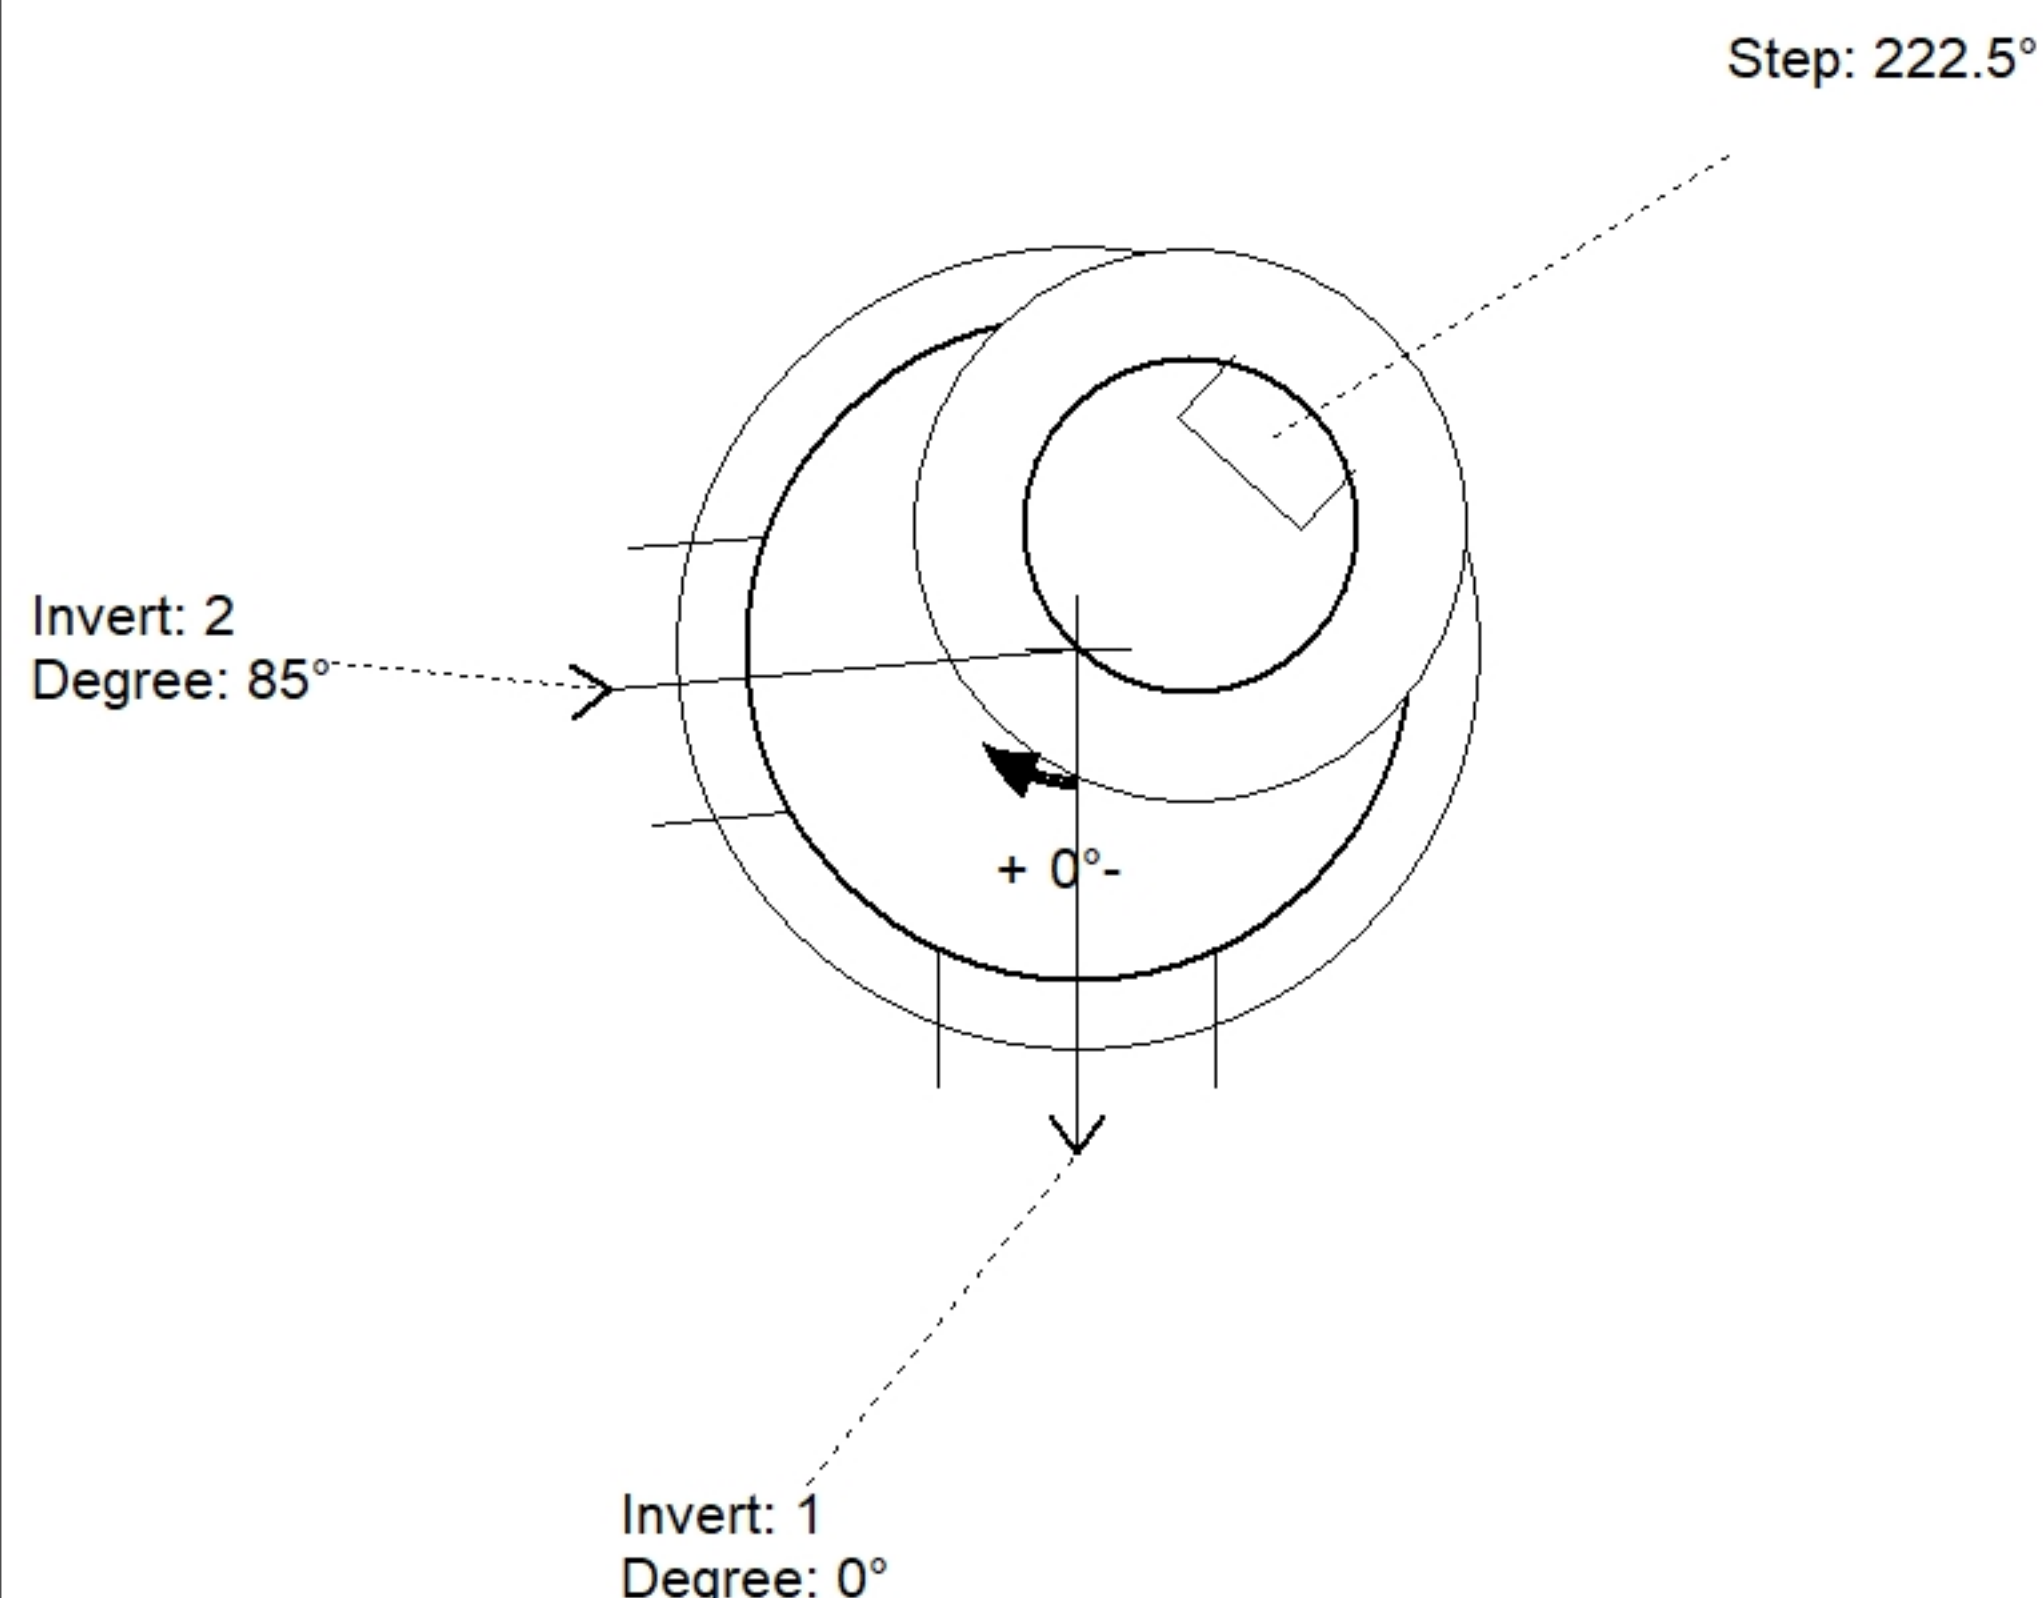

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	888.44'							
Reducer								
Invert 1	883.51'	0°	15" HDPE	17.6"	20"	Hole 20	-2.5"	P1
Invert 2	883.51'	85°	15" HDPE	17.6"	20"	Hole 20	-2.5"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

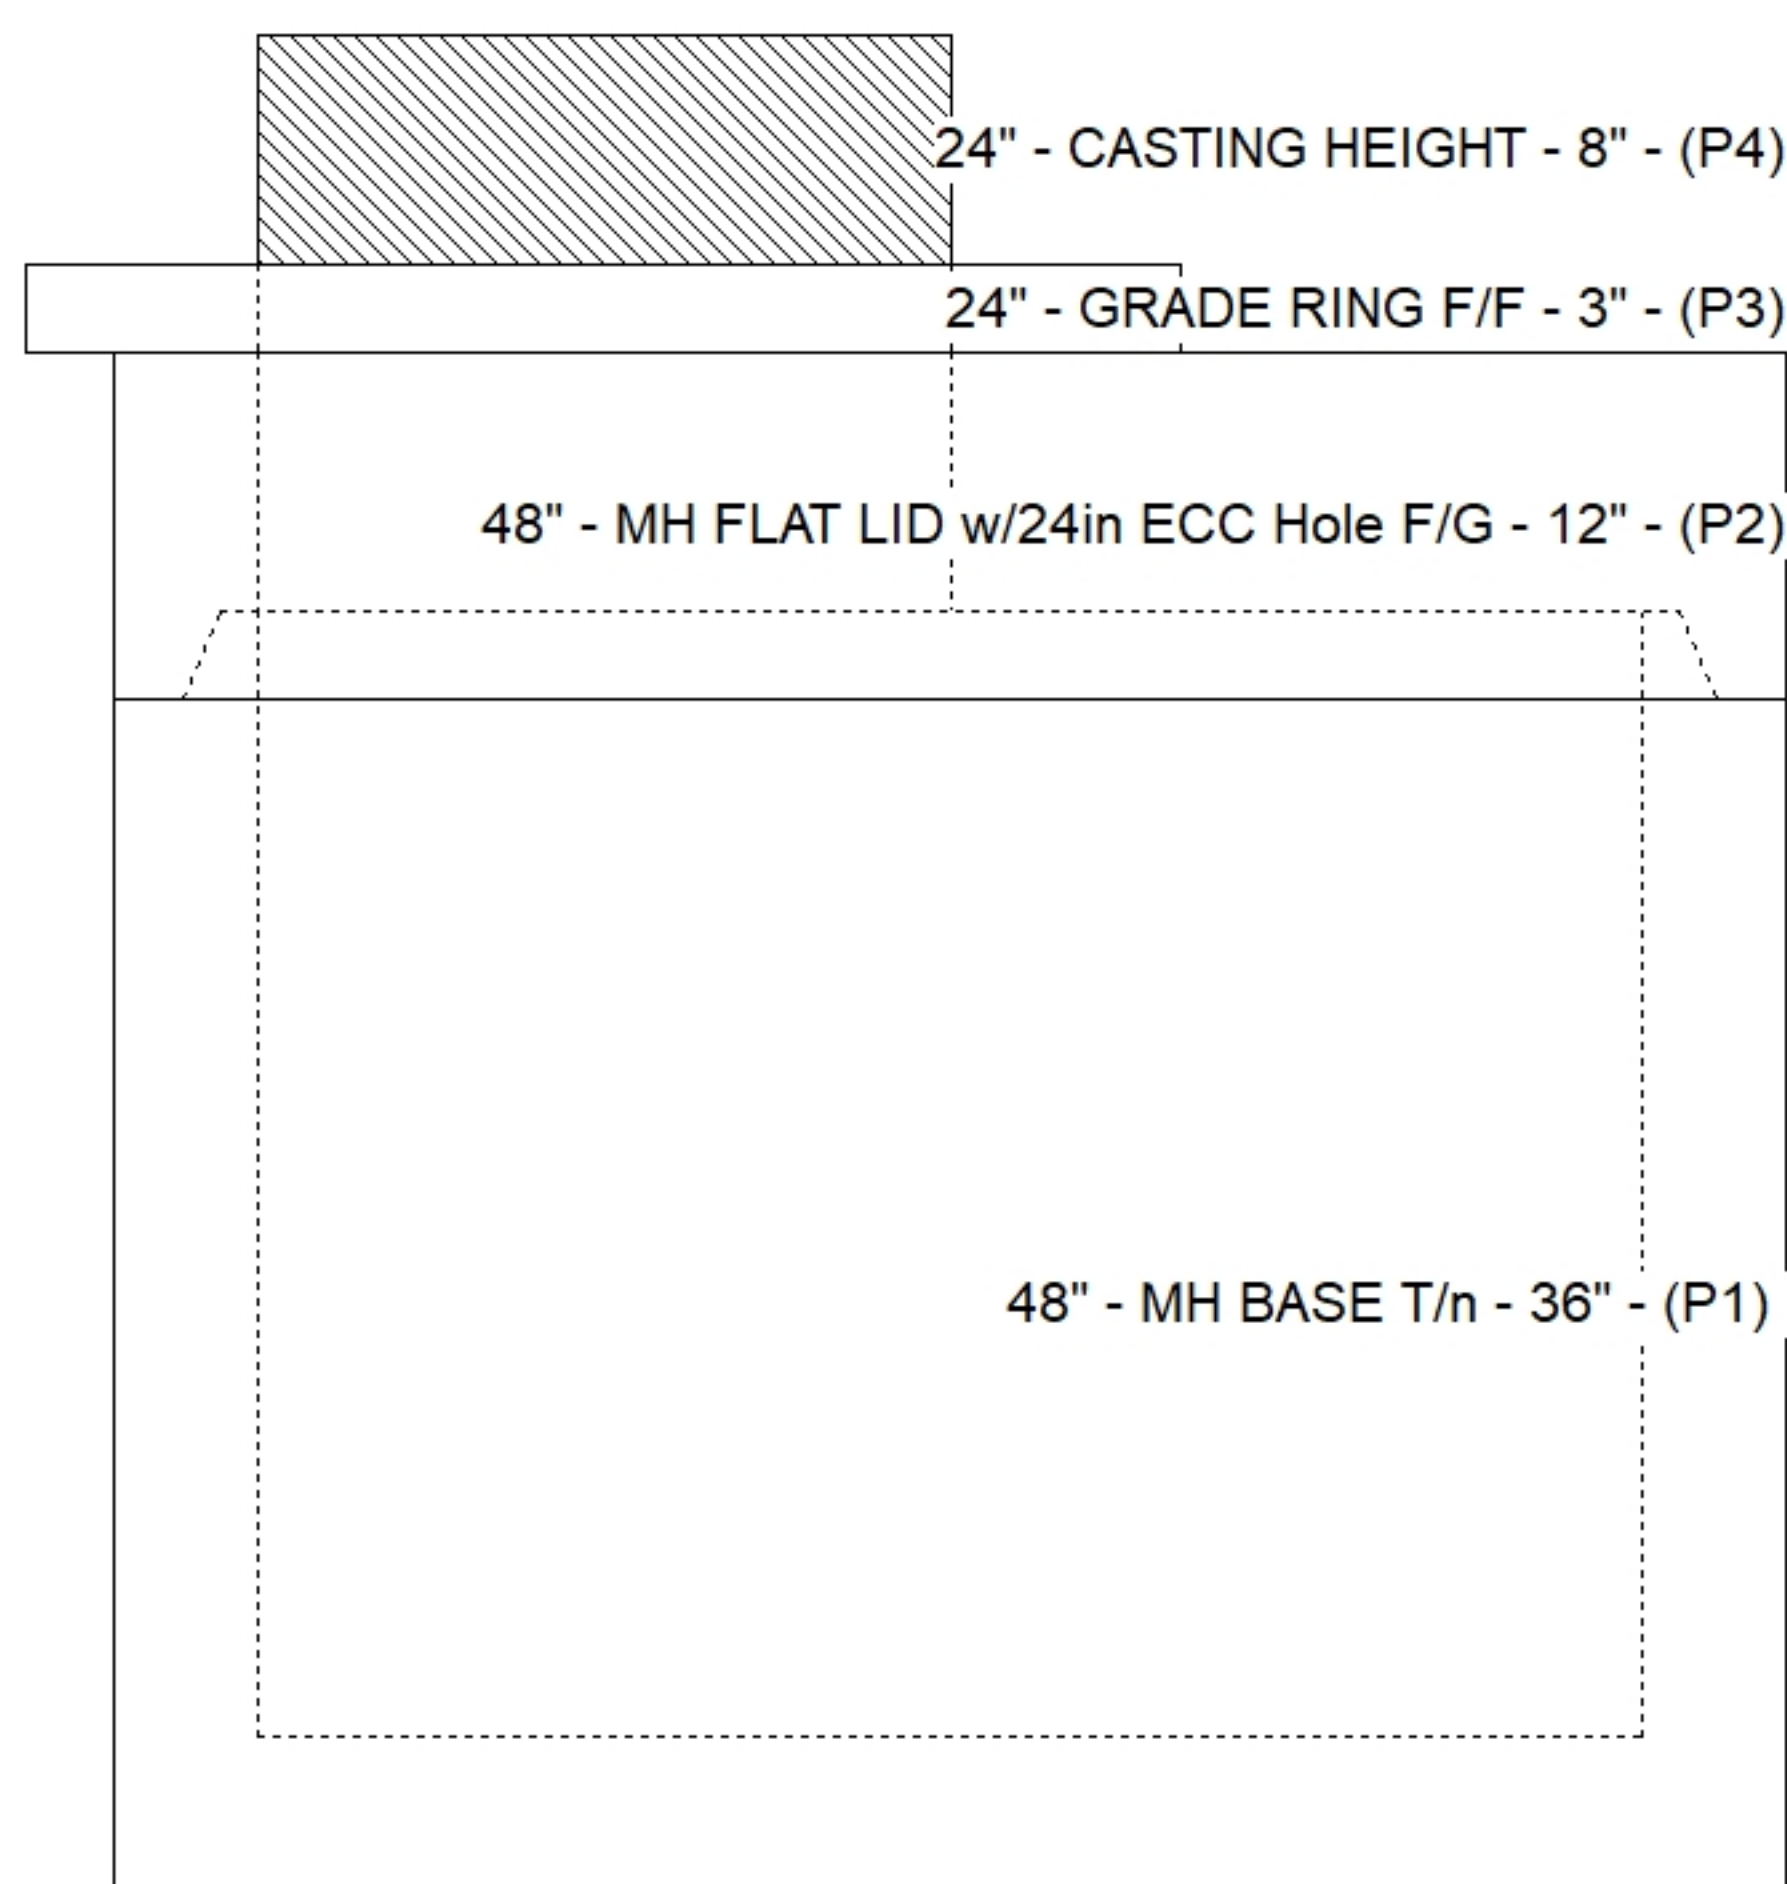

Cast (Int. Dim.) - Interior Dimensions

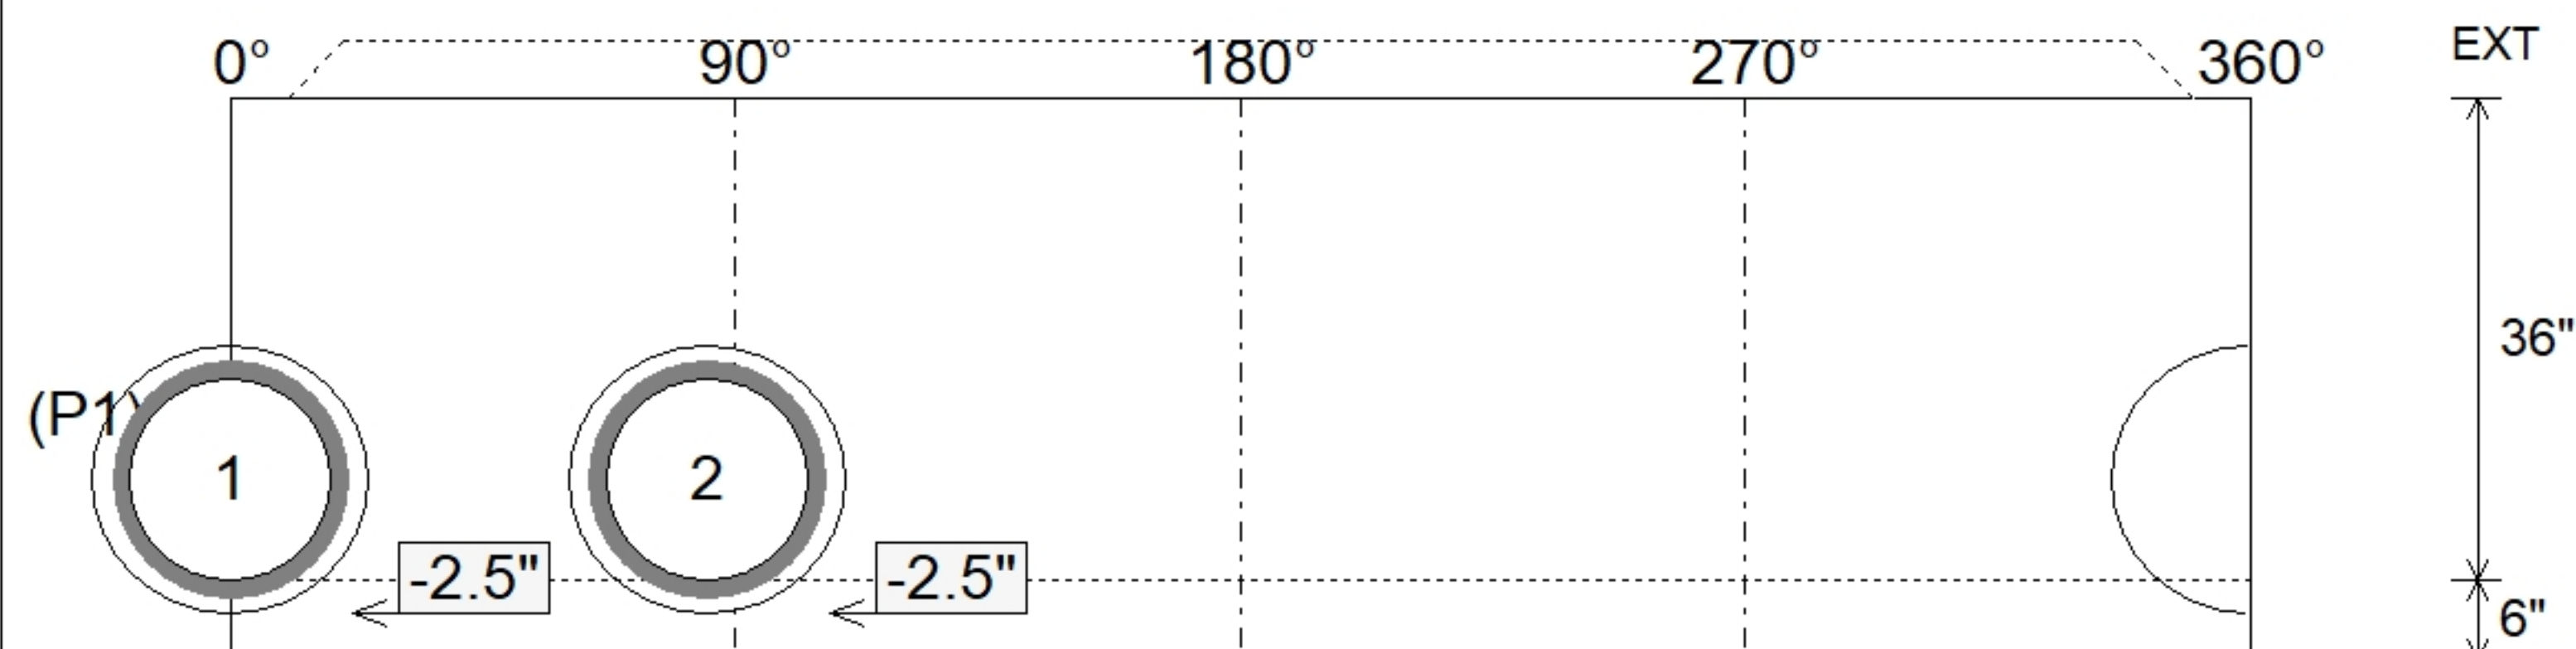

Submittal Drawing
5/13/2026 2:21:22 PM

SUBMITTAL
APPROVED BY:
