

Contractor: Seven Earthmovers LLC

TECH: J. Horsley

Plant: 100



Size: 24" x 36"

Rim to Invert: 4.5'

Floor Height: 8"

Slack: 0"


REINFORCING PER ASTM AS615 (GRADE 60).

- TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W.
- BASE WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- BASE FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


P3) 24" x 120" - CB INLET KY A 10' TOP SAG F/G - 10"
P2) 24" x 120" - CB INLET KY A 10' BOTTOM SAG T/G - 18"
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht T/n - 26"
1) CASTING - HOE KY-206 F/C (KY CBI A)
1) 24" x 36" - Conseal CS-102 1.00"
2) Hole - 24
1) Hole - 22

3398 lb
5270 lb
3263 lb
206 lb
0 lb
0 lb
0 lb


Structure Total: 12136 lb

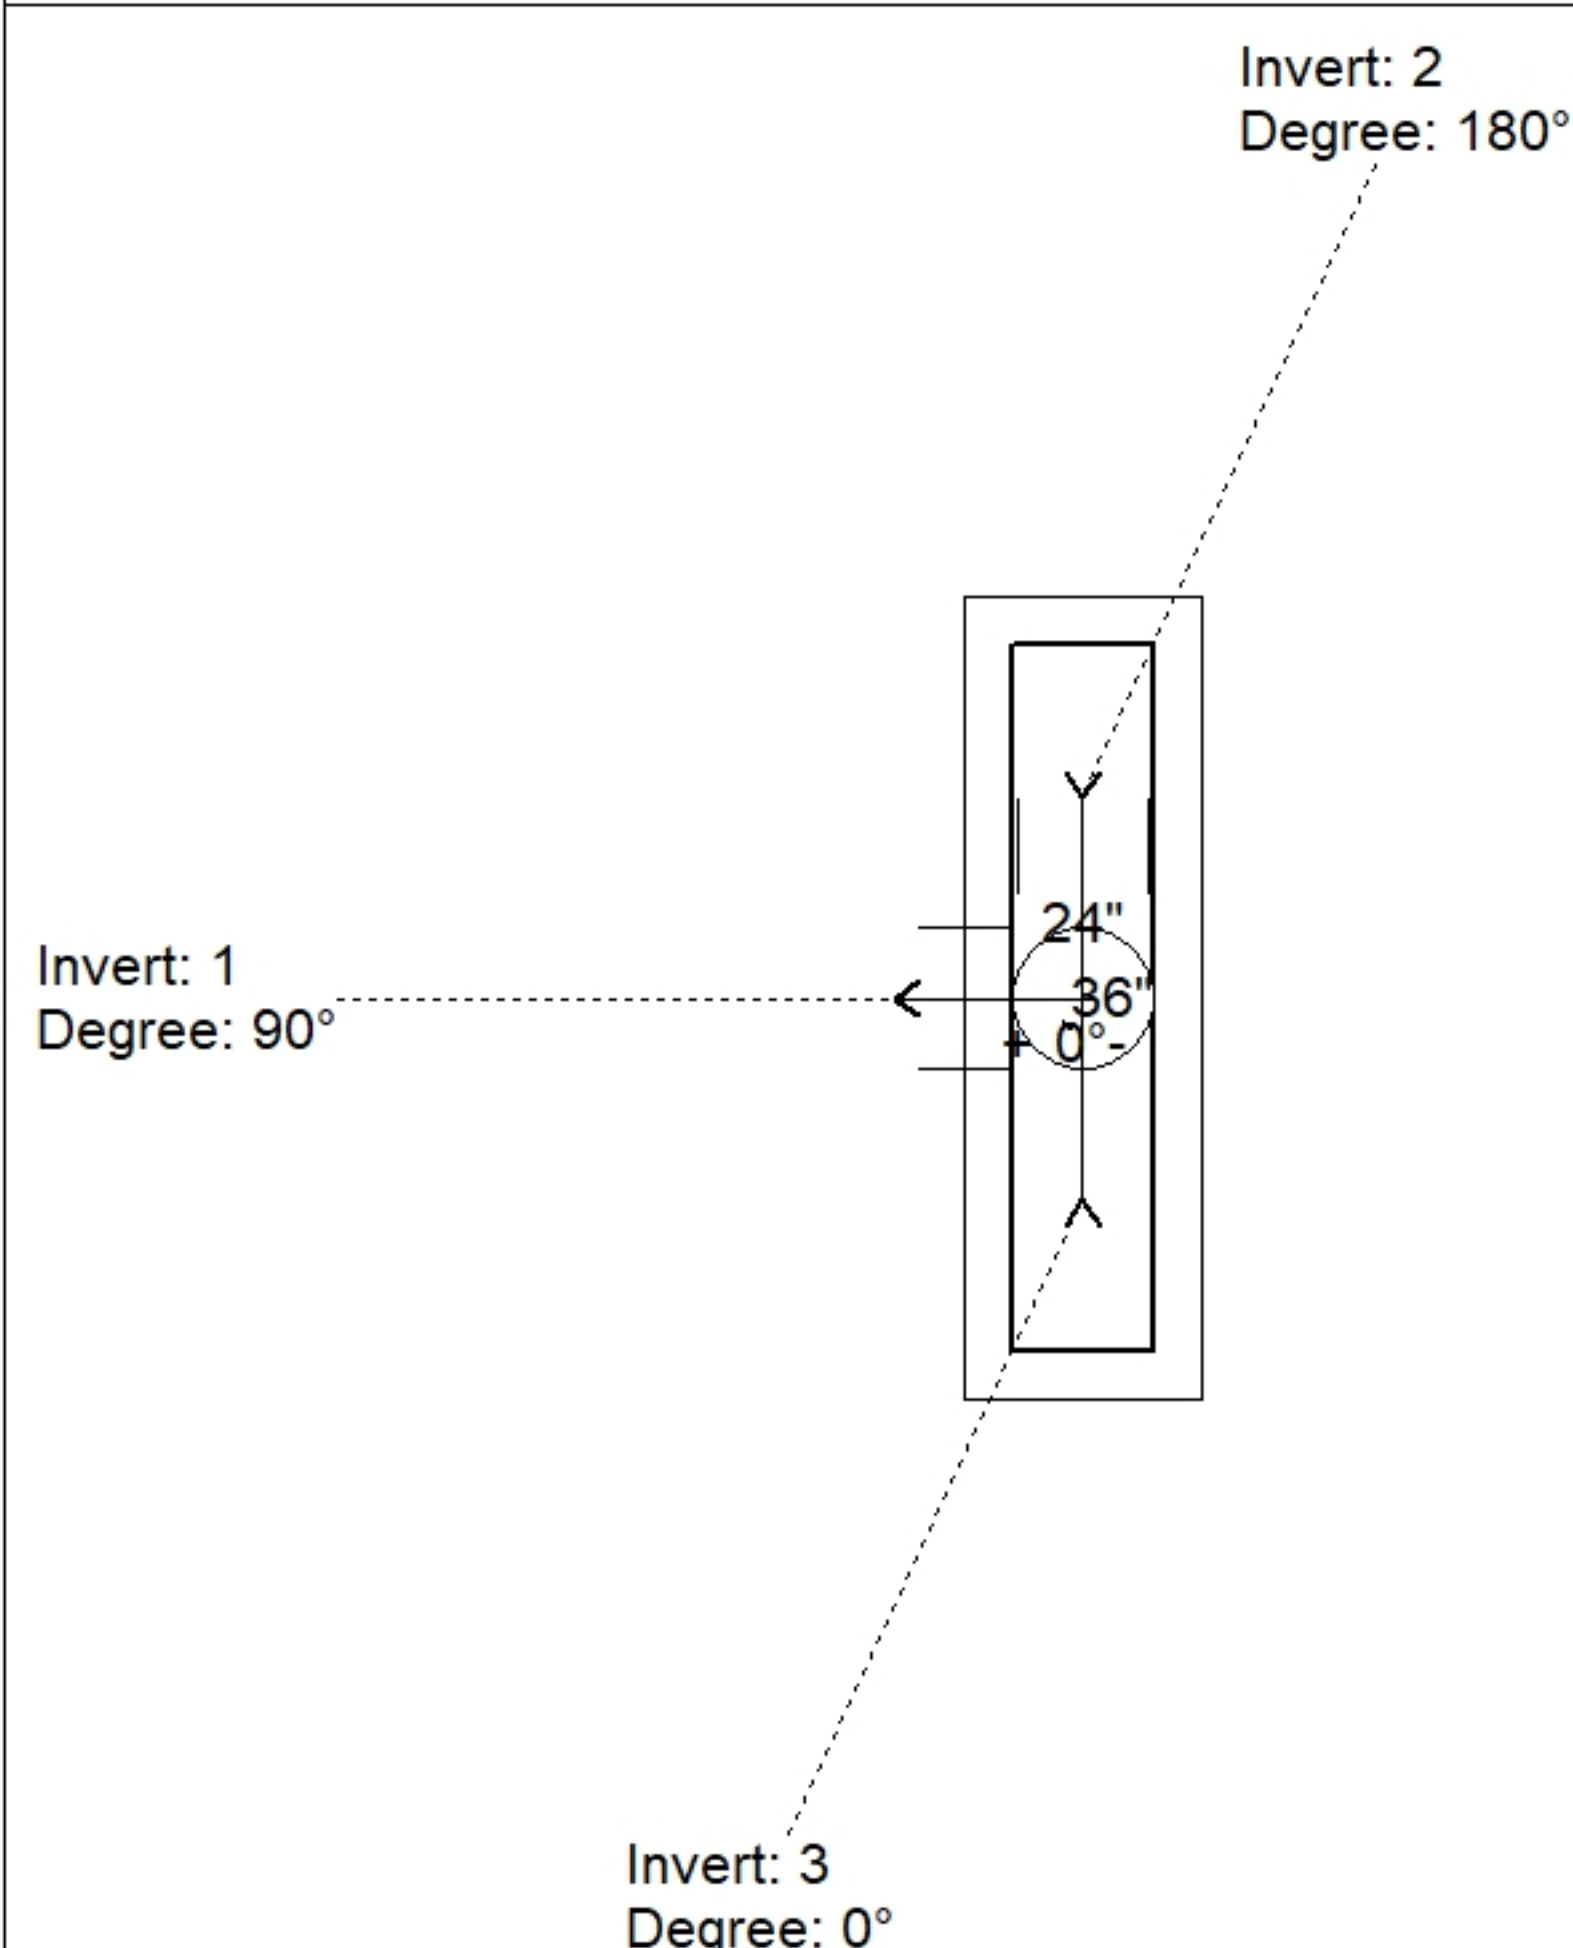

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (")	Ref
Rim	906.98'							
Reducer								
Invert 1	902.48'	90°	18" ADS N-12	22"	24"	Hole 24	-3"	P1
Invert 2	902.73'	180°	15" ADS N-12	18"	22"	Hole 22	-0.5"	P1
Invert 3	902.73'	0°	15" ADS N-12	18"	24"	Hole 24	-1.5"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

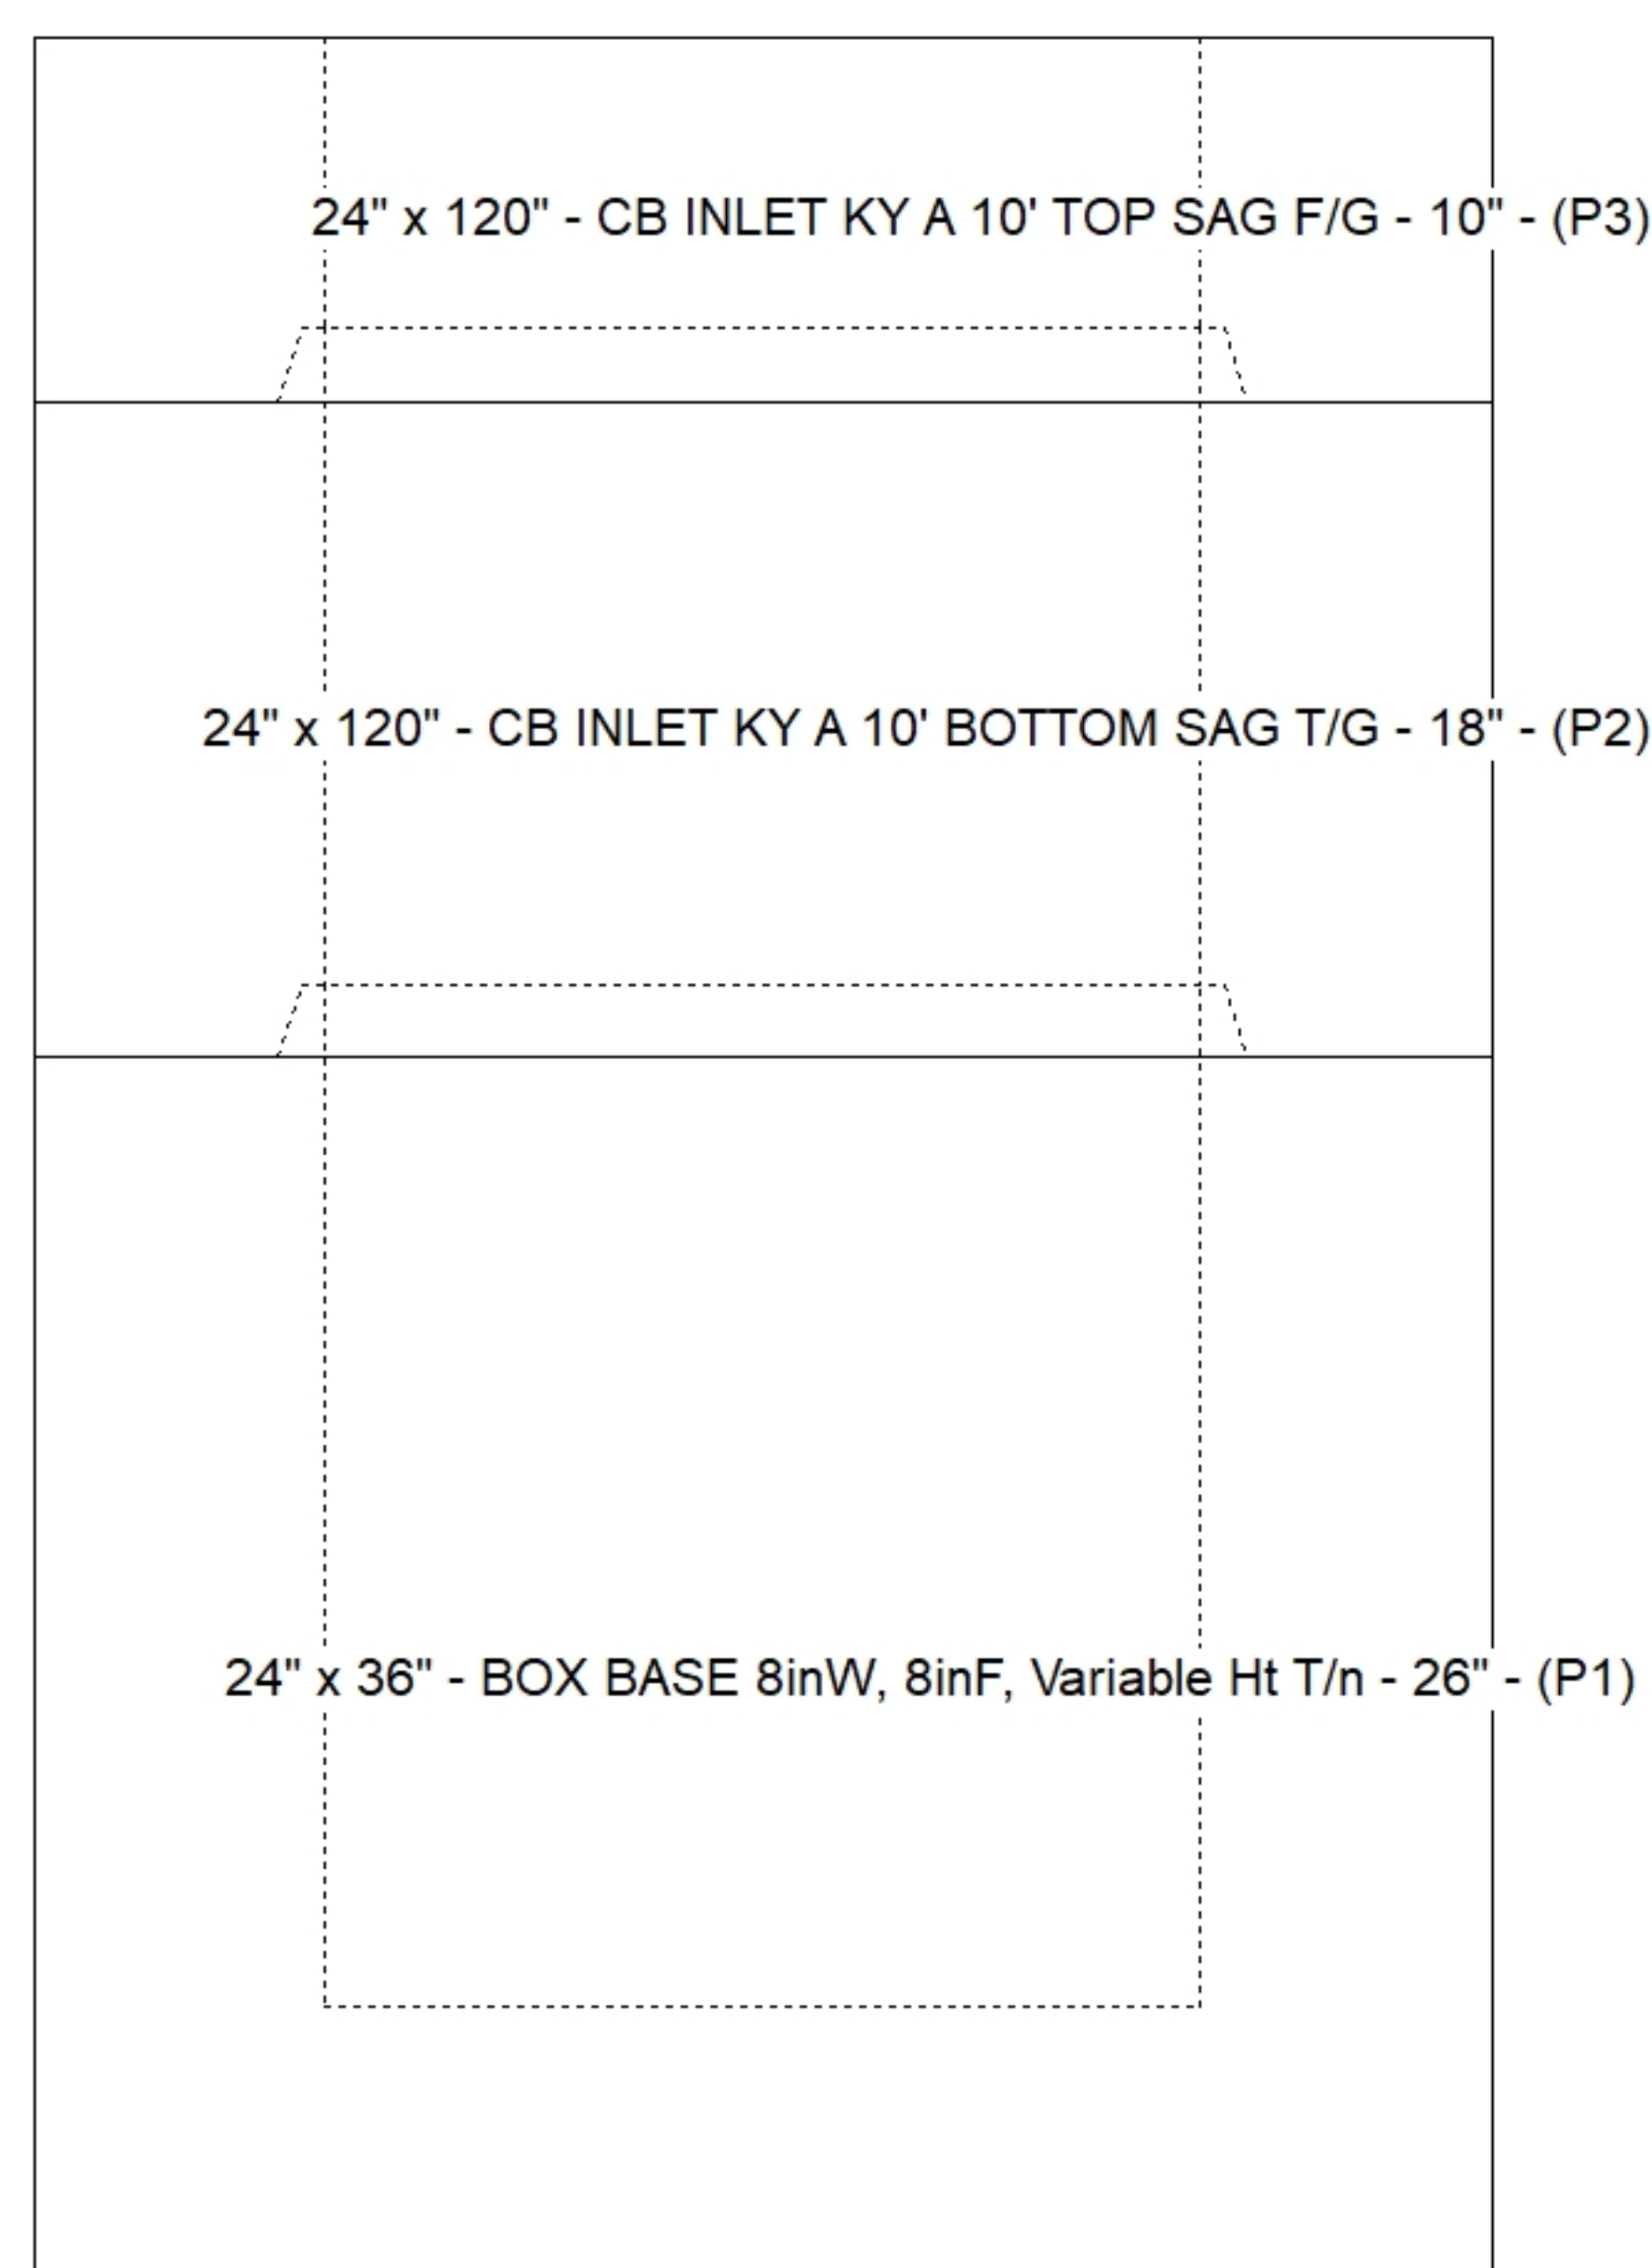

Cast (Int. Dim.) - Interior Dimensions

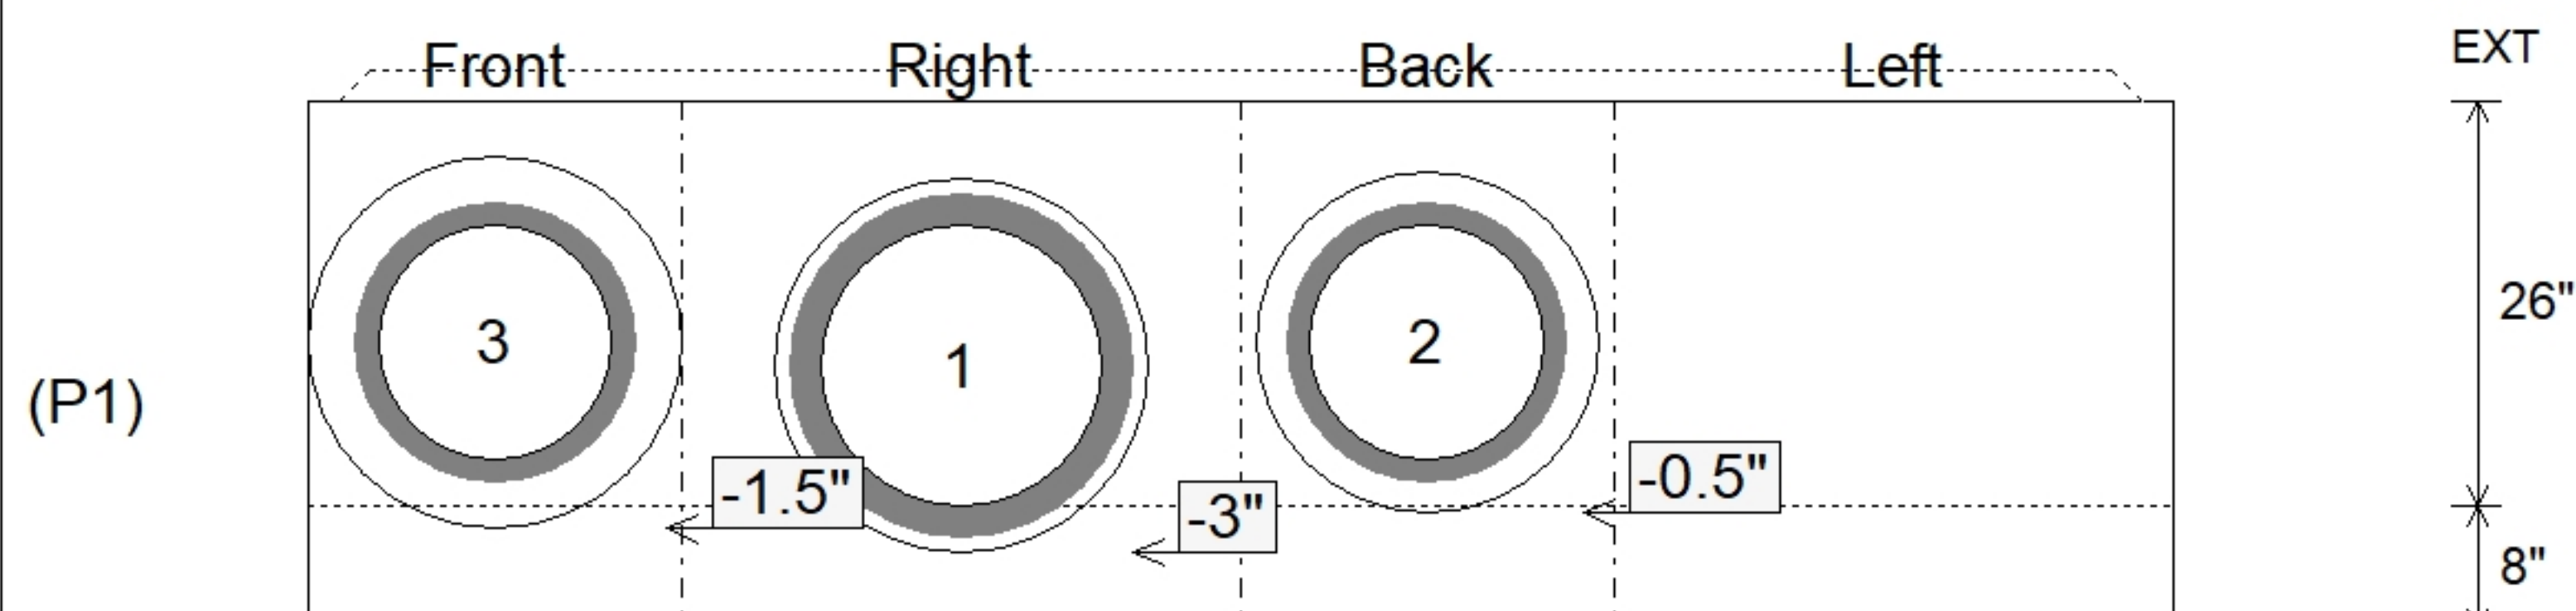

Submittal Drawing
5/19/2026 12:54:52 PM

SUBMITTAL
APPROVED BY:
