

Contractor: Seven Earthmovers LLC

TECH: J. Horsley

Plant: 100



Size: 24" x 36"

Rim to Invert: 4.25'

Floor Height: 8"

Slack: 0"


REINFORCING PER ASTM AS615 (GRADE 60).

- TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W.
- BASE WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- BASE FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

P3) 24" x 120" - CB INLET KY A 10' TOP LEFT F/G - 10"
P2) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT T/G - 18"
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht T/n - 23"
1) CASTING - HOE KY-206 F/C (KY CBI A)
1) 24" x 36" - Conseal CS-102 1.00"
2) Hole - 22

3400 lb
5270 lb
3233 lb
206 lb
0 lb
0 lb

Structure Total: 12108 lb

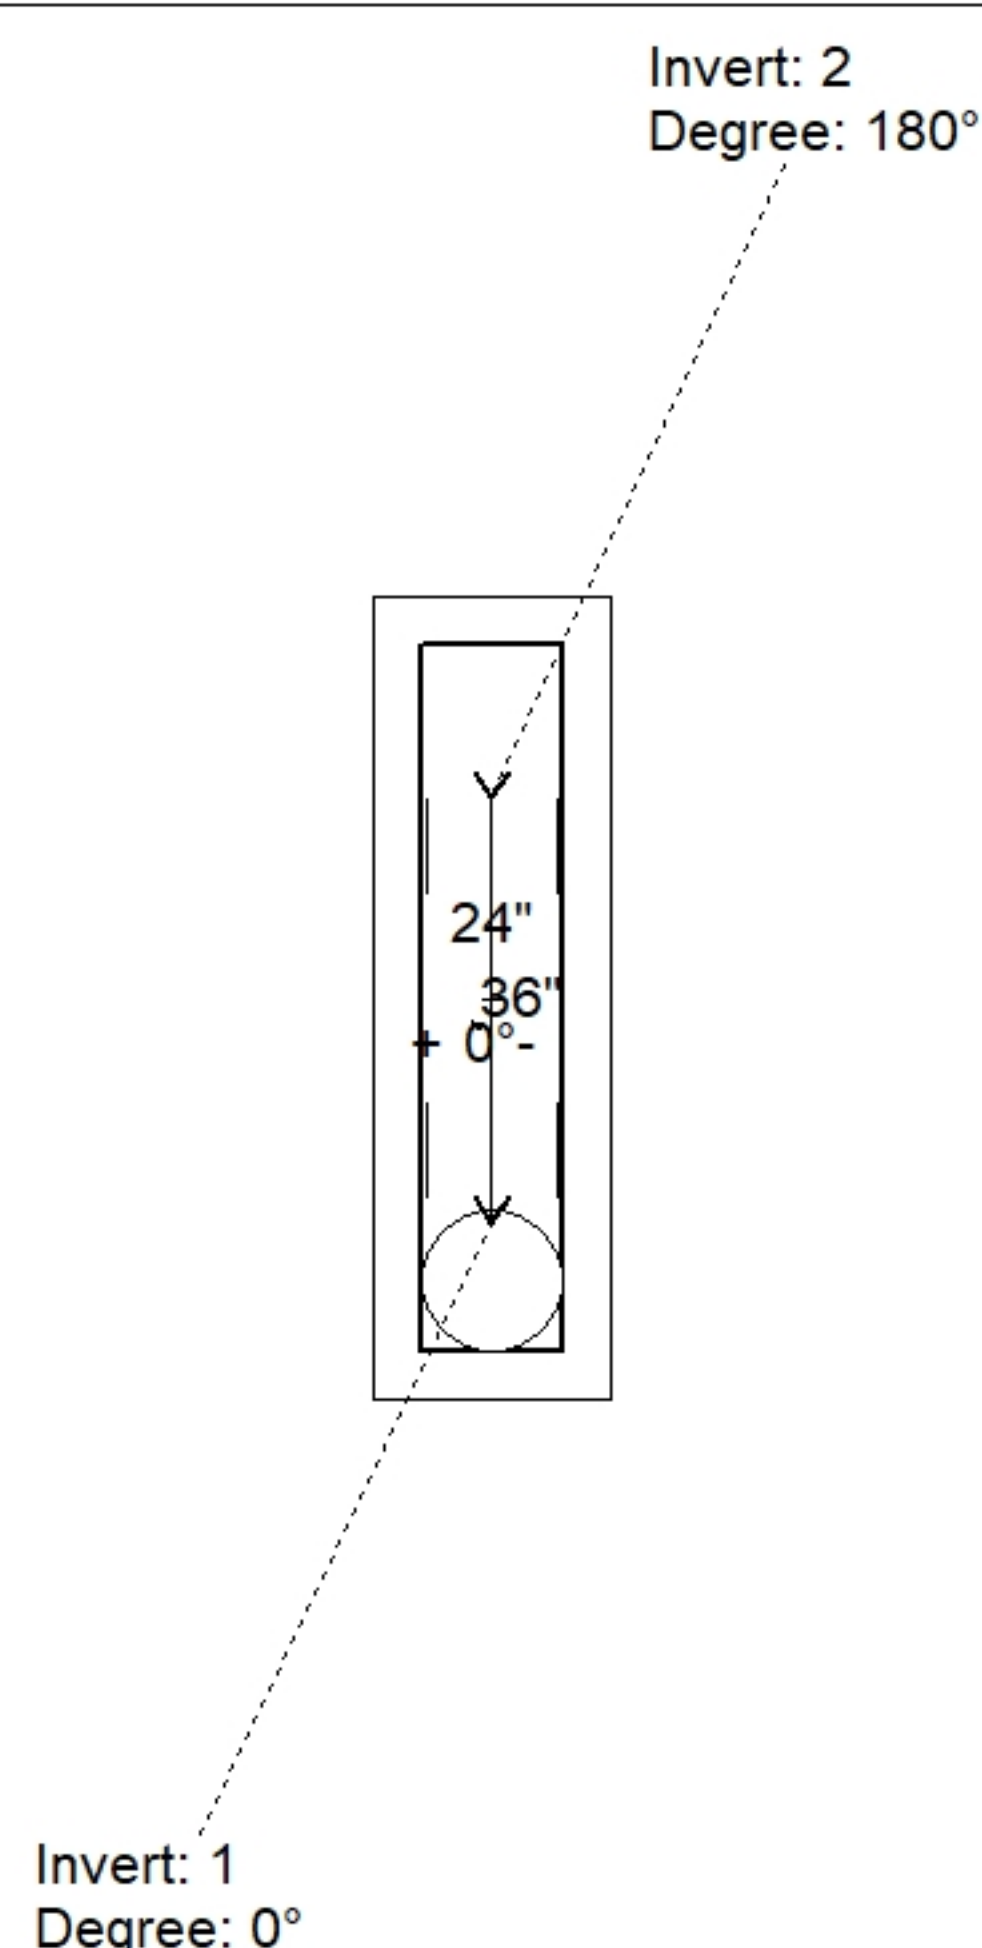


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')_	Ref
Rim	908.17'							
Reducer								
Invert 1	903.92'	0°	15" ADS N-12	18"	22"	Hole 22	-3.5"	P1
Invert 2	903.92'	180°	15" ADS N-12	18"	22"	Hole 22	-3.5"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" x 120" - CB INLET KY A 10' TOP LEFT F/G - 10" - (P3)

24" x 120" - CB INLET KY A 10' BOTTOM LEFT T/G - 18" - (P2)

24" x 36" - BOX BASE 8inW, 8inF, Variable Ht T/n - 23" - (P1)

Cast (Int. Dim.) - Interior Dimensions

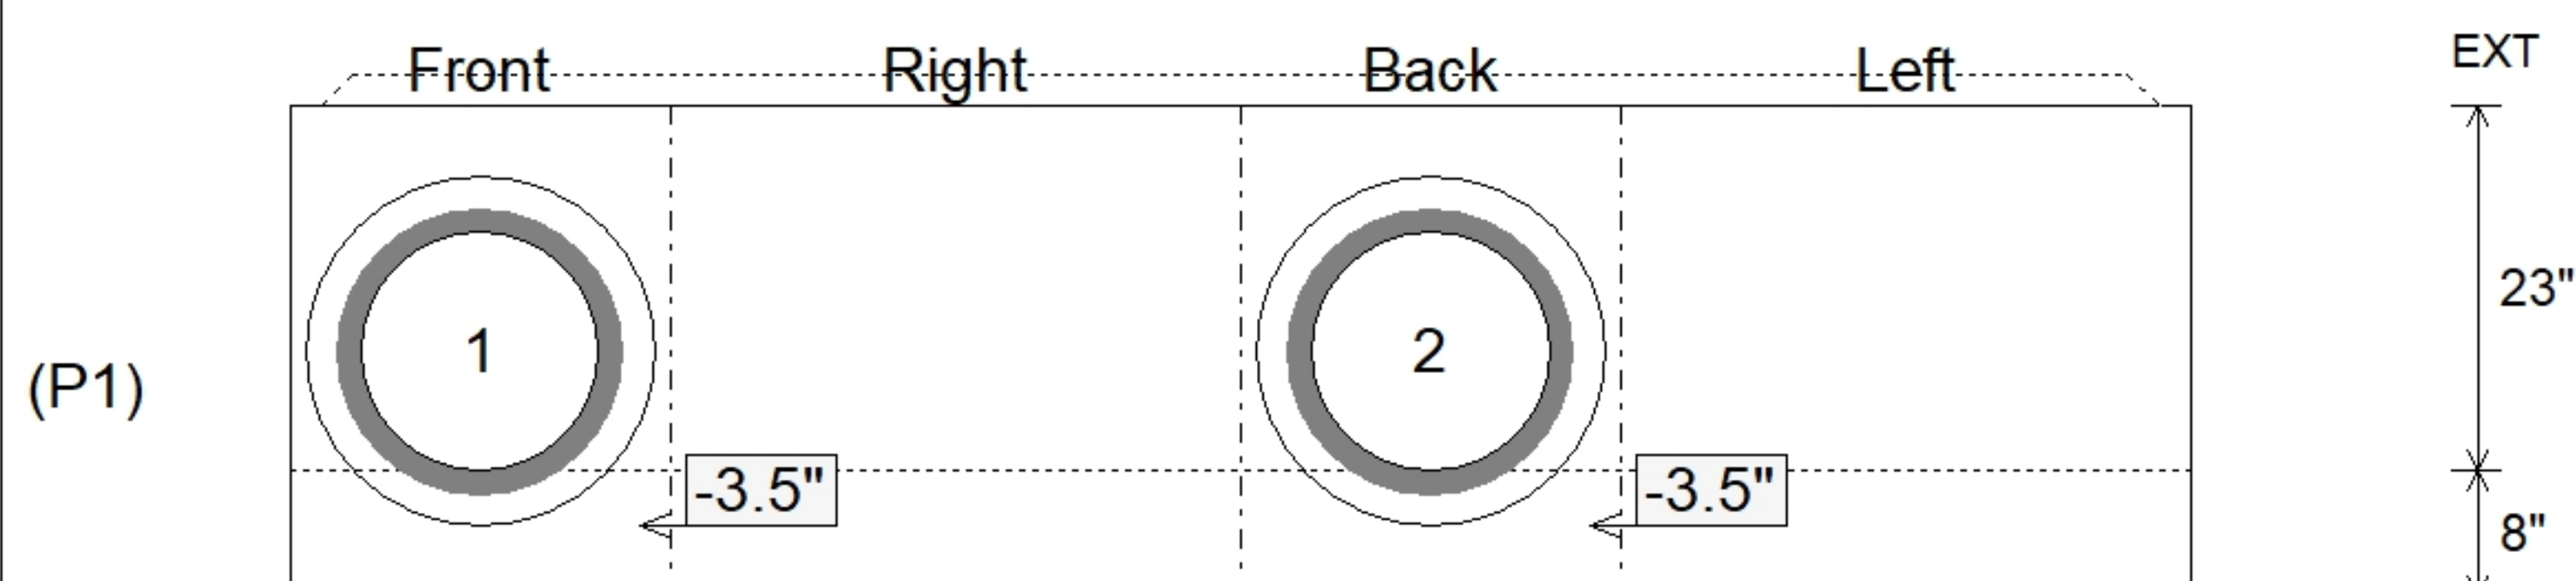

Submittal Drawing
5/19/2026 12:54:52 PM

SUBMITTAL
APPROVED BY:
