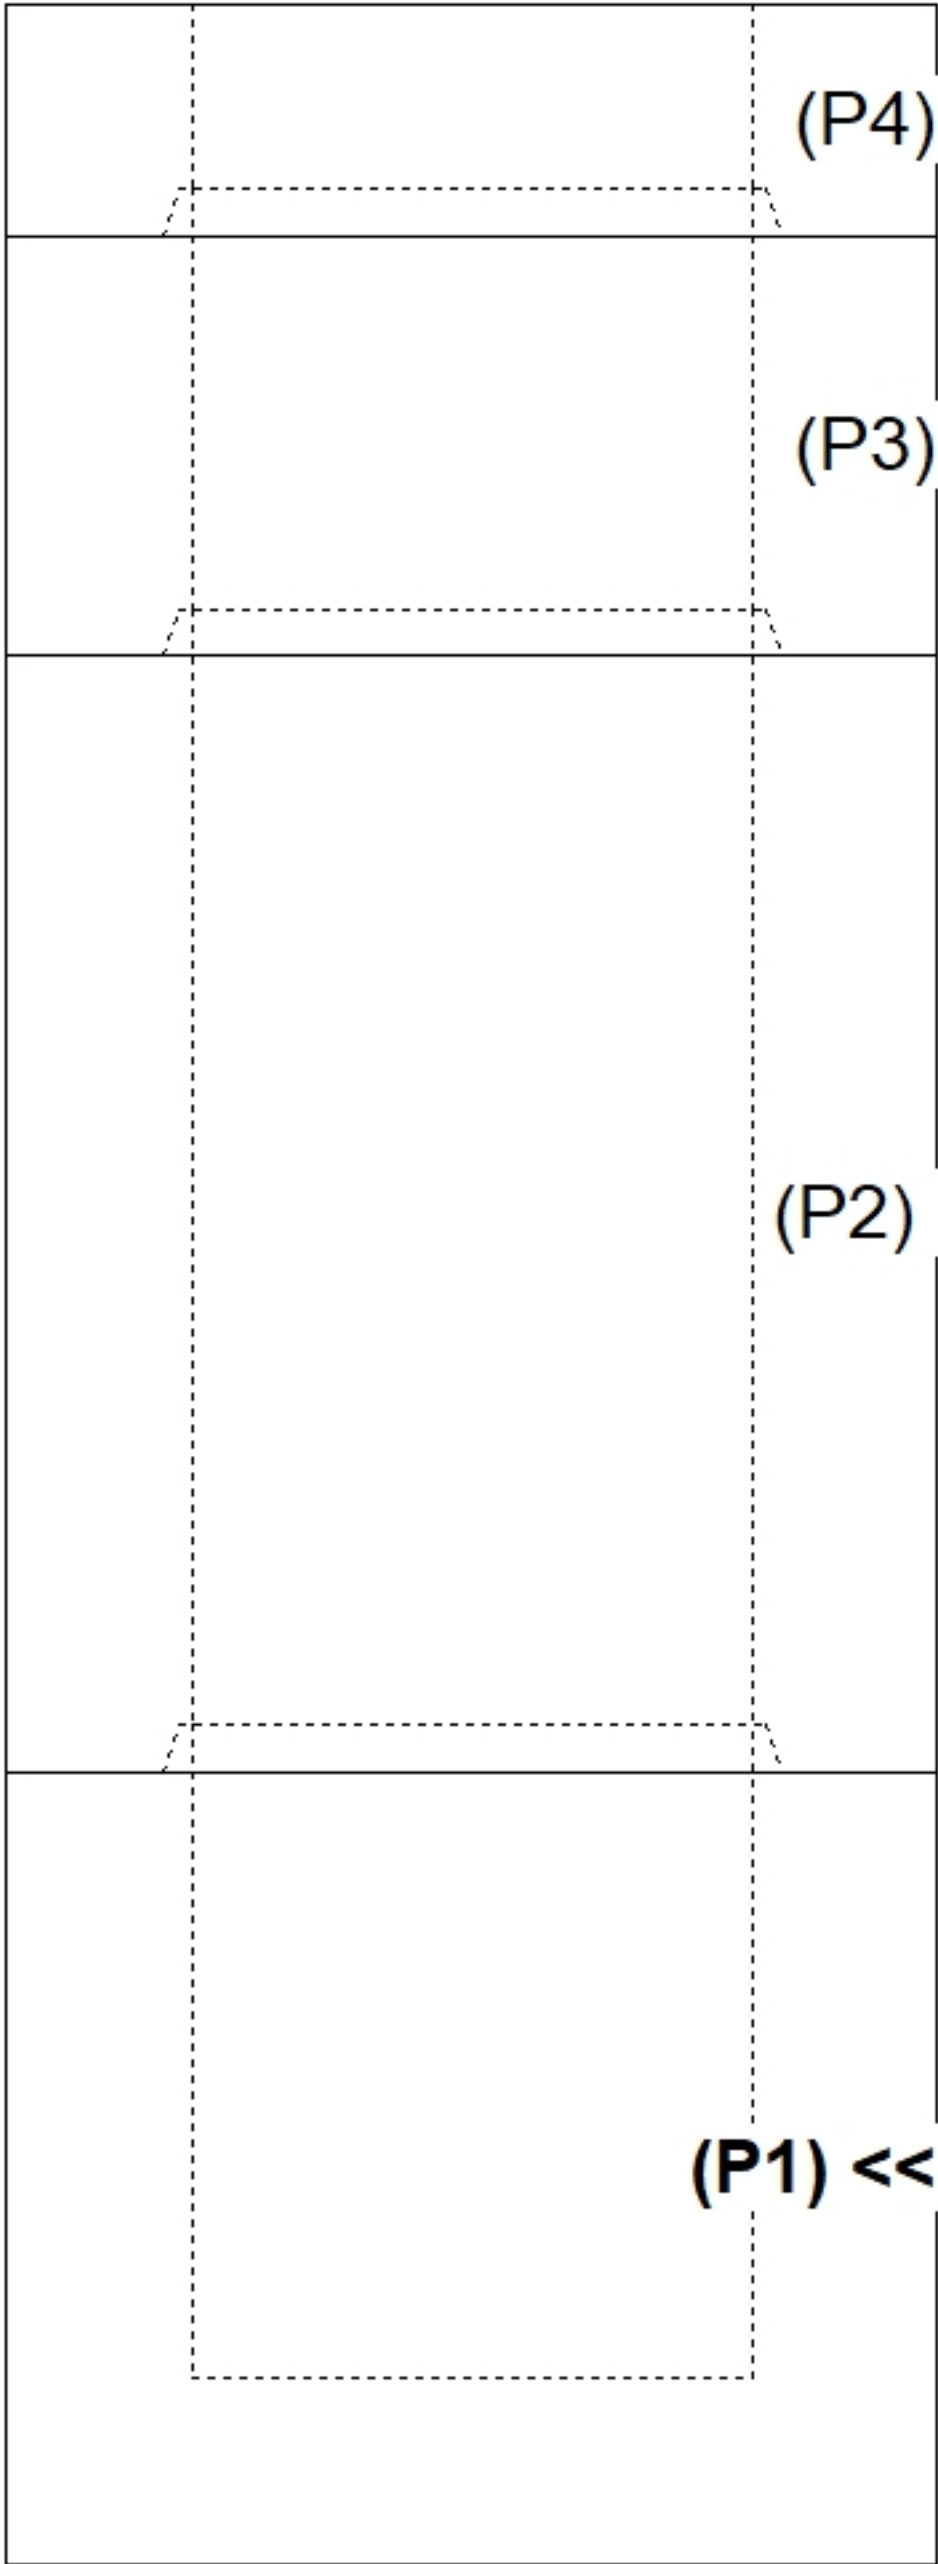
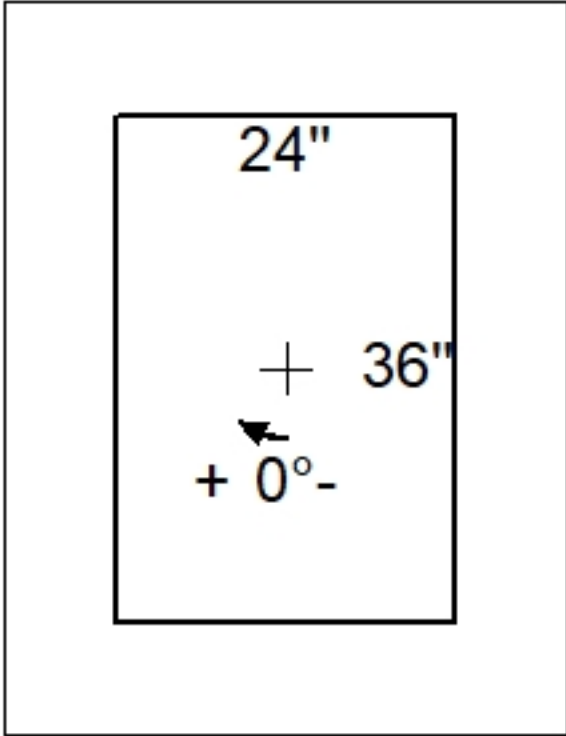
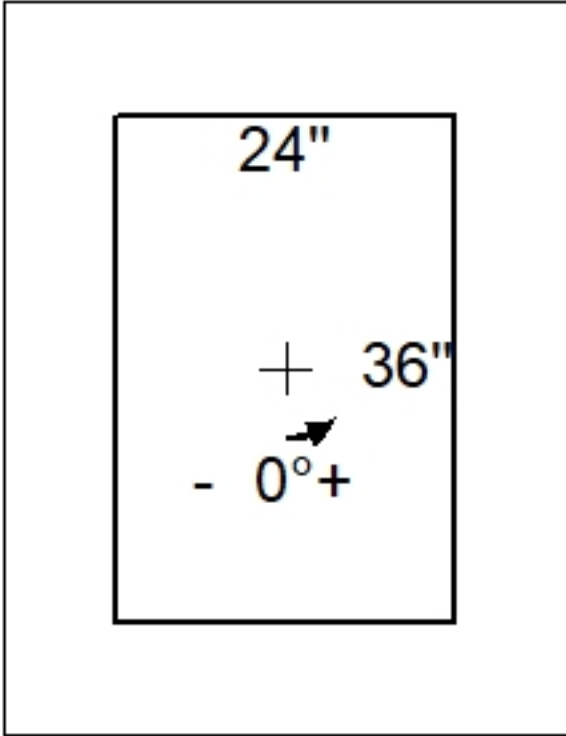


Job Name: 23-2404 Hampton Hills (Phase 1) Job Location: Richmond, KY Contractor: Seven Earthmovers LLC				Plant: 100 5/19/2026 12:59:24 PM		Tech: J. Horsley PC: C. Golf					
Structure ID: CBI-H2 P1 BX2436-08BVF BOX BASE 8inW, 8inF, Variable Ht T/n											
P4) 24" x 120" - CB INLET KY A 10' TOP LEFT F/G - 10" P3) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT T/G - 18" P2) 24" x 36" - BOX RISER 8inW T/G - 48" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht T/n - 26" 1) CASTING - HOE KY-206 F/C (KY CBI A) 1) SNOUT - BMP SNOUT 18F w/ KIT 2) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 22						3400 lb 5270 lb 4387 lb 4049 lb 206 lb 25 lb 0 lb 0 lb ----- Structure Total: 17337 lb		Structure Notes: 1. PER KYTC CBI A / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING (HOE KY-206) TO BE CAST INTO TOP PHASE. 4. BMP SNOUT 18F w/KIT. REINFORCING PER ASTM AS615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - BASE WALLS (As .31) #5 BARS AT 12" C.C.E.W. - BASE FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 910.68' Rim to Invert: 5' Slack: 0" Sump: 42" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (┘)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimenions)											
  											
INSIDE WALL DIMENSIONS 											
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 26" Height (Ext): 34"		Weight (Net): 4049 lb Volume (Net): 1.03cu.yd		
